



United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme

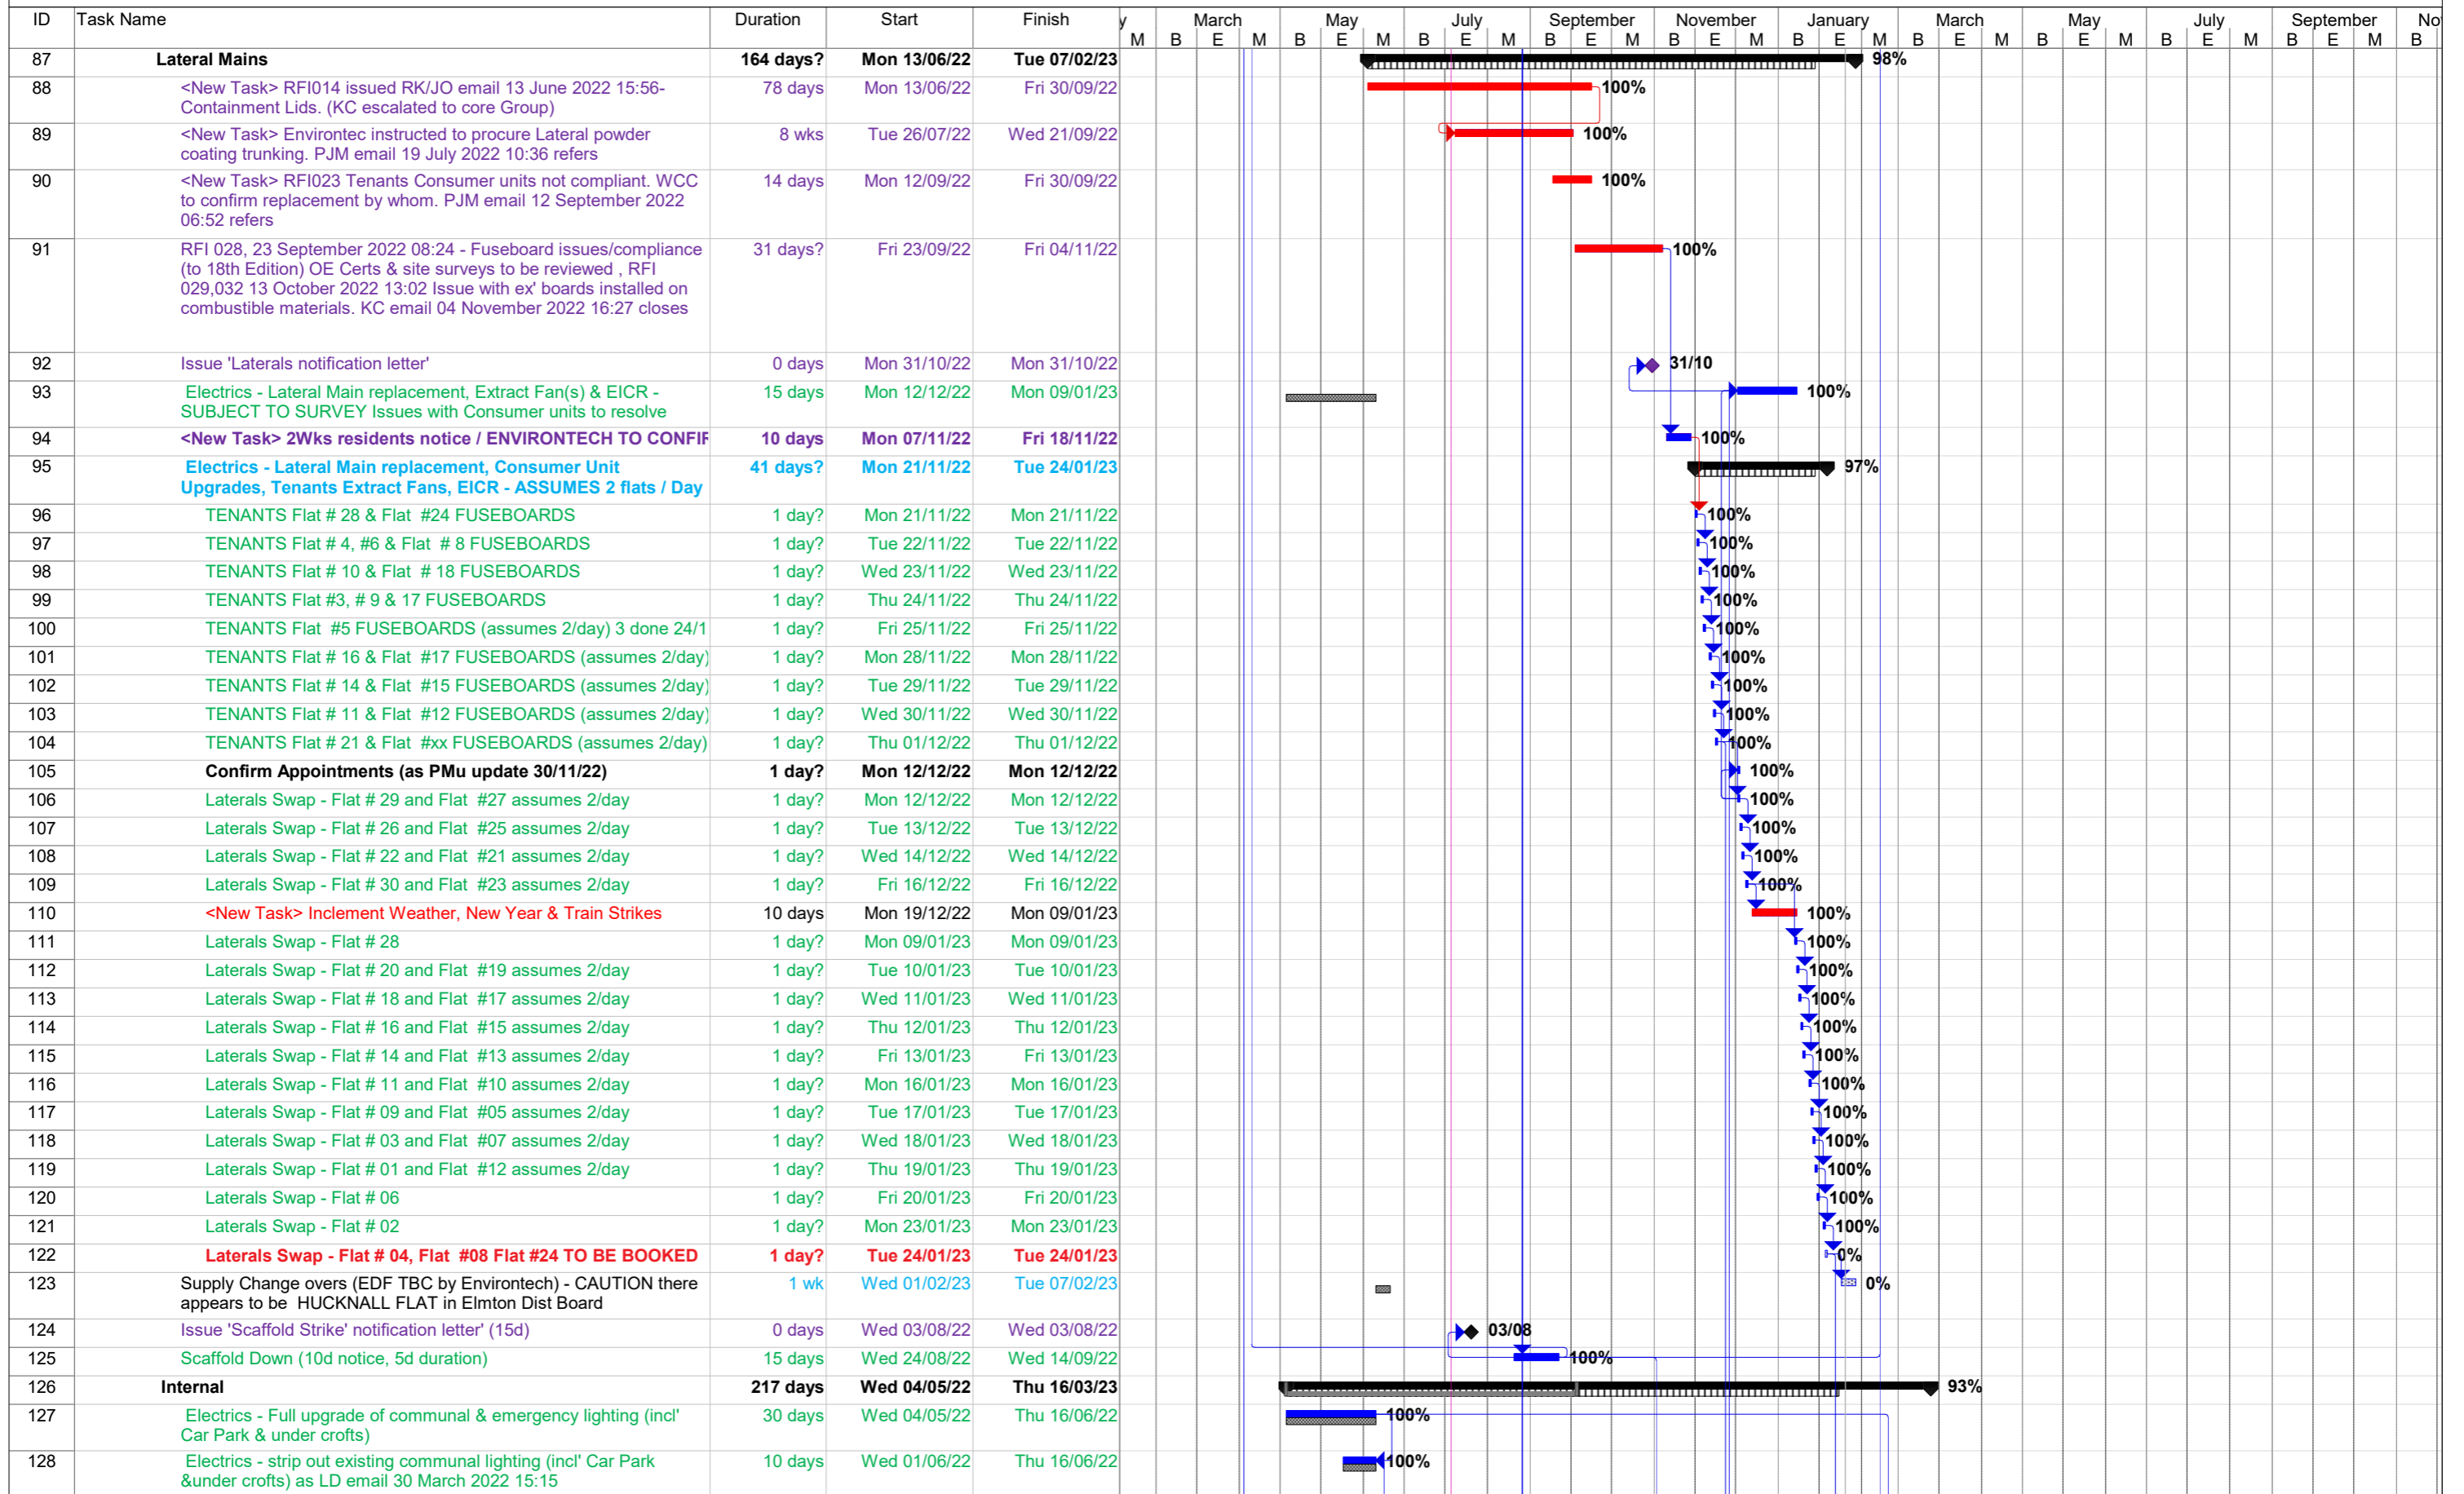


United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme

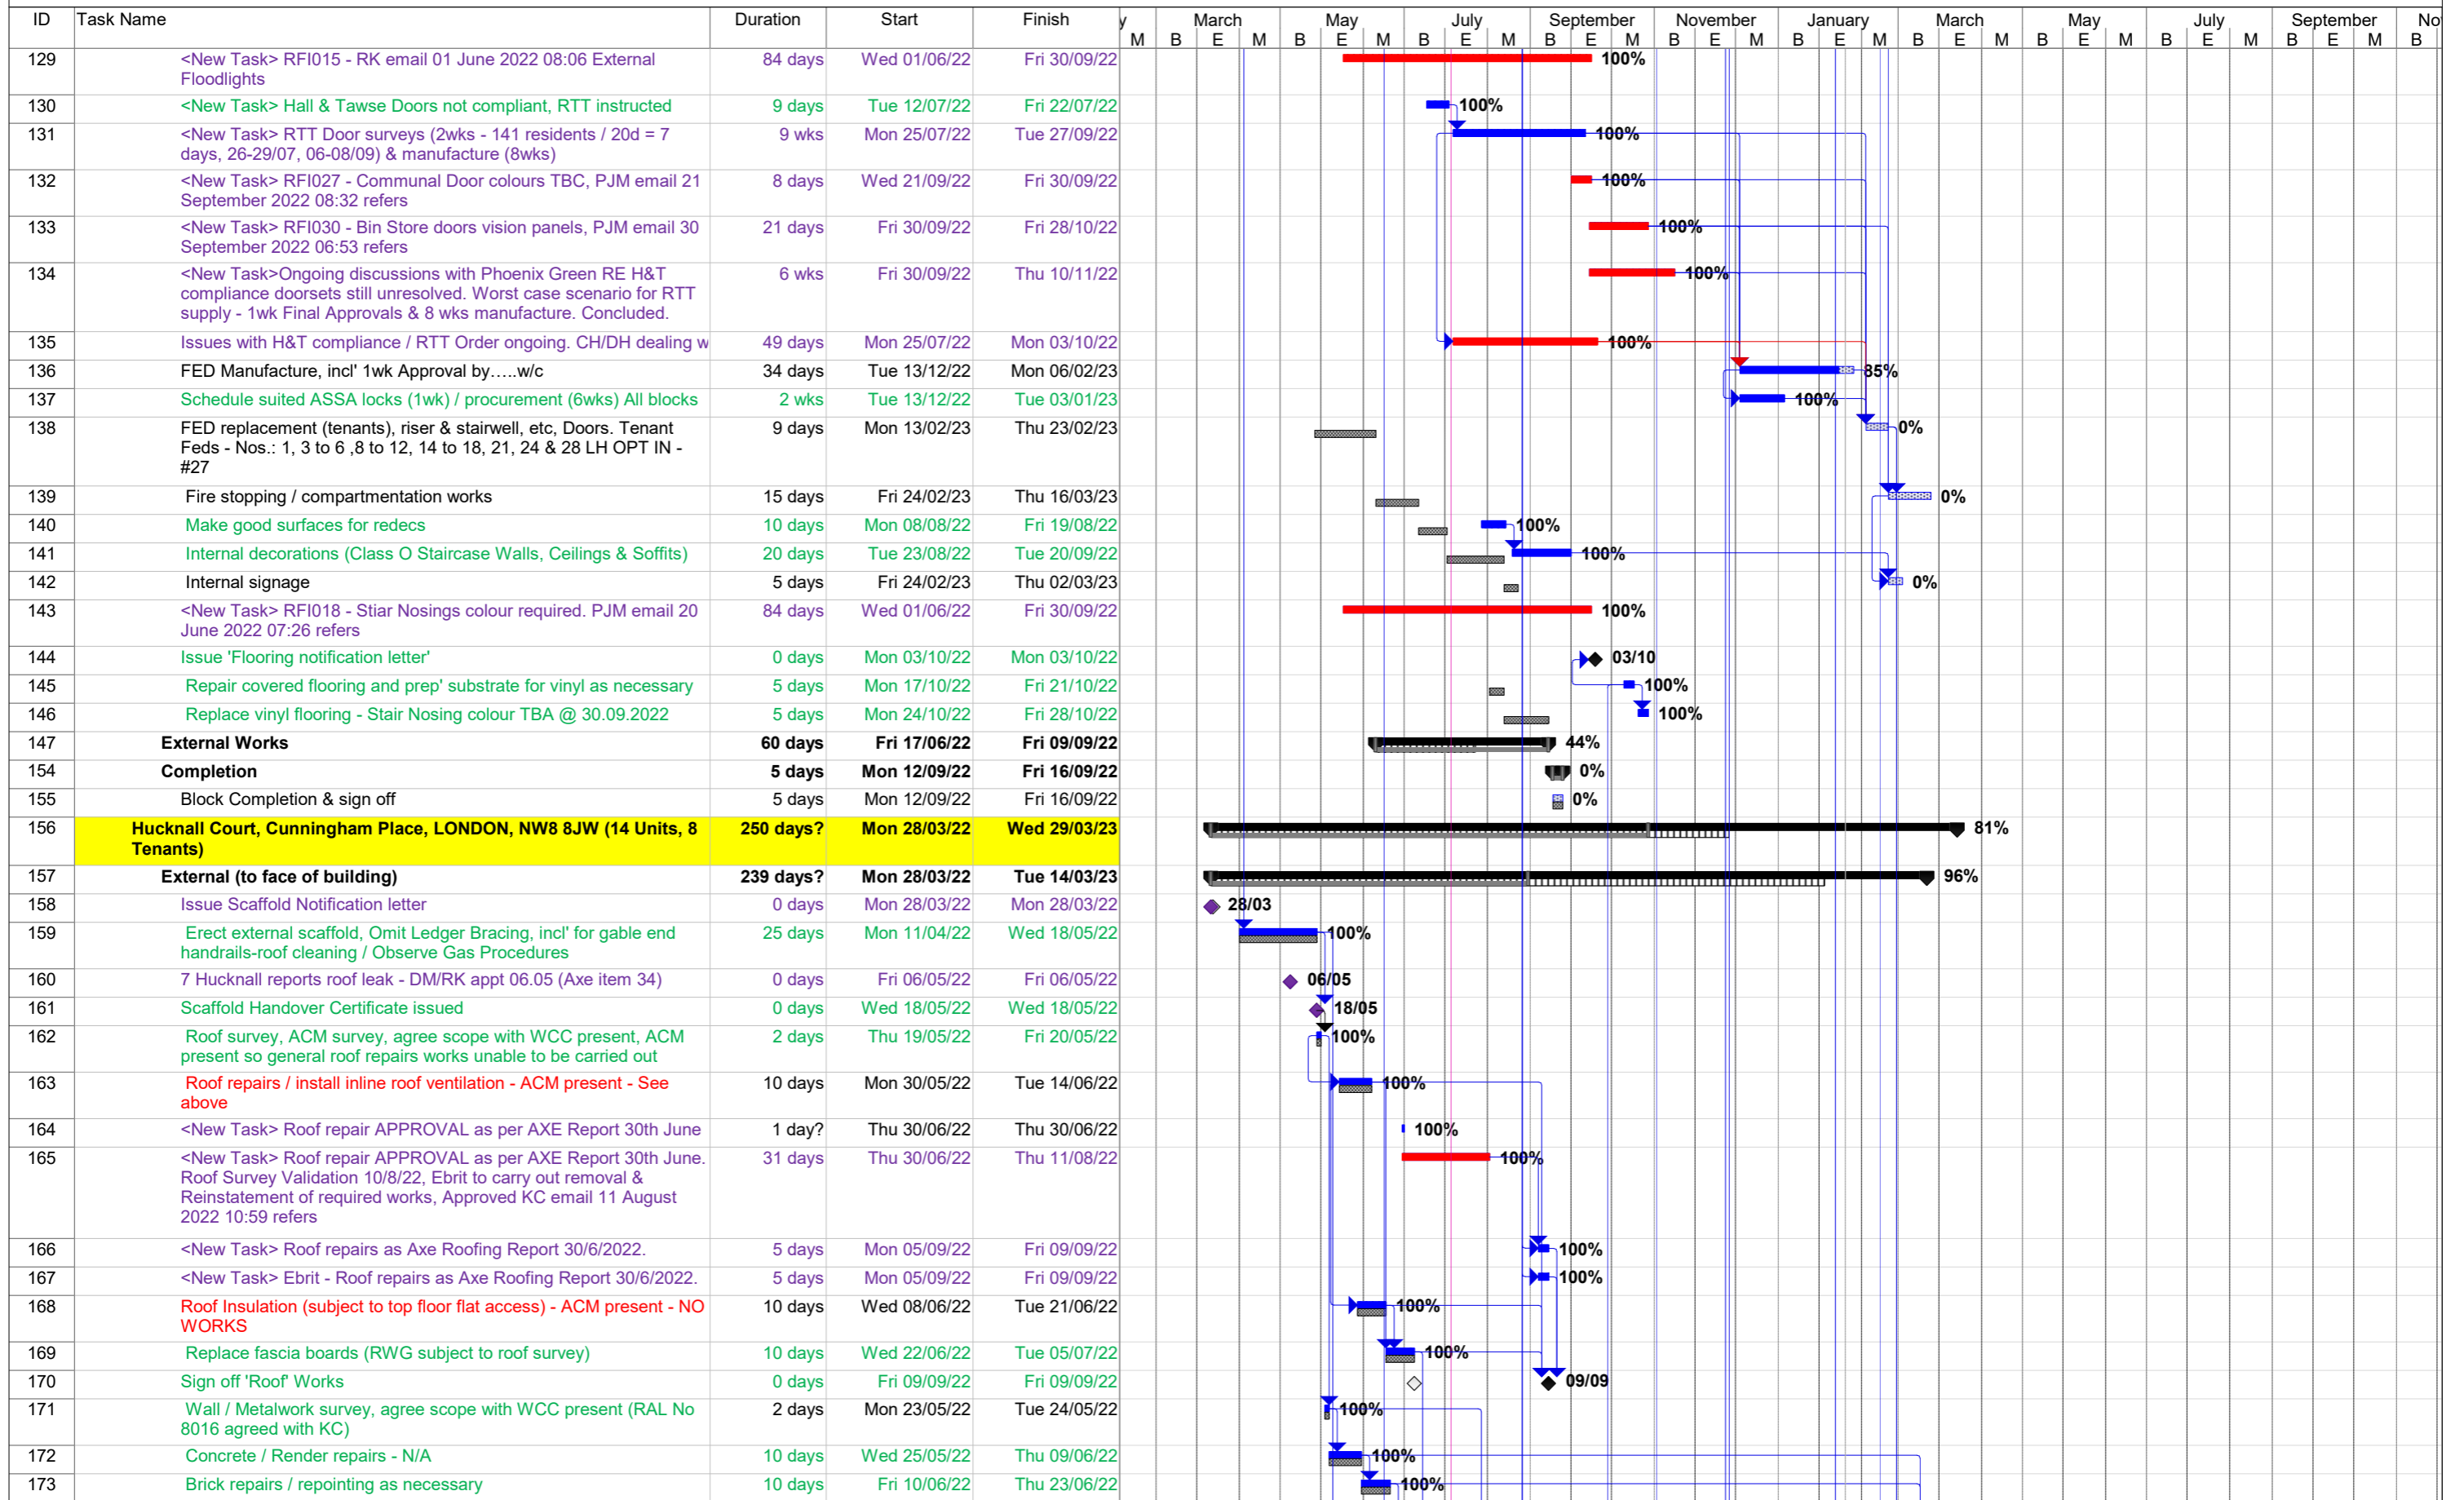


United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme

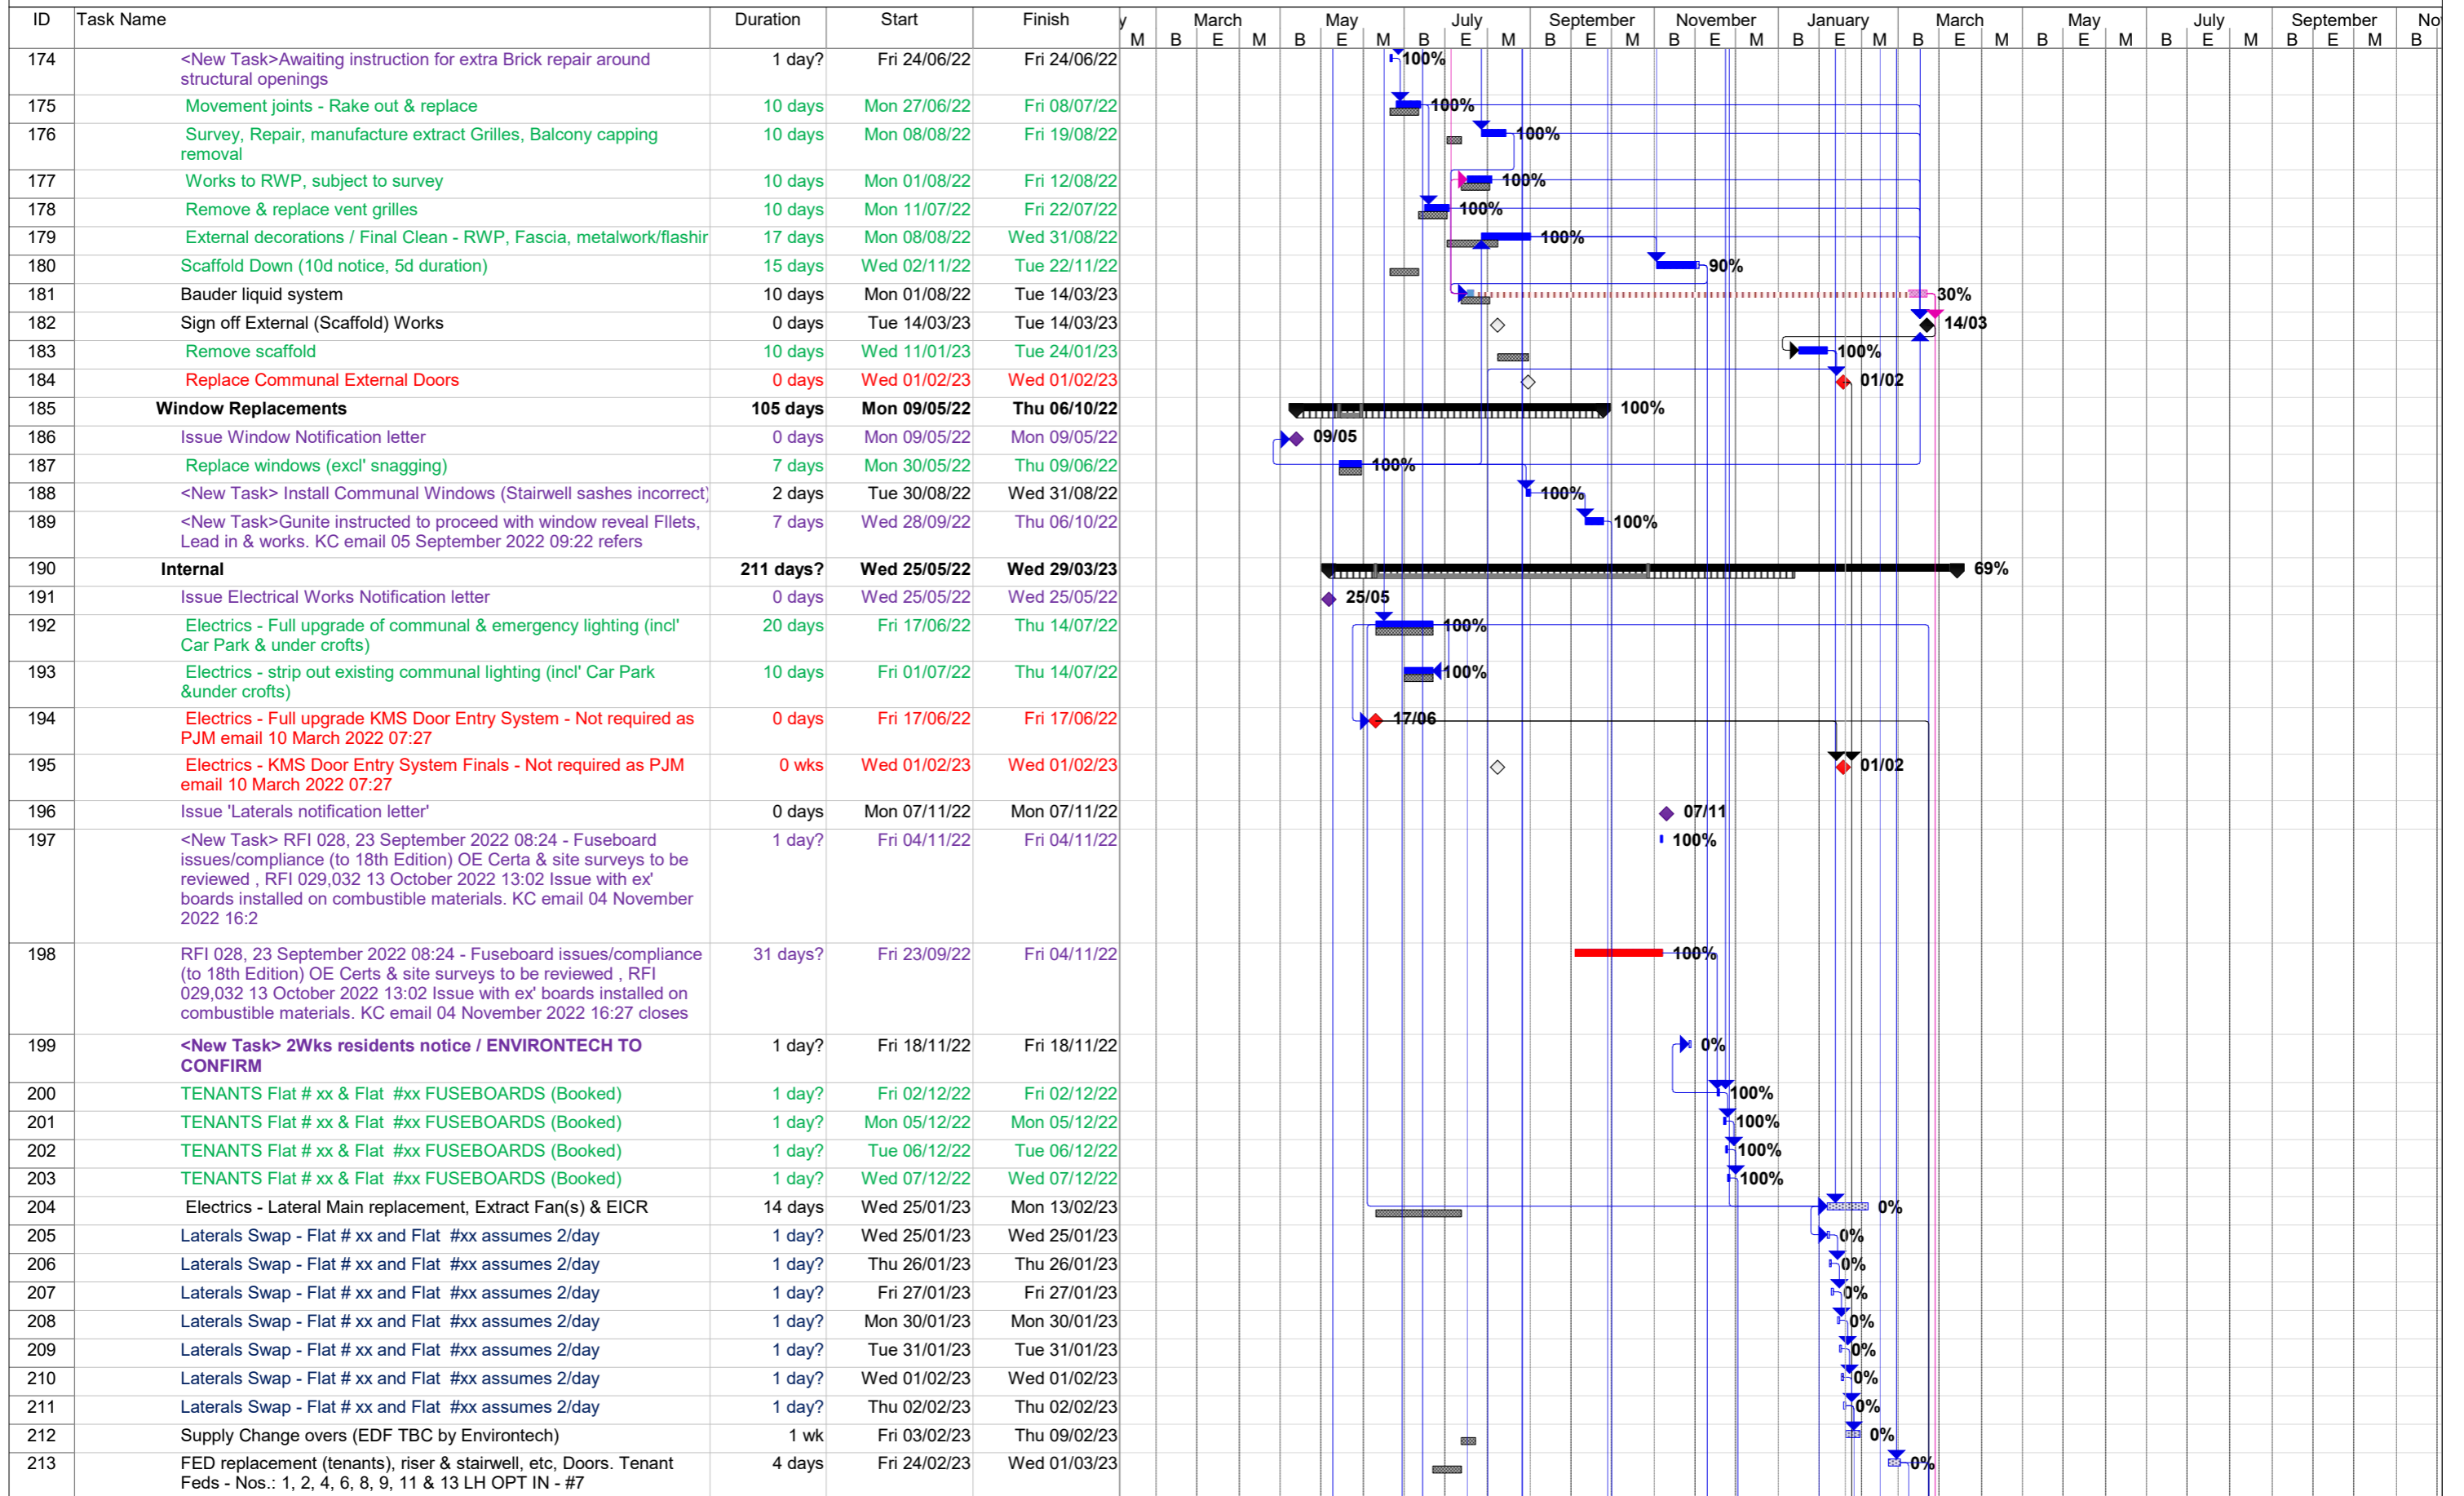

United Living 02692 - WHARNCLIFFE GARDENS - (AC103) Programme

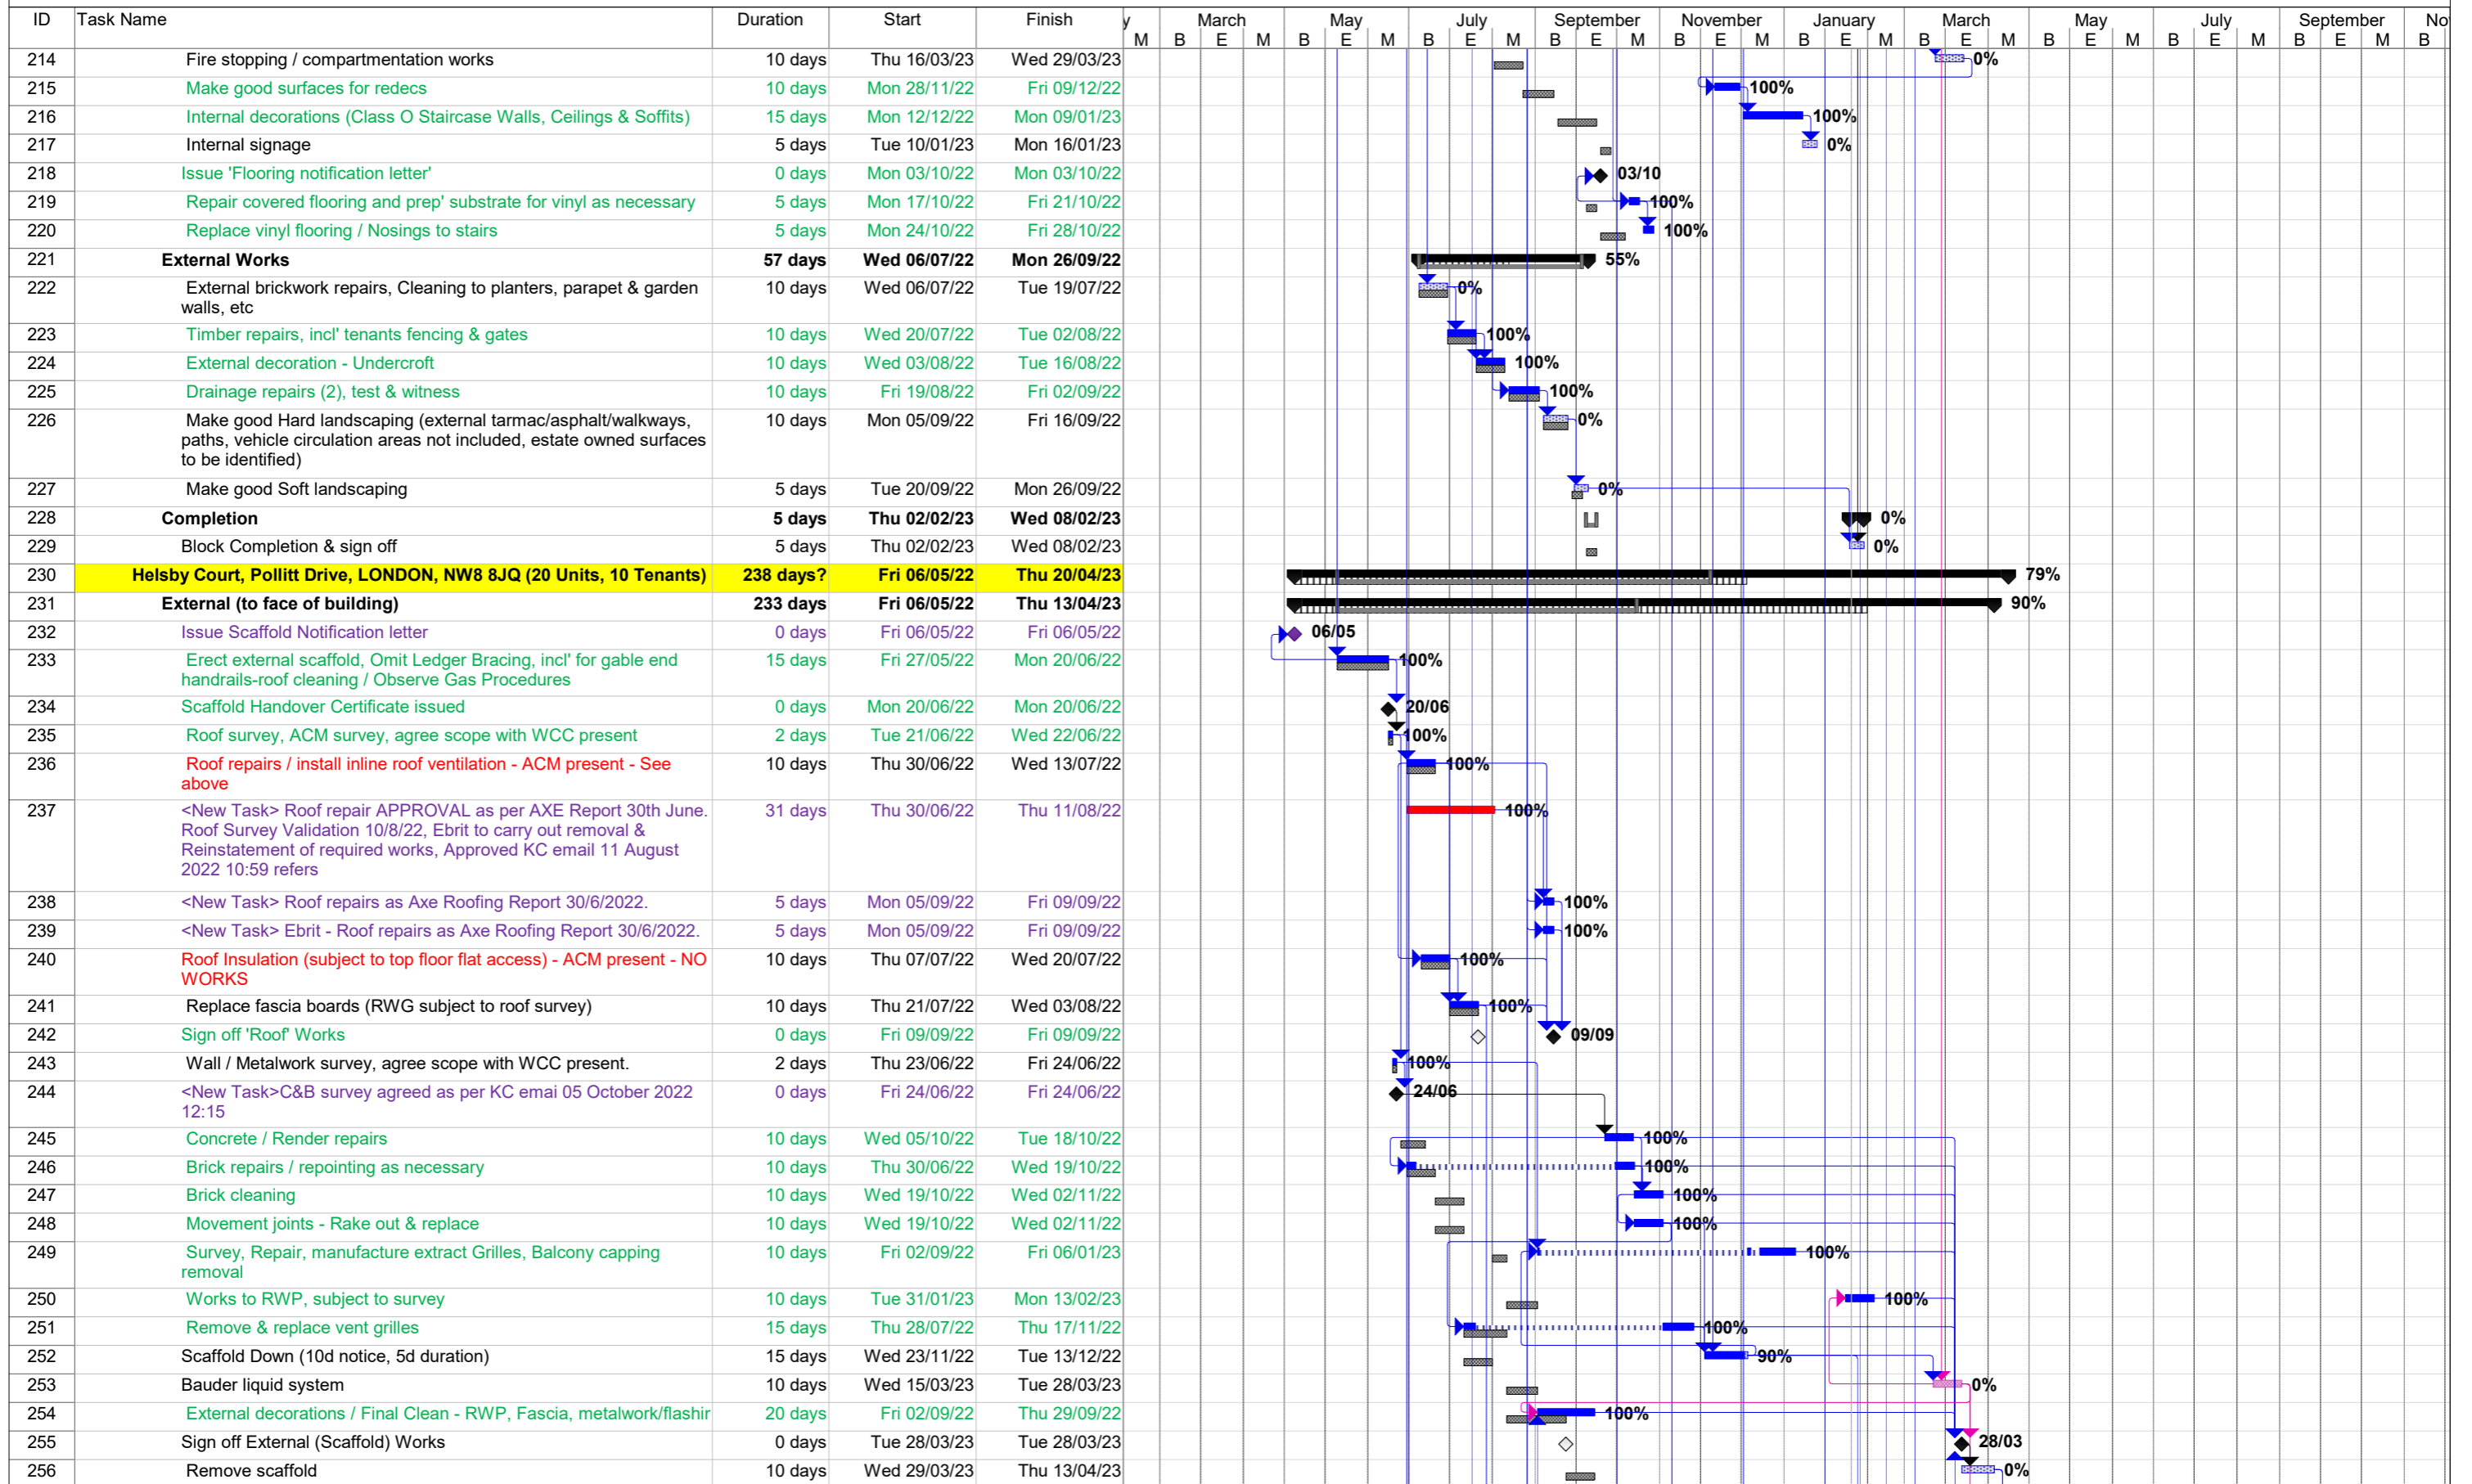


United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme




ID	Task Name	Duration	Start	Finish	Gantt Chart (March to November)																											
257	Replace Communal External Doors	0 days	Thu 13/04/23	Thu 13/04/23	[Gantt bar for 257: 100% complete]																											
258	Window Replacements	94 days	Thu 09/06/22	Thu 20/10/22	[Gantt bar for 258: 100% complete]																											
259	Issue Window Notification letter	0 days	Thu 09/06/22	Thu 09/06/22	[Gantt bar for 259: 100% complete]																											
260	Replace windows	20 days	Thu 30/06/22	Wed 27/07/22	[Gantt bar for 260: 100% complete]																											
261	<New Task> Install Communal Windows (Stairwell sashes incorrect)	2 days	Tue 30/08/22	Wed 31/08/22	[Gantt bar for 261: 100% complete]																											
262	<New Task> Gunite instructed to proceed with window reveal Fillets, Lead in & works. KC email 05 September 2022 09:22 refers	10 days	Fri 07/10/22	Thu 20/10/22	[Gantt bar for 262: 100% complete]																											
263	No access to flats #1, 17, 19. WCC aware (Report 13.07 refers)	23 days	Wed 13/07/22	Fri 12/08/22	[Gantt bar for 263: 100% complete]																											
264	Internal	186 days?	Fri 24/06/22	Wed 22/03/23	[Gantt bar for 264: 74% complete]																											
265	Issue Electrical Works Notification letter	0 days	Fri 24/06/22	Fri 24/06/22	[Gantt bar for 265: 100% complete]																											
266	Electrics - Full upgrade of communal & emergency lighting (incl' Car Park & under crofts)	15 days	Mon 01/08/22	Fri 19/08/22	[Gantt bar for 266: 100% complete]																											
267	Electrics - strip out existing communal lighting (incl' Car Park & under crofts)	10 days	Mon 08/08/22	Fri 19/08/22	[Gantt bar for 267: 100% complete]																											
268	Electrics - Full upgrade of Landlords LV system	40 days	Mon 01/08/22	Tue 27/09/22	[Gantt bar for 268: 100% complete]																											
269	Electrics - Full upgrade KMS Door Entry System - Not required as PJM email 10 March 2022 07:27	0 days	Mon 01/08/22	Mon 01/08/22	[Gantt bar for 269: 100% complete]																											
270	Electrics - KMS Door Entry System Finals - Not required as PJM email 10 March 2022 07:27	0 wks	Thu 13/10/22	Thu 13/10/22	[Gantt bar for 270: 100% complete]																											
271	Issue Electrical Works Notification letter	0 days	Thu 17/11/22	Thu 17/11/22	[Gantt bar for 271: 100% complete]																											
272	RFI 028, 23 September 2022 08:24 - Fuseboard issues/compliance (to 18th Edition) OE Certs & site surveys to be reviewed , RFI 029,032 13 October 2022 13:02 Issue with ex' boards installed on combustible materials. KC email 04 November 2022 16:27 closes	31 days?	Fri 23/09/22	Fri 04/11/22	[Gantt bar for 272: 100% complete]																											
273	RFI 028, 23 September 2022 08:24 - Fuseboard issues/compliance (to 18th Edition) OE Certs & site surveys to be reviewed , RFI 029,032 13 October 2022 13:02 Issue with ex' boards installed on combustible materials. KC email 04 November 2022 16:27 closes	31 days?	Fri 23/09/22	Fri 04/11/22	[Gantt bar for 273: 100% complete]																											
274	<New Task> 2Wks residents notice / ENVIRONTECH TO CONFIRM	1 day?	Thu 24/11/22	Thu 24/11/22	[Gantt bar for 274: 100% complete]																											
275	TENANTS Flat # xx & Flat #xx FUSEBOARDS (Booked)	1 day?	Thu 08/12/22	Thu 08/12/22	[Gantt bar for 275: 100% complete]																											
276	TENANTS Flat # xx & Flat #xx FUSEBOARDS (Booked)	1 day?	Fri 09/12/22	Fri 09/12/22	[Gantt bar for 276: 100% complete]																											
277	TENANTS Flat # xx & Flat #xx FUSEBOARDS (Booked)	1 day?	Mon 12/12/22	Mon 12/12/22	[Gantt bar for 277: 100% complete]																											
278	TENANTS Flat # xx & Flat #xx FUSEBOARDS (Booked)	1 day?	Tue 13/12/22	Tue 13/12/22	[Gantt bar for 278: 100% complete]																											
279	TENANTS Flat # xx & Flat #xx FUSEBOARDS (Booked)	1 day?	Wed 14/12/22	Wed 14/12/22	[Gantt bar for 279: 100% complete]																											
280	Electrics - Lateral Main replacement, Extract Fan(s) & EICR	20 days	Fri 03/02/23	Thu 02/03/23	[Gantt bar for 280: 0% complete]																											
281	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Fri 03/02/23	Fri 03/02/23	[Gantt bar for 281: 0% complete]																											
282	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Mon 06/02/23	Mon 06/02/23	[Gantt bar for 282: 0% complete]																											
283	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Tue 07/02/23	Tue 07/02/23	[Gantt bar for 283: 0% complete]																											
284	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Wed 08/02/23	Wed 08/02/23	[Gantt bar for 284: 0% complete]																											
285	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Thu 09/02/23	Thu 09/02/23	[Gantt bar for 285: 0% complete]																											
286	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Fri 10/02/23	Fri 10/02/23	[Gantt bar for 286: 0% complete]																											
287	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Mon 13/02/23	Mon 13/02/23	[Gantt bar for 287: 0% complete]																											
288	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Tue 14/02/23	Tue 14/02/23	[Gantt bar for 288: 0% complete]																											
289	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Wed 15/02/23	Wed 15/02/23	[Gantt bar for 289: 0% complete]																											
290	Laterals Swap - Flat # xx and Flat #xx assumes 2/day	1 day?	Thu 16/02/23	Thu 16/02/23	[Gantt bar for 290: 0% complete]																											
291	Supply Change overs (EDF TBC by Environtech)	1 wk	Fri 17/02/23	Thu 23/02/23	[Gantt bar for 291: 0% complete]																											
292	FED replacement (tenants), riser & stairwell, etc, Doors. Tenant Feds - Nos.: 1 to 4 , 6, 7, 9, 10, 15 & 16	5 days	Thu 02/03/23	Wed 08/03/23	[Gantt bar for 292: 0% complete]																											
293	Fire stopping / compartmentation works	10 days	Thu 09/03/23	Wed 22/03/23	[Gantt bar for 293: 0% complete]																											
294	Make good surfaces for redecs	10 days	Mon 05/12/22	Fri 16/12/22	[Gantt bar for 294: 100% complete]																											
295	Internal decorations (Class O Staircase Walls, Ceilings & Soffits)	15 days	Wed 14/12/22	Wed 11/01/23	[Gantt bar for 295: 100% complete]																											
296	Internal signage	5 days	Thu 12/01/23	Wed 18/01/23	[Gantt bar for 296: 0% complete]																											

United Living 02692 - WHARNCLIFFE GARDENS - (AC103) Programme

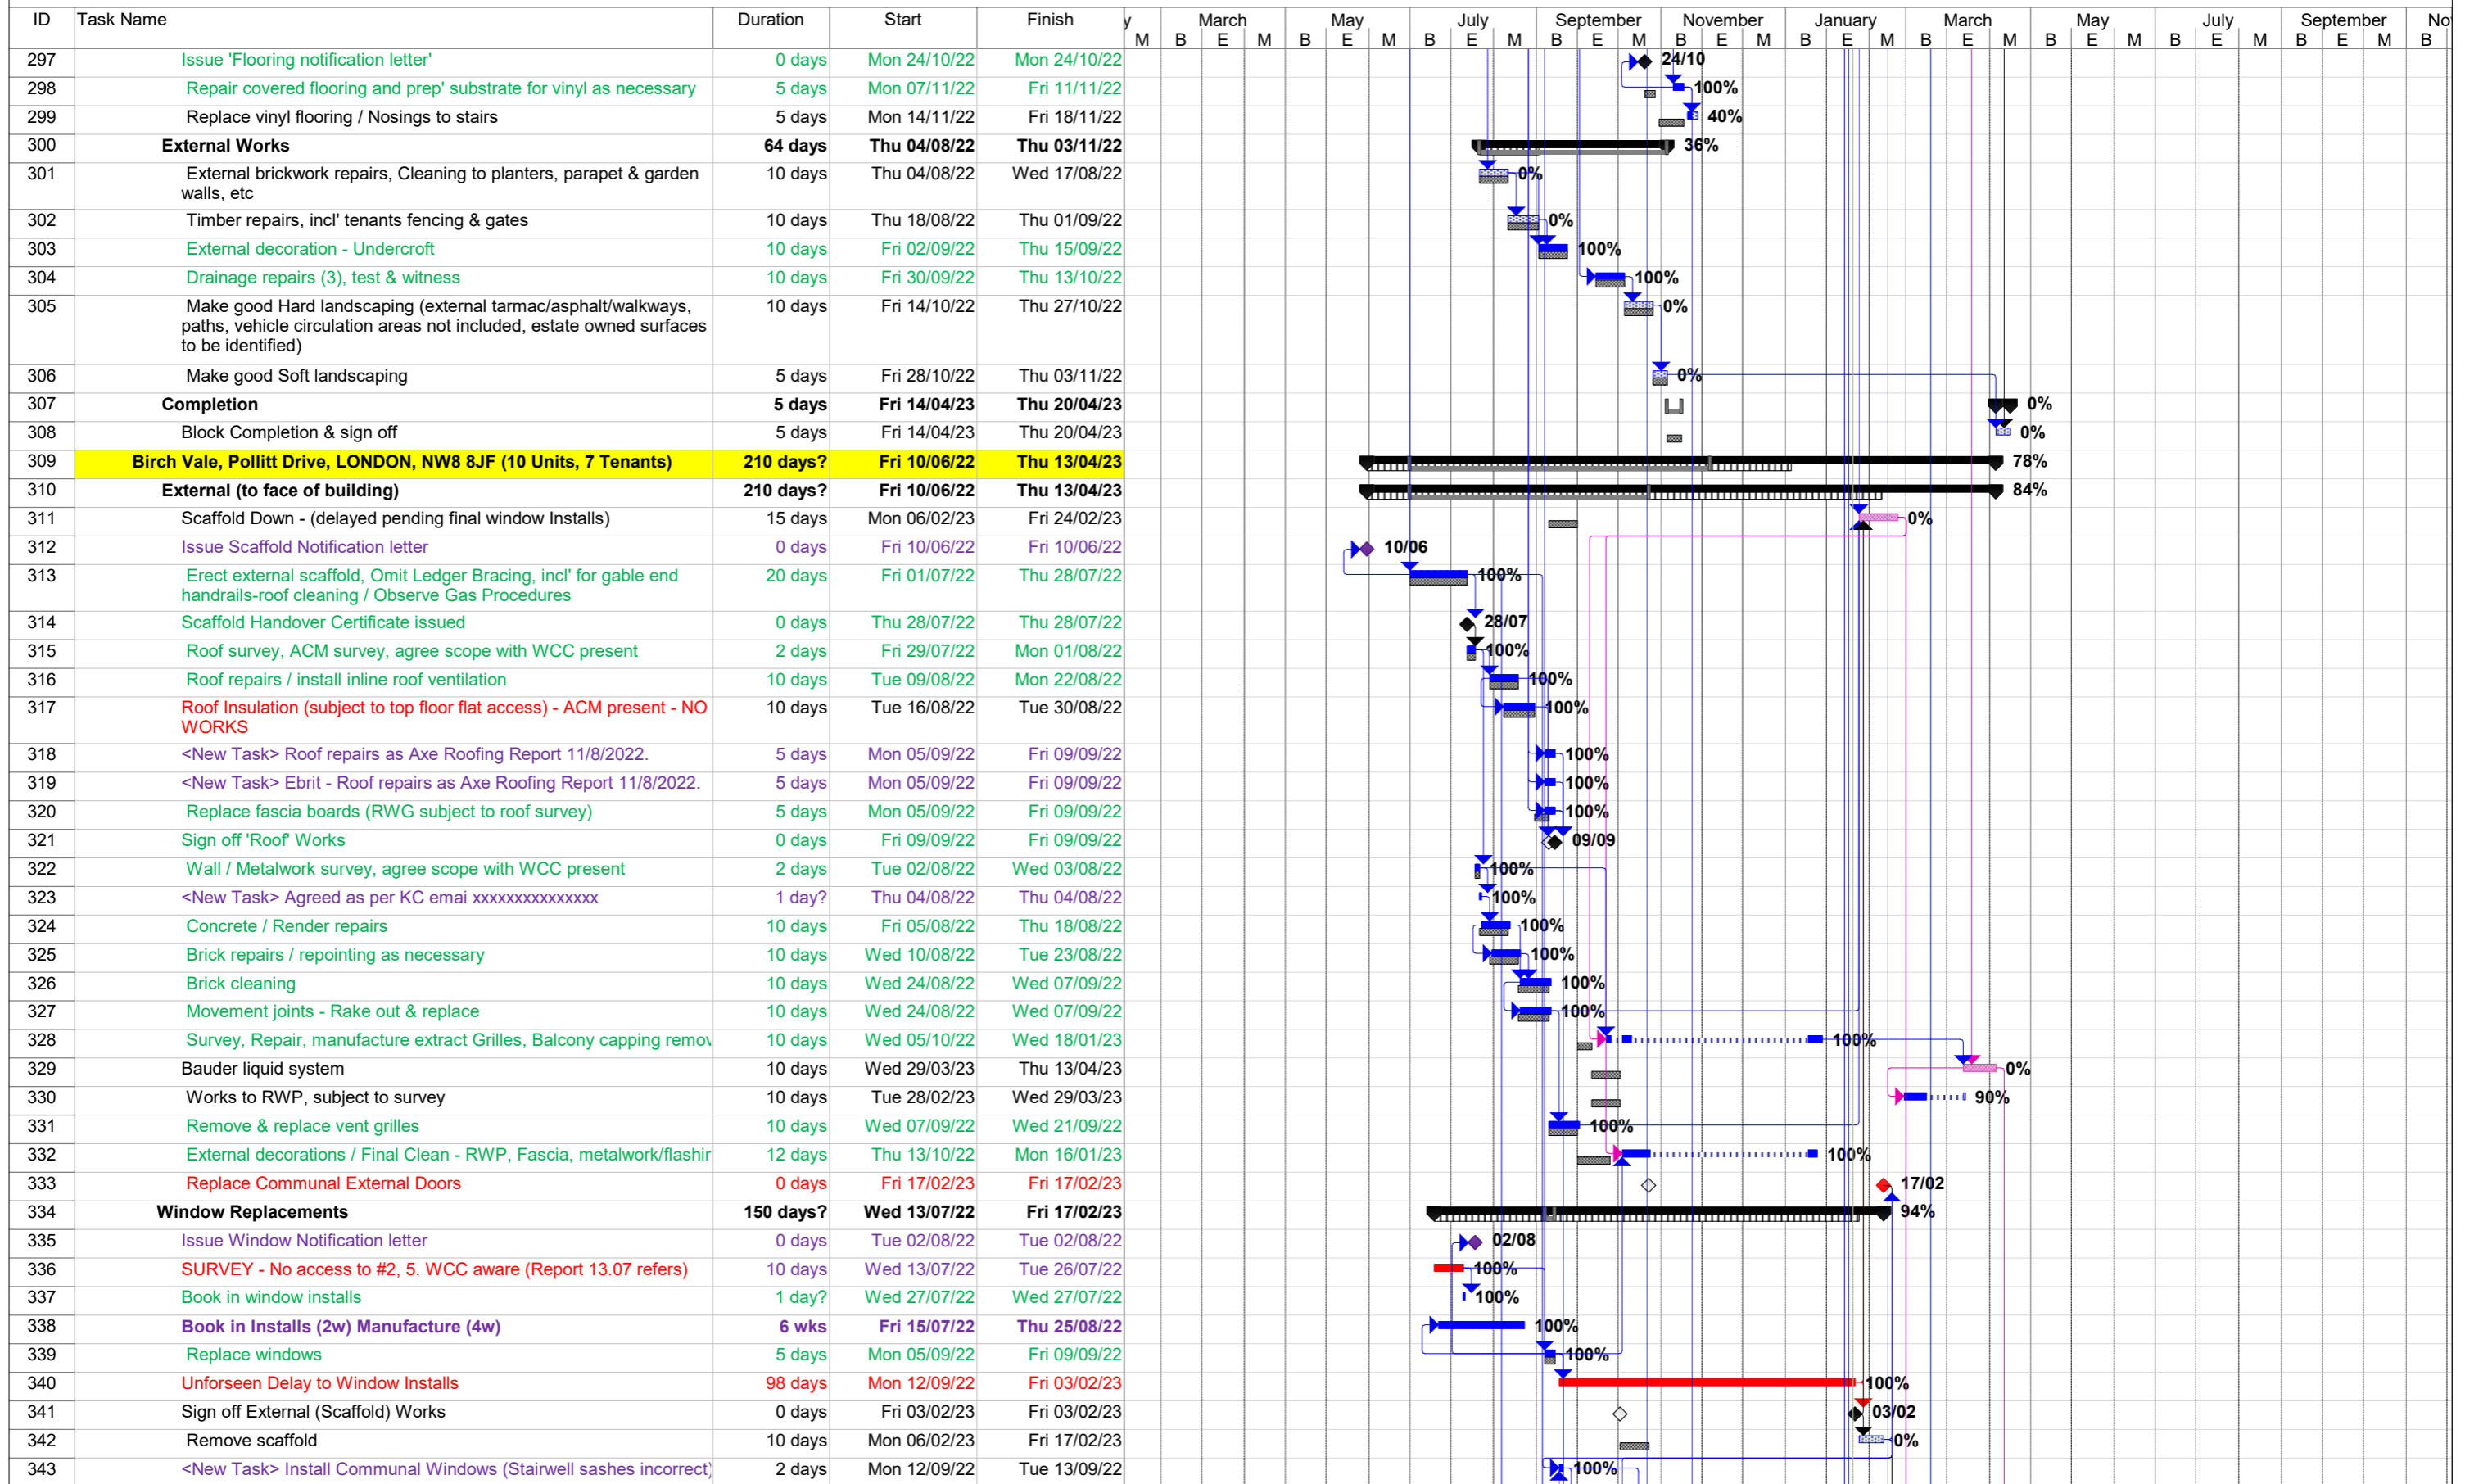

United Living 02692 - WHARNCLIFFE GARDENS - (AC103) Programme

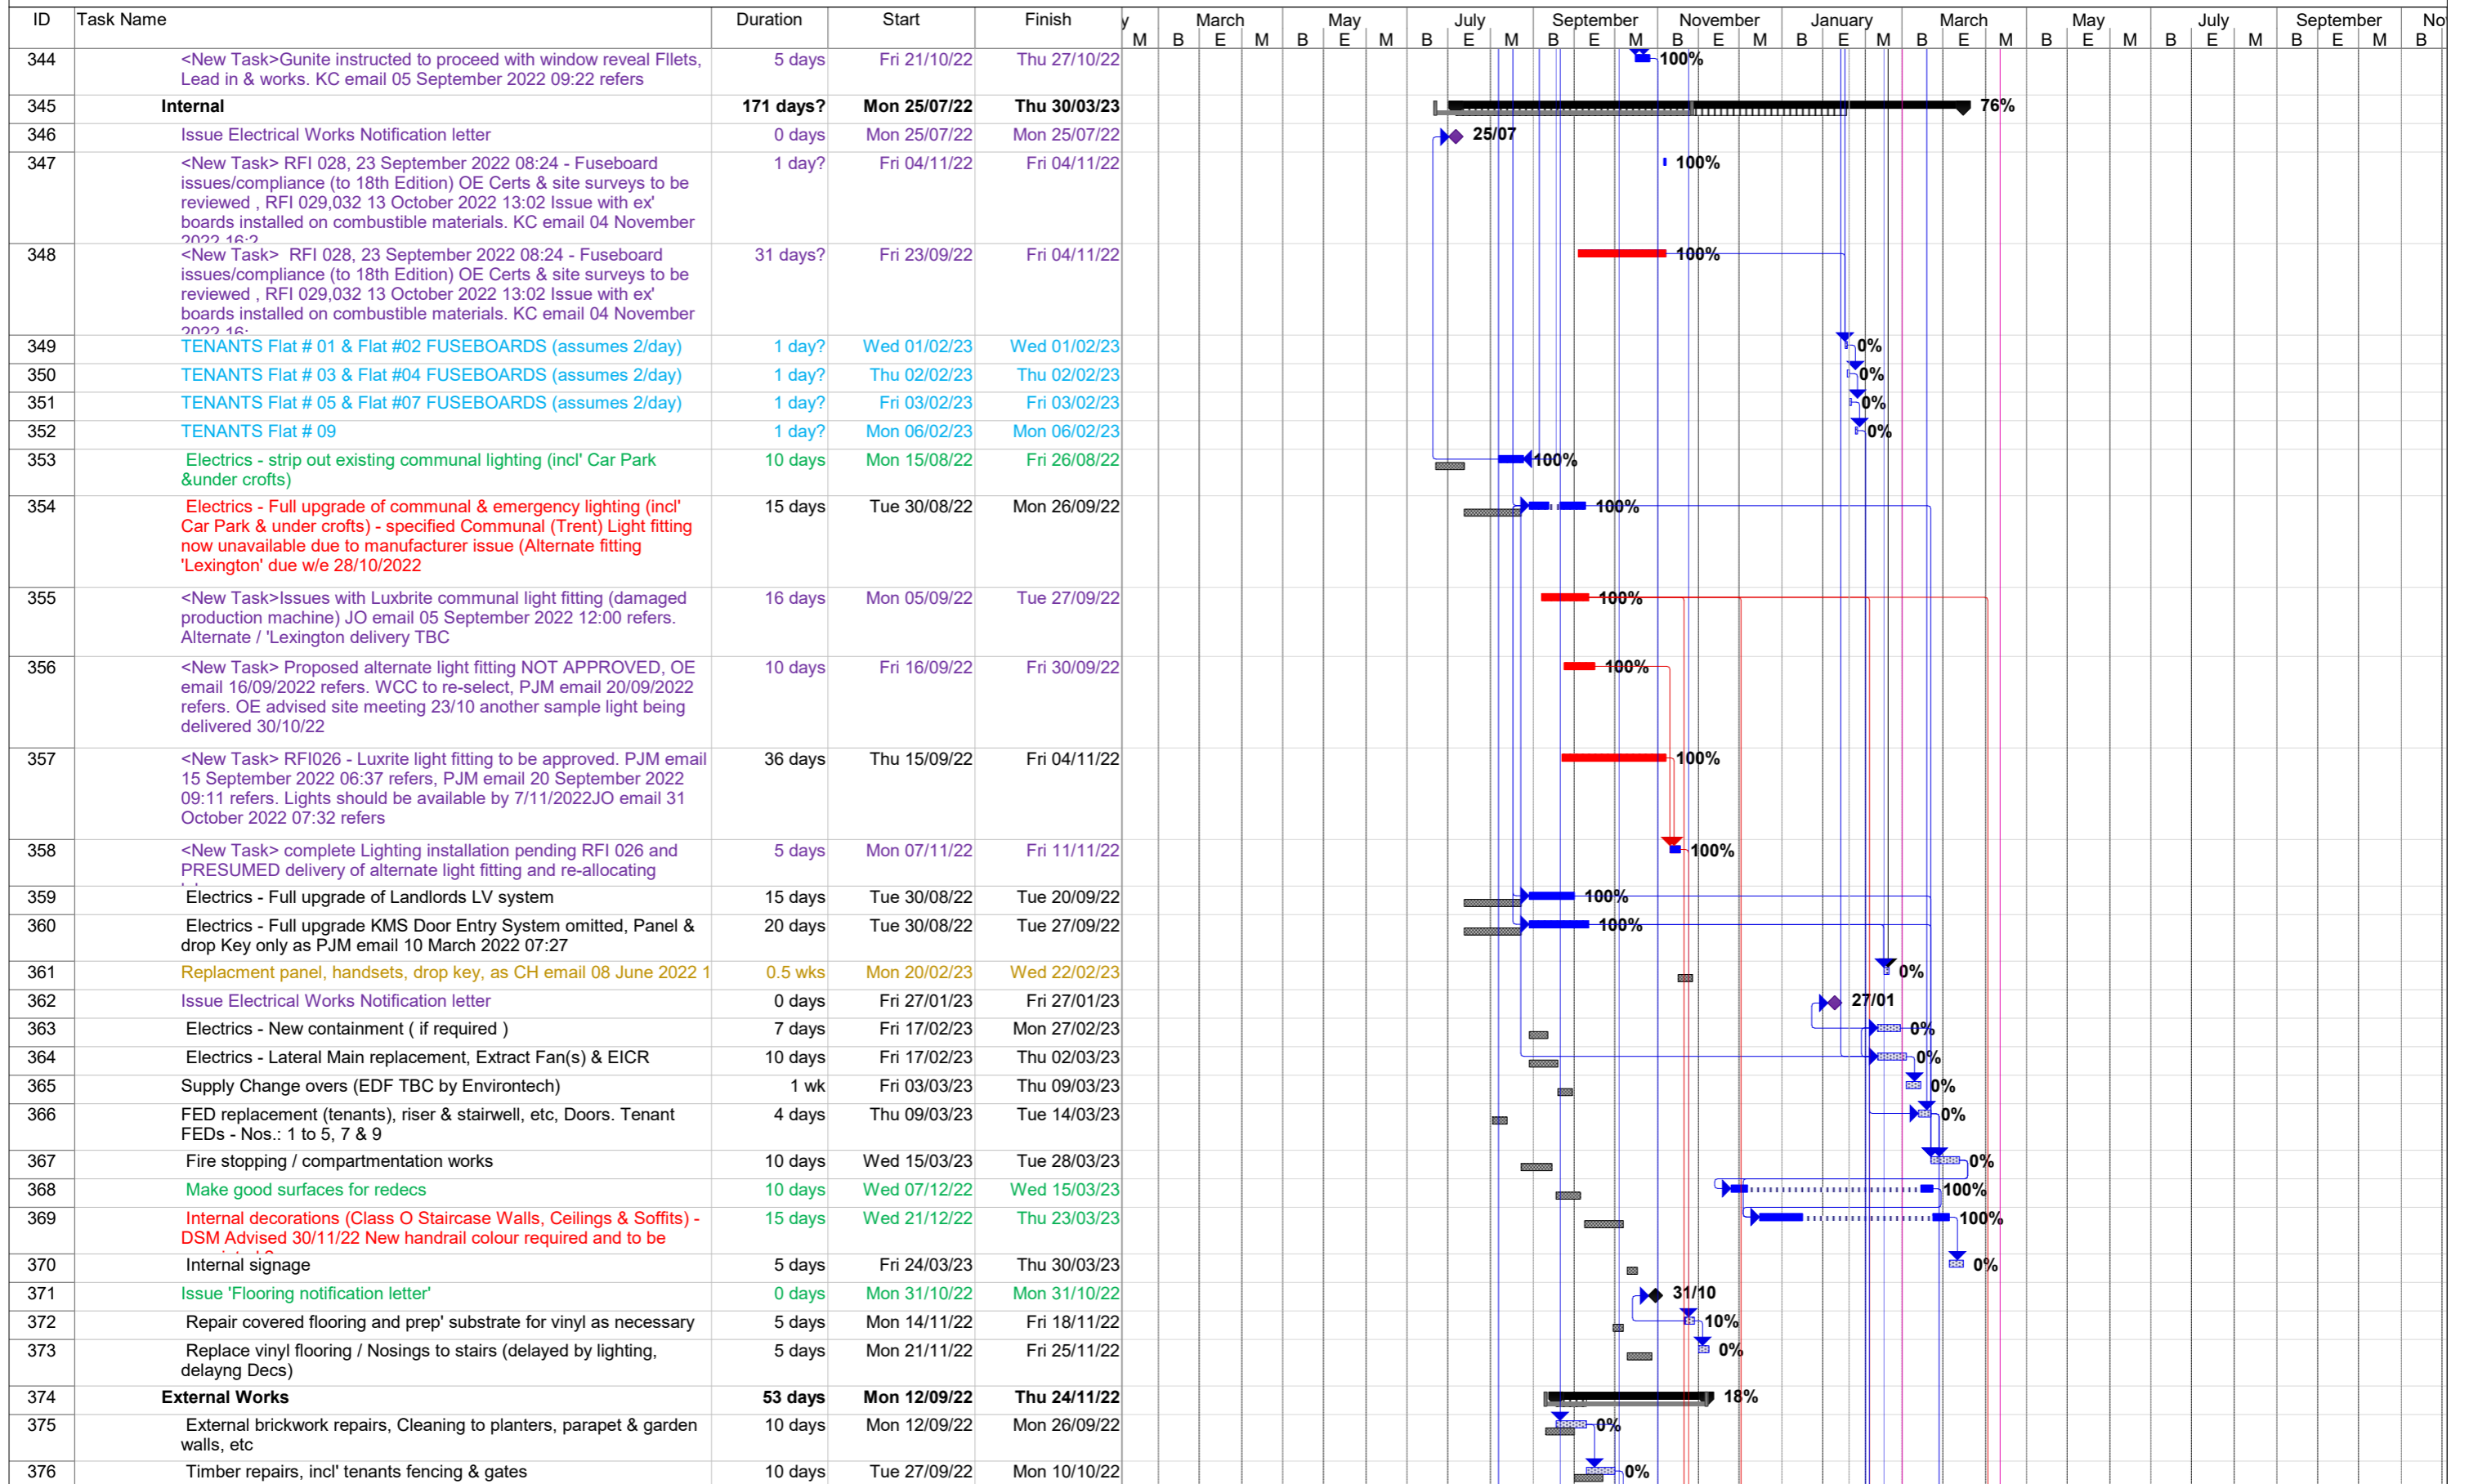


United Living 02692 - WHARNCLIFFE GARDENS - (AC103) Programme



ID	Task Name	Duration	Start	Finish	Gantt Chart (Months: March, May, July, September, November, January, March, May, July, September, No)																											
377	External decoration - Undercroft	10 days	Tue 11/10/22	Mon 24/10/22	[Gantt bar]																											
378	Drainage repairs (4), test & witness	10 days	Fri 21/10/22	Thu 03/11/22	[Gantt bar]																											
379	Make good Hard landscaping (external tarmac/asphalt/walkways, paths, vehicle circulation areas not included, estate owned surfaces to be identified)	10 days	Fri 04/11/22	Thu 17/11/22	[Gantt bar]																											
380	Make good Soft landscaping	5 days	Fri 18/11/22	Thu 24/11/22	[Gantt bar]																											
381	Rothley Court, 22 St. Johns Wood Road, LONDON, NW8 8UL (17 Units, 0 Tenants)	212 days?	Wed 22/06/22	Thu 27/04/23	[Gantt bar: 67%]																											
382	External (to face of building)	212 days?	Wed 22/06/22	Thu 27/04/23	[Gantt bar: 77%]																											
383	Temp' works Structure Application	0 days	Wed 22/06/22	Wed 22/06/22	[Gantt bar]																											
384	Issue Scaffold Notification letter	0 days	Wed 20/07/22	Wed 20/07/22	[Gantt bar]																											
385	Erect external scaffold, Omit Ledger Bracing, incl' for gable end handrails-roof cleaning / Observe Gas Procedures	15 days	Mon 15/08/22	Mon 05/09/22	[Gantt bar]																											
386	<New Task>RFI031 - Extra scaffold to 'Pinner Court' Roof discussed with KC 15/09/2022, PJM email 30 September 2022	5 days	Fri 30/09/22	Thu 06/10/22	[Gantt bar]																											
387	Scaffold Handover Certificate issued	0 days	Mon 05/09/22	Mon 05/09/22	[Gantt bar]																											
388	Roof survey, ACM survey, agree scope with WCC present	2 days	Tue 06/09/22	Wed 07/09/22	[Gantt bar]																											
389	Roof repairs / install inline roof ventilation	10 days	Thu 08/09/22	Thu 22/09/22	[Gantt bar]																											
390	Replace fascia boards (RWG subject to roof survey)	10 days	Fri 30/09/22	Thu 13/10/22	[Gantt bar]																											
391	Sign off 'Roof' Works	0 days	Thu 13/10/22	Thu 13/10/22	[Gantt bar]																											
392	Wall / Metalwork survey, agree scope with WCC present	2 days	Thu 08/09/22	Fri 09/09/22	[Gantt bar]																											
393	<New Task> Agreed as per KC emai xxxxxxxxxxxxxxxx	1 day?	Mon 12/09/22	Mon 12/09/22	[Gantt bar]																											
394	Concrete / Render repairs	10 days	Tue 13/09/22	Tue 27/09/22	[Gantt bar]																											
395	Brick repairs / repointing as necessary	10 days	Fri 16/09/22	Fri 30/09/22	[Gantt bar]																											
396	Brick cleaning	10 days	Mon 03/10/22	Fri 14/10/22	[Gantt bar]																											
397	Movement joints - Rake out & replace	10 days	Mon 03/10/22	Fri 14/10/22	[Gantt bar]																											
398	Strike balcony scaffold	10 days	Mon 17/10/22	Fri 28/10/22	[Gantt bar]																											
399	Survey, Repair, manufacture extract Grilles, Balcony capping removal	10 days	Mon 31/10/22	Fri 11/11/22	[Gantt bar]																											
400	Bauder liquid system	10 days	Fri 14/04/23	Thu 27/04/23	[Gantt bar]																											
401	Works to RWP, subject to survey	10 days	Wed 08/02/23	Tue 21/02/23	[Gantt bar]																											
402	Remove & replace vent grilles	10 days	Mon 17/10/22	Fri 28/10/22	[Gantt bar]																											
403	External decorations / Final Clean - RWP, Fascia, metalwork/flashir	10 days	Thu 02/02/23	Wed 15/02/23	[Gantt bar]																											
404	Sign off External (Scaffold) Works	0 days	Fri 24/02/23	Fri 24/02/23	[Gantt bar]																											
405	Scaffold Down (10d notice, 5d duration)	15 days	Mon 27/02/23	Fri 17/03/23	[Gantt bar]																											
406	Remove scaffold	10 days	Mon 27/02/23	Fri 10/03/23	[Gantt bar]																											
407	Replace Communal External Doors	0 days	Fri 10/03/23	Fri 10/03/23	[Gantt bar]																											
408	Window Replacements (#8, #12 over Pinner Ct!)	84 days	Wed 13/07/22	Wed 09/11/22	[Gantt bar: 100%]																											
409	Issue Window Notification letter	0 days	Fri 19/08/22	Fri 19/08/22	[Gantt bar]																											
410	No access to flats #4, 9, 13, 15. WCC aware (Report 13.07 refers)	10 days	Wed 13/07/22	Tue 26/07/22	[Gantt bar]																											
411	Book in Installs (2w) Manufacture (4w)	6 wks	Fri 22/07/22	Fri 02/09/22	[Gantt bar]																											
412	Replace windows, Flats, Bin Stores, Stairwells	9 days	Mon 12/09/22	Fri 23/09/22	[Gantt bar]																											
413	<New Task>Gunite instructed to proceed with window reveal Filets, Lead in & works. KC email 05 September 2022 09:22 refers	9 days	Fri 28/10/22	Wed 09/11/22	[Gantt bar]																											
414	Internal	174.75 days?	Mon 01/08/22	Fri 14/04/23	[Gantt bar: 58%]																											
415	Issue Electrical Works Notification letter	0 days	Mon 01/08/22	Mon 01/08/22	[Gantt bar]																											
416	<New Task> RFI 028, 23 September 2022 08:24 - Fuseboard issues/compliance (to 18th Edition) OE Certs & site surveys to be reviewed , RFI 029,032 13 October 2022 13:02 Issue with ex' boards installed on combustible materials. KC email 04 November 2022 16:2	31 days?	Fri 23/09/22	Fri 04/11/22	[Gantt bar]																											
417	ZERO TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/d	0 days	Tue 14/02/23	Tue 14/02/23	[Gantt bar]																											
418	Electrics - strip out existing communal lighting (incl' Car Park & under crofts)	10 days	Mon 22/08/22	Mon 05/09/22	[Gantt bar]																											
419	Electrics - Full upgrade of communal & emergency lighting (incl' Car Park & under crofts)	20 days	Mon 14/11/22	Fri 09/12/22	[Gantt bar]																											


United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme

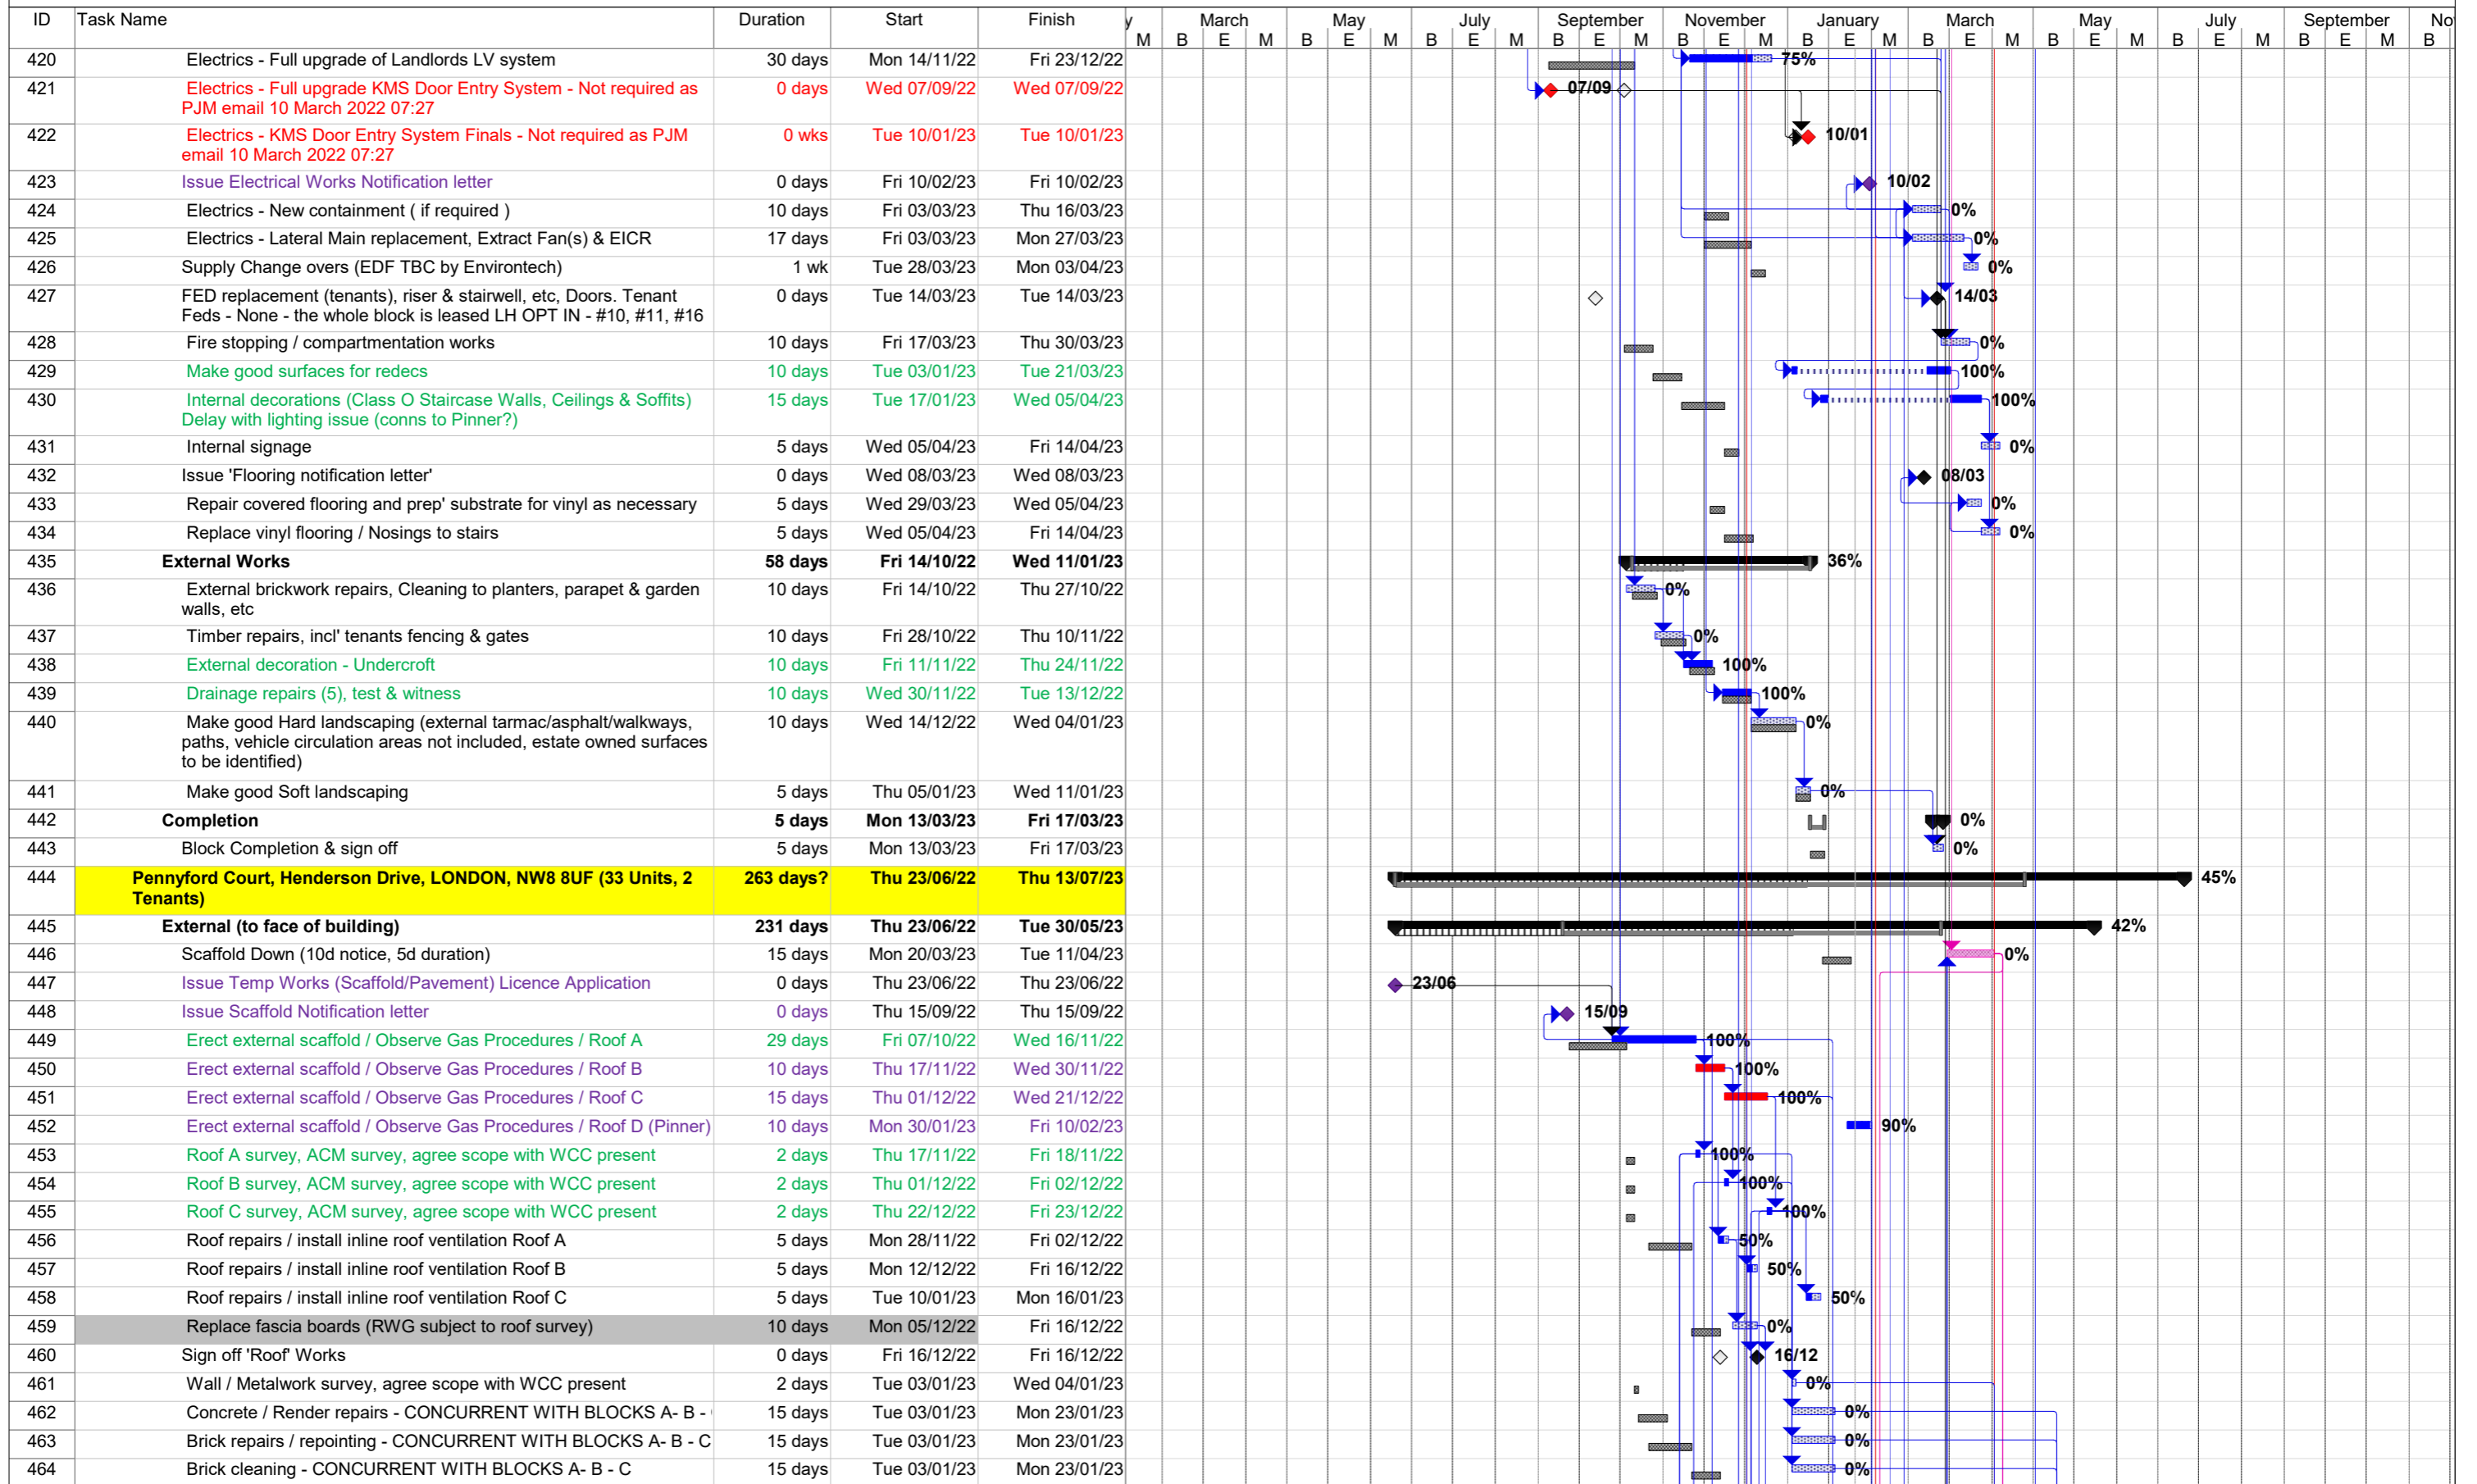



United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme

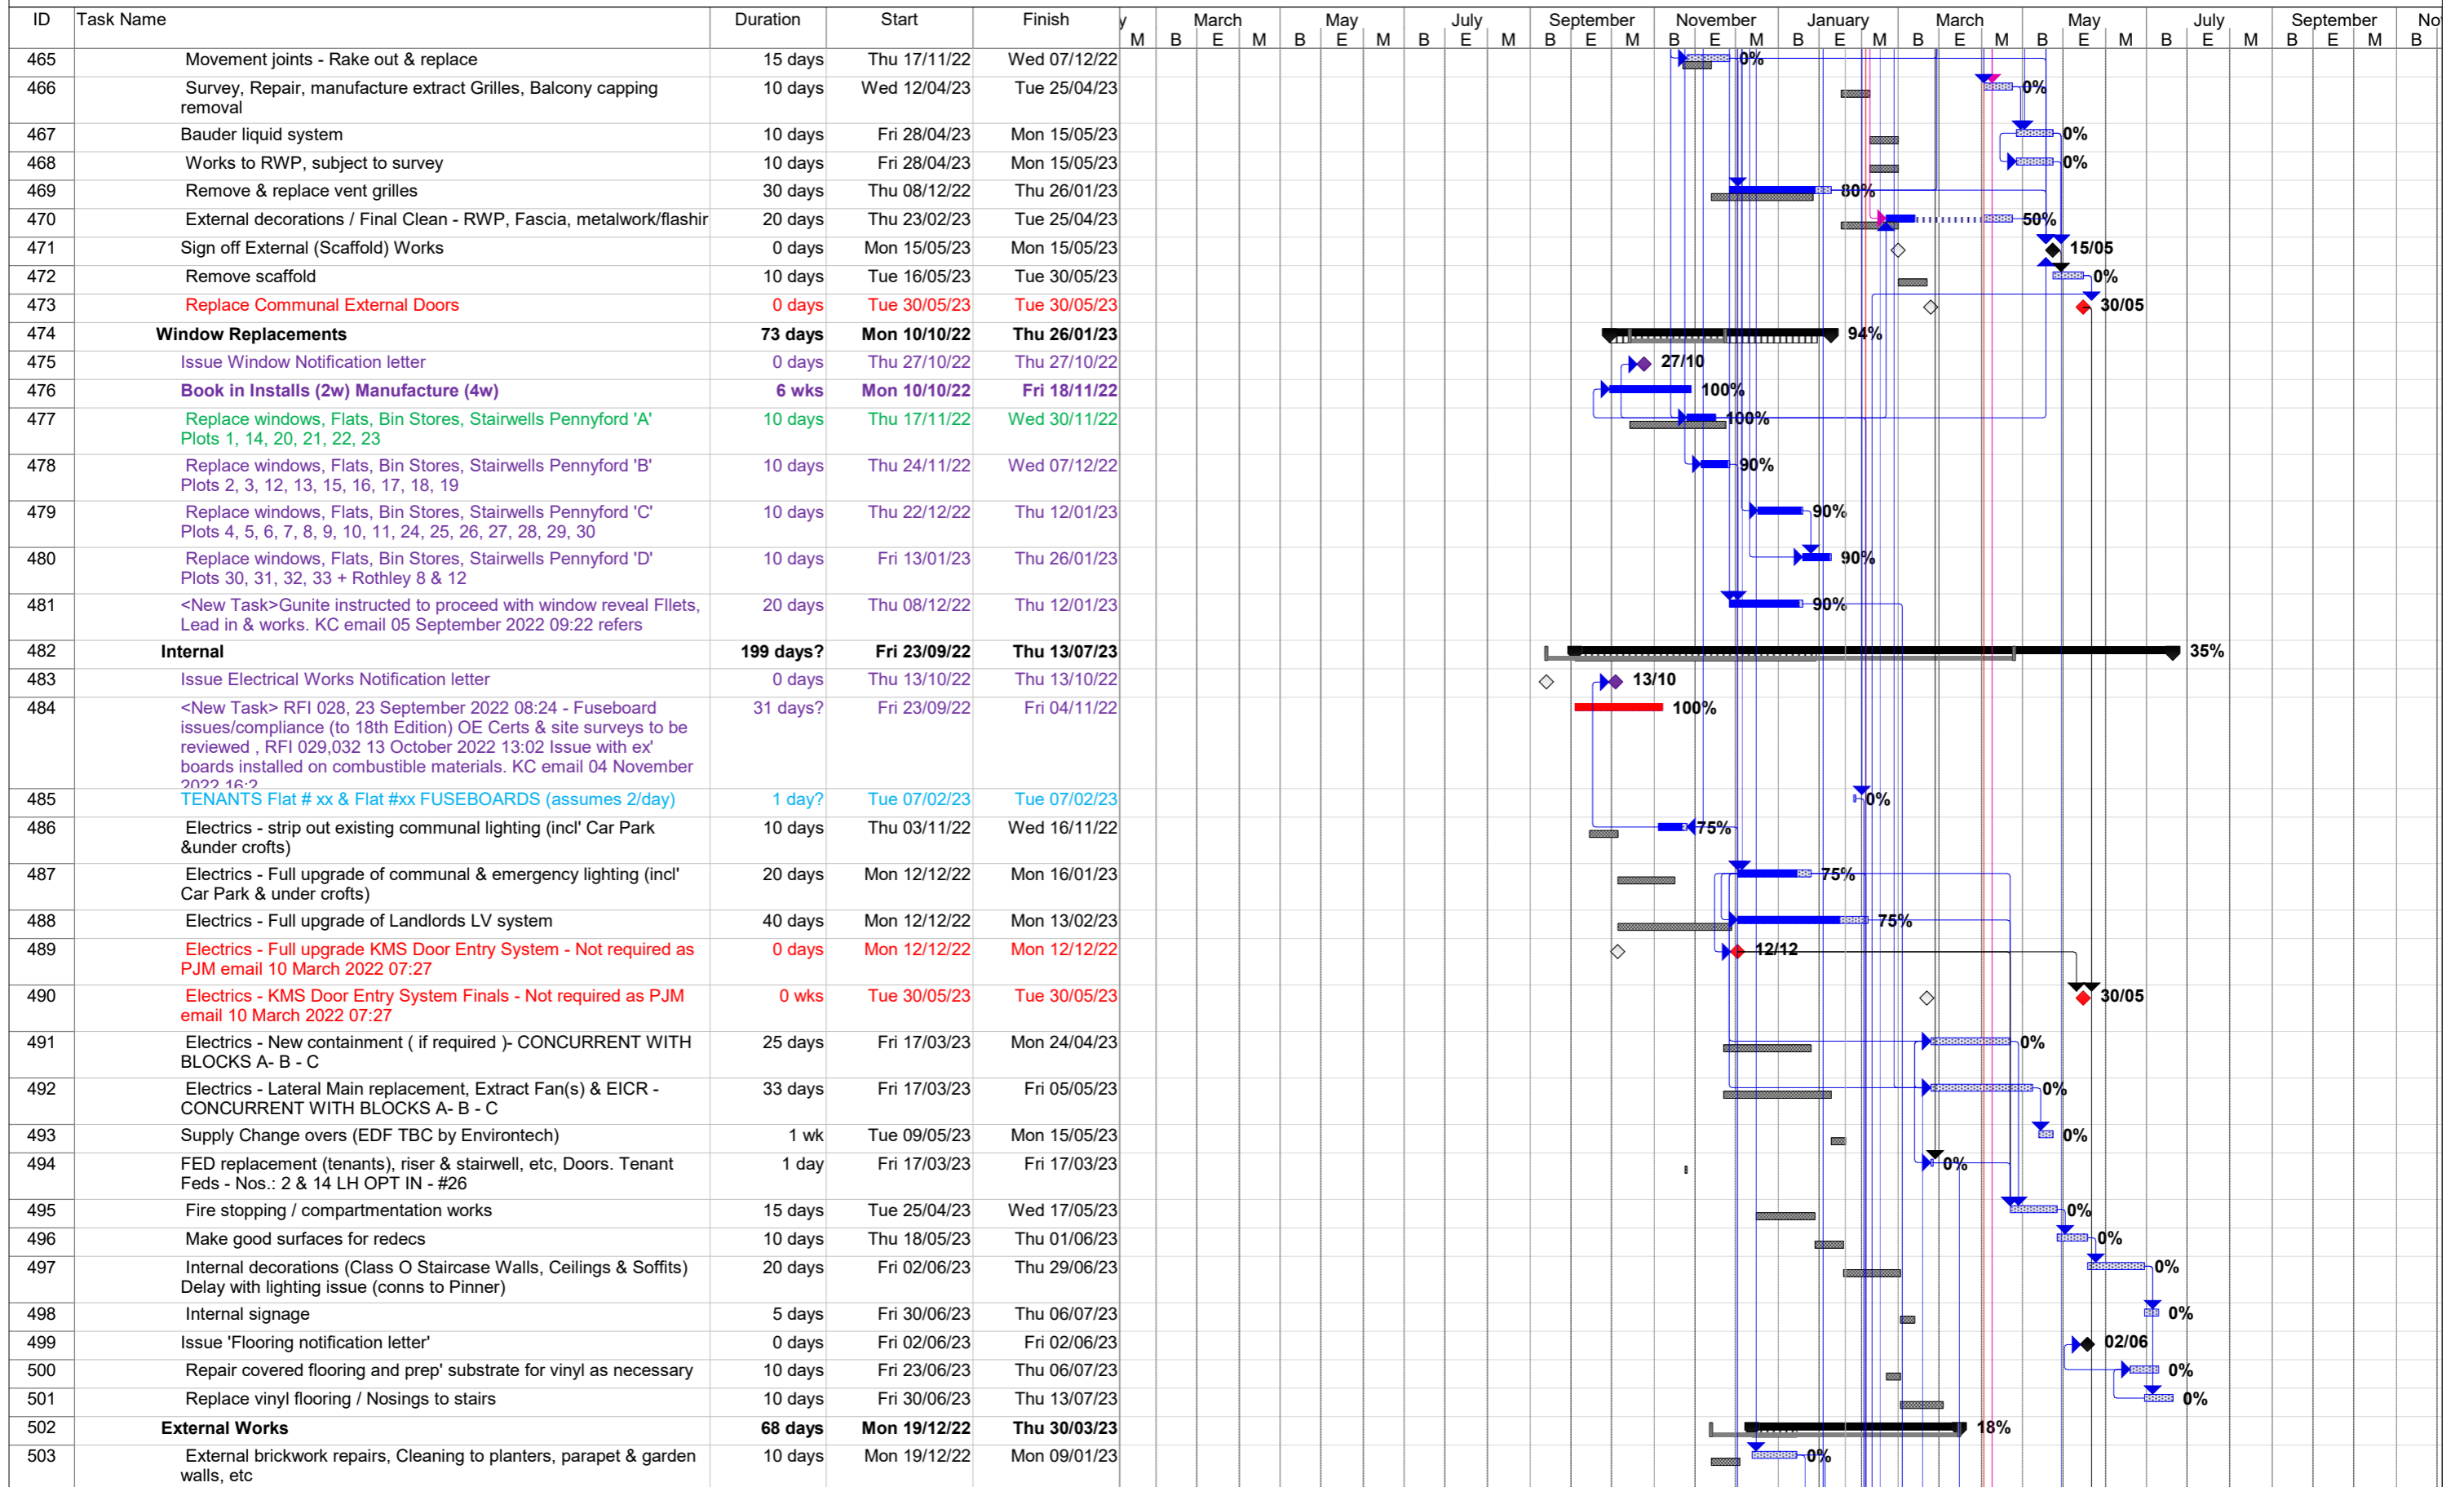



United Living 02692 - WHARNCLIFFE GARDENS - (AC103) Programme

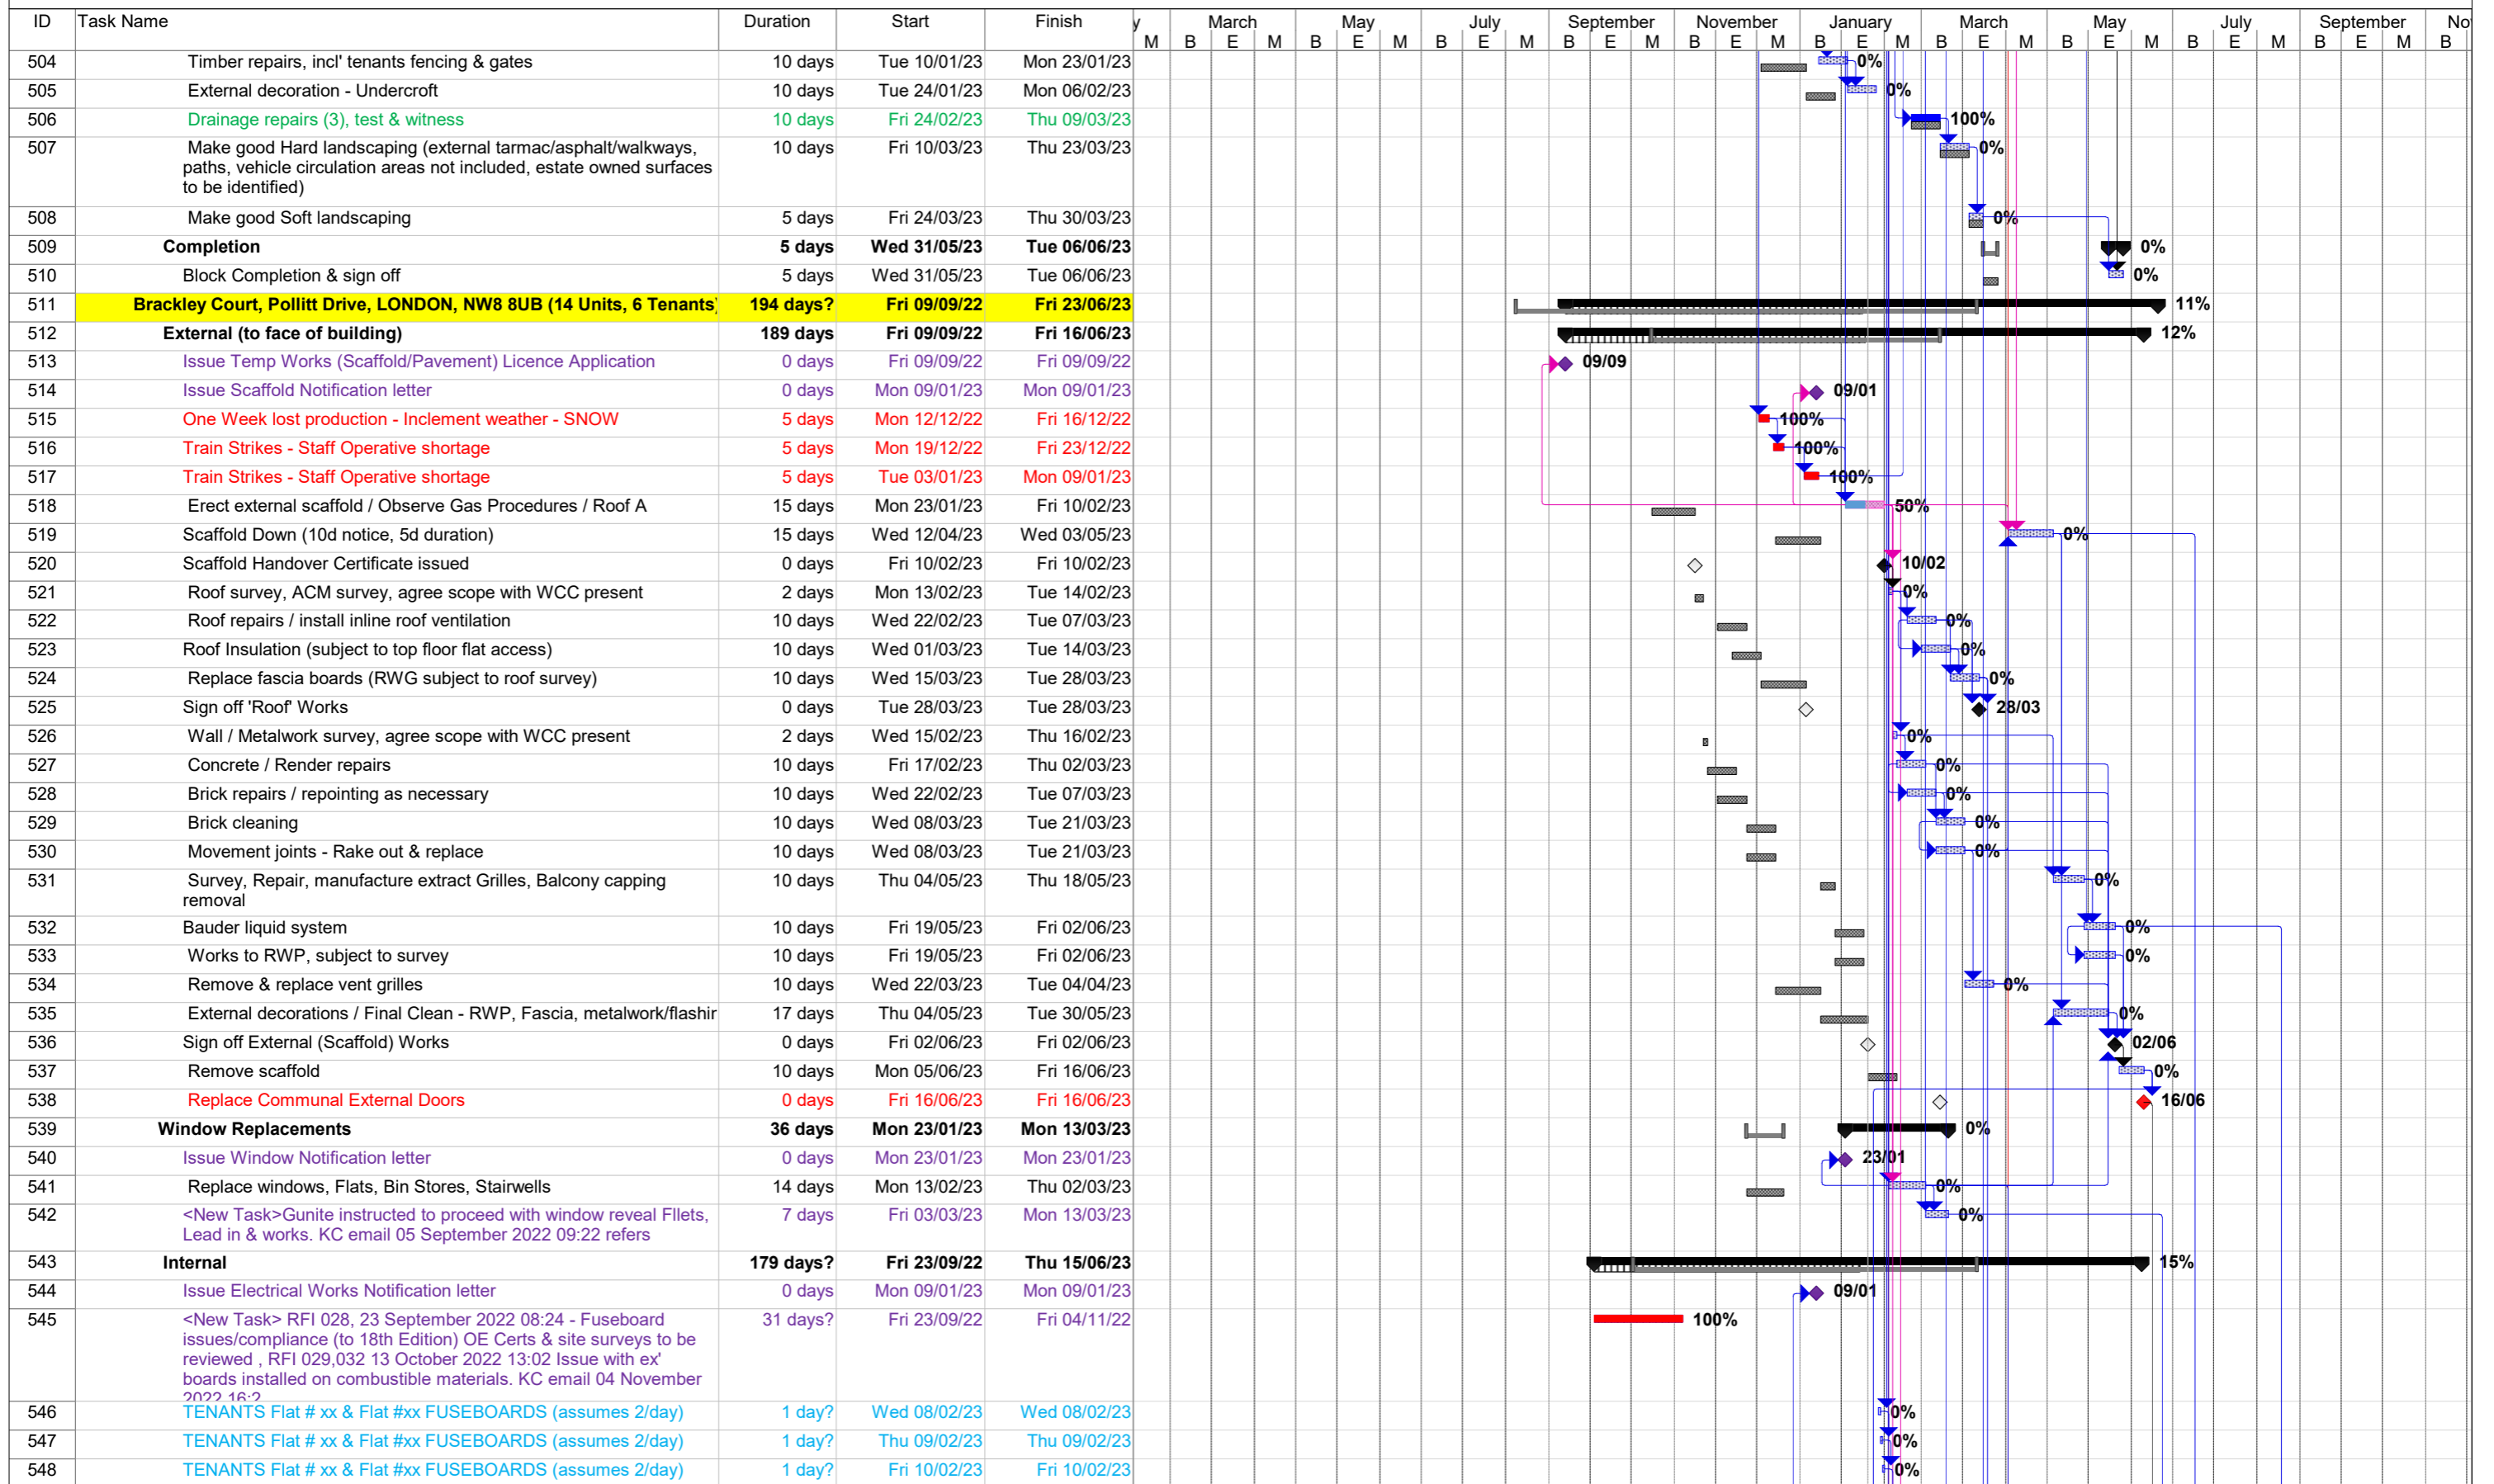

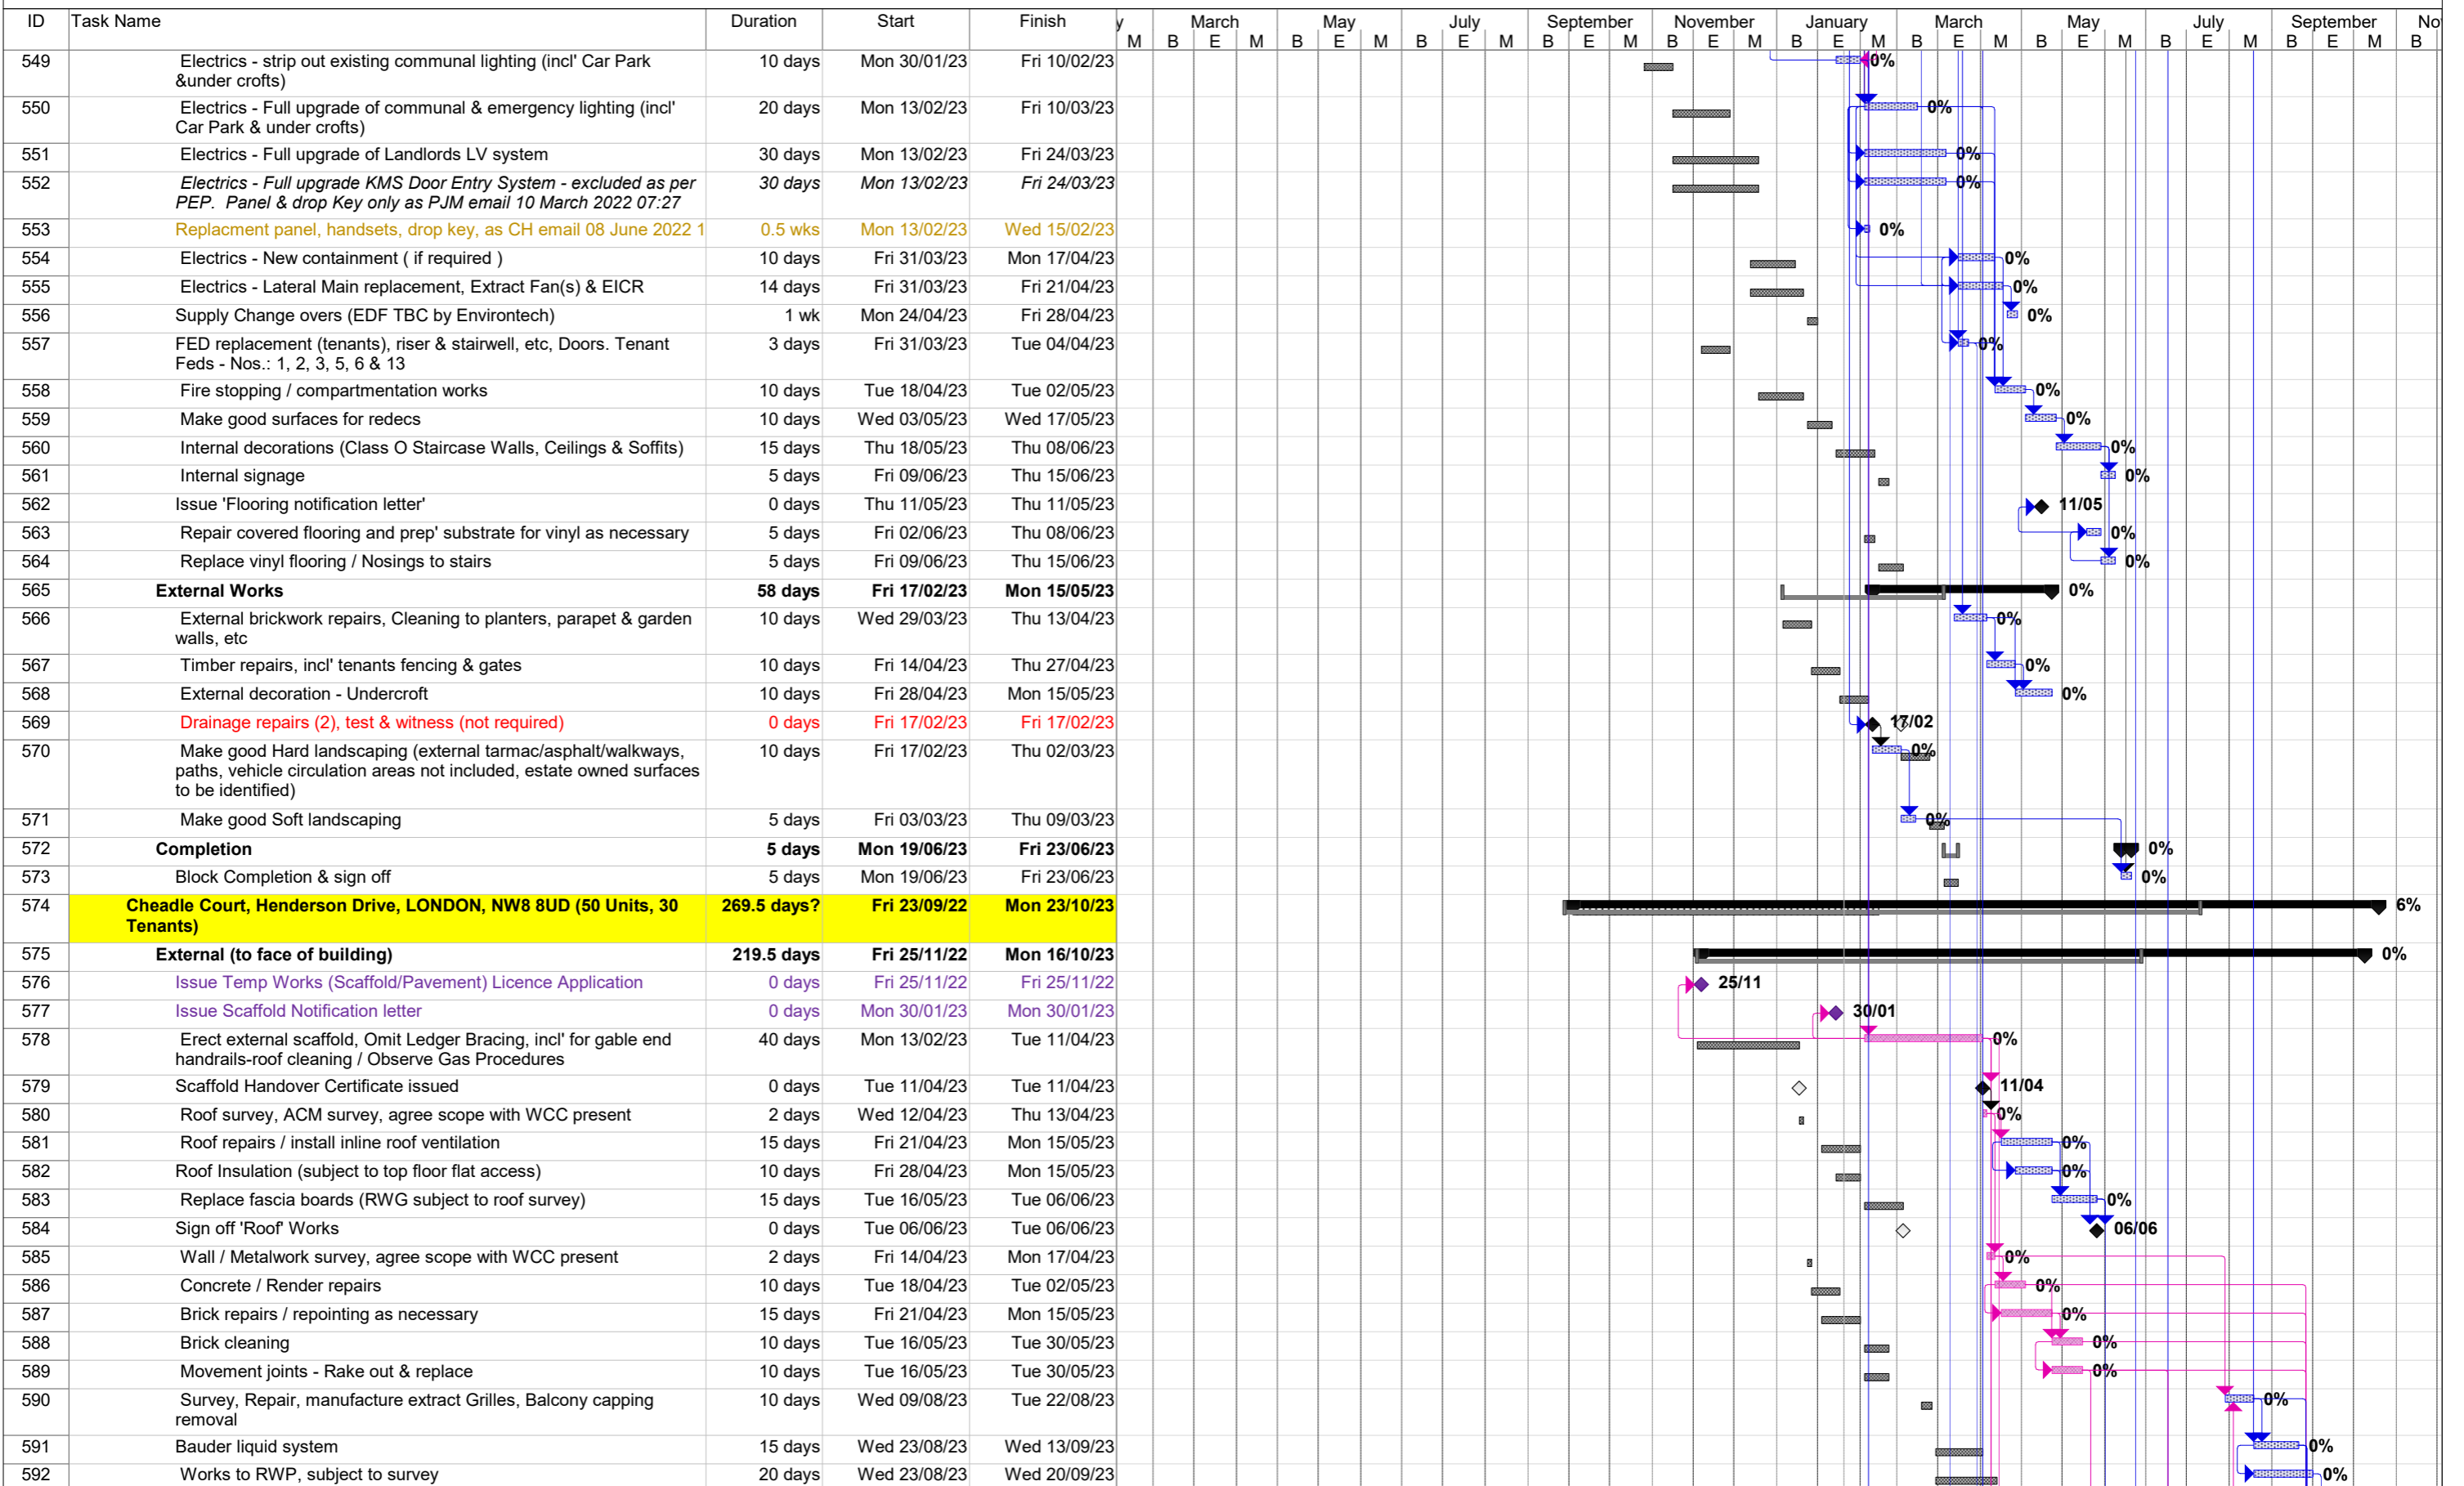

United Living 02692 - WHARNCLIFFE GARDENS - (AC103) Programme

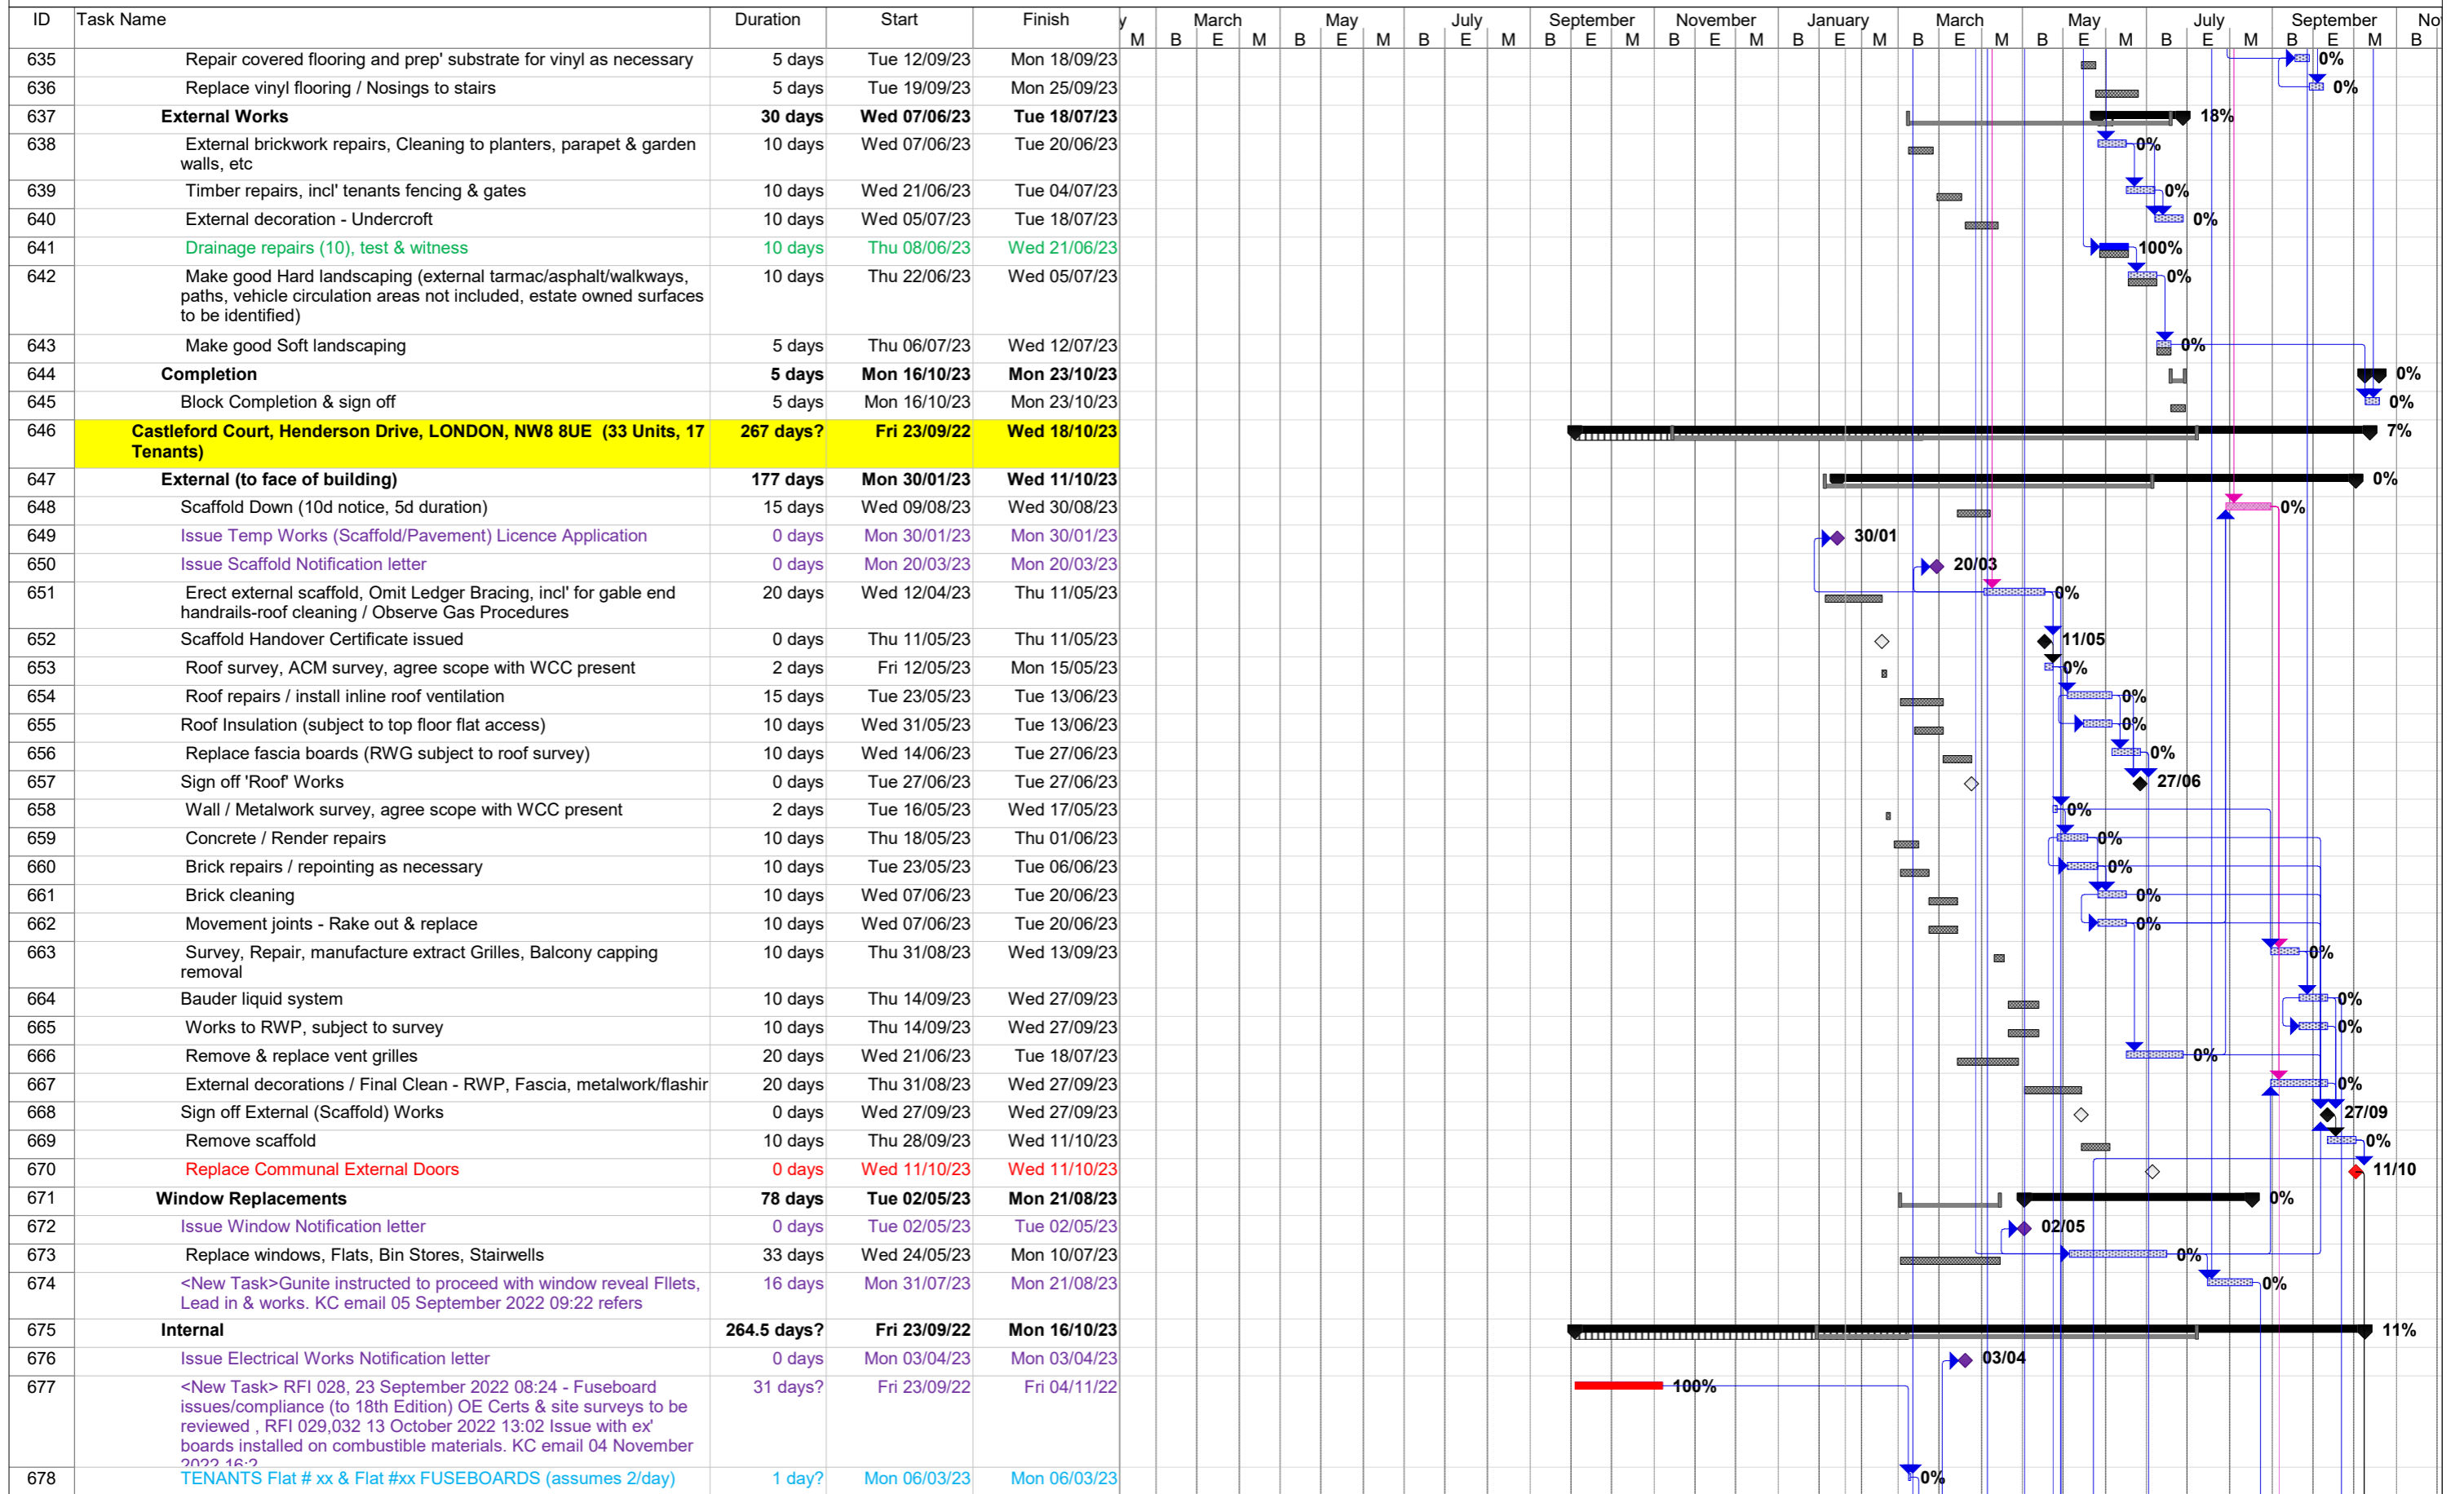

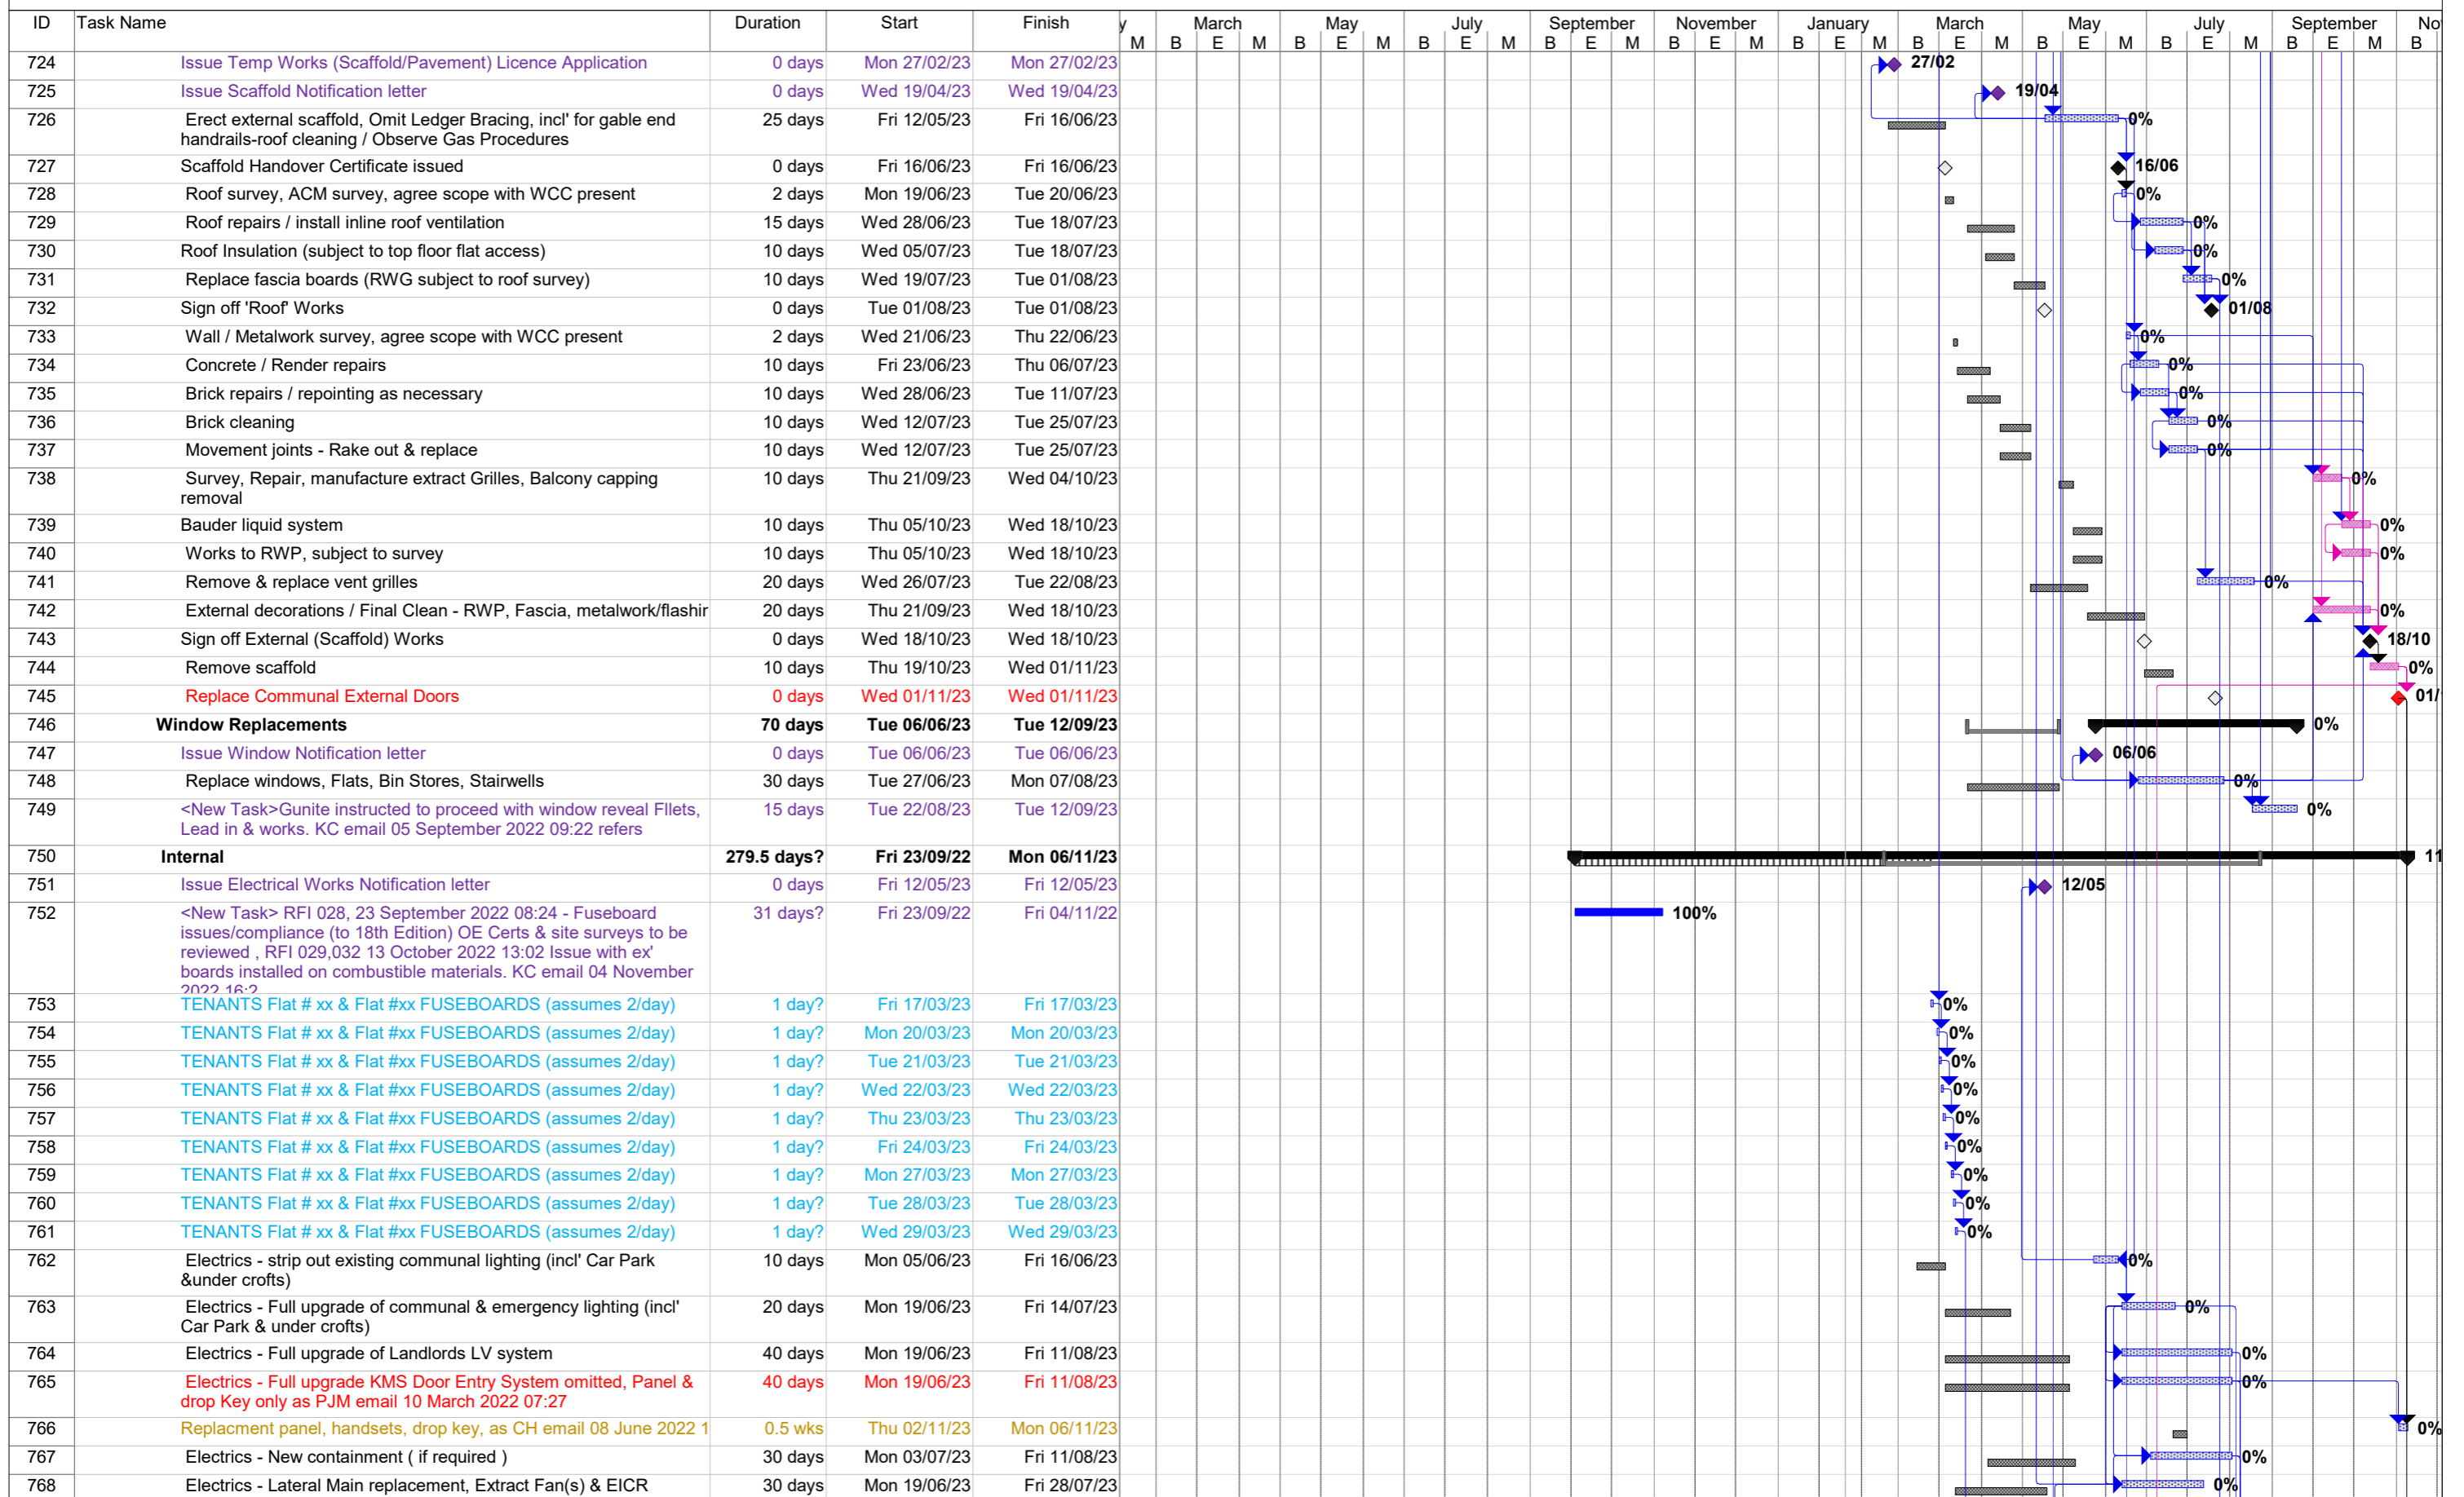

United Living

02692 - WHARNCLIFFE GARDENS - (AC103) Programme



ID	Task Name	Duration	Start	Finish	March		May		July		September		November		January		March		May		July		September		No	
					M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M
814	Issue Electrical Works Notification letter	0 days	Wed 12/04/23	Wed 12/04/23														12/04								
815	<New Task> RFI 028, 23 September 2022 08:24 - Fuseboard issues/compliance (to 18th Edition) OE Certs & site surveys to be reviewed , RFI 029,032 13 October 2022 13:02 Issue with ex' boards installed on combustible materials. KC email 04 November 2022 16:2	31 days?	Fri 23/09/22	Fri 04/11/22																						100%
816	TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/day)	1 day?	Thu 30/03/23	Thu 30/03/23															0%							
817	TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/day)	1 day?	Fri 31/03/23	Fri 31/03/23															0%							
818	TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/day)	1 day?	Mon 03/04/23	Mon 03/04/23															0%							
819	TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/day)	1 day?	Tue 04/04/23	Tue 04/04/23															0%							
820	TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/day)	1 day?	Wed 05/04/23	Wed 05/04/23															0%							
821	TENANTS Flat # xx & Flat #xx FUSEBOARDS (assumes 2/day)	1 day?	Thu 06/04/23	Thu 06/04/23															0%							
822	Electrics - strip out existing communal lighting	10 days	Thu 04/05/23	Thu 18/05/23																0%						
823	Electrics - Full upgrade of communal & emergency lighting (incl' Car Park & under crofts)	20 days	Fri 19/05/23	Fri 16/06/23																	0%					
824	Electrics - Full upgrade of Landlords LV system	30 days	Fri 19/05/23	Fri 30/06/23																		0%				
825	Electrics - Full upgrade KMS Door Entry System, Front & Rear doors, Panel & drop Key as PJM email 10 March 2022 07:27	30 days	Fri 19/05/23	Fri 30/06/23																			0%			
826	Replacment panel, handsets, drop key fobs, master controller with GPRS, locks changing. Replacement front & rear doors, as CH email 08 June 2022 13:19	0.5 wks	Thu 28/09/23	Mon 02/10/23																						0%
827	Electrics - New containment (if required)	20 days	Thu 25/05/23	Thu 22/06/23																			0%			
828	Laterals have been renewed recently (galv trunking) Main head's been double tapped, but incomplete. Old installation needs stripping to extend new metal trunking to above head, fit new switch & Rufford Panel	20 days	Thu 25/05/23	Thu 22/06/23																			0%			
829	Supply Change overs (EDF TBC by Environtech)	1 wk	Fri 23/06/23	Thu 29/06/23																				0%		
830	FED replacement (tenants), riser & stairwell, etc, Doors. Tenant Feds - Nos.: 1, 5 to 7, 9, 11, 13, 17, 18 & 21 to 23	6 days	Fri 26/05/23	Mon 05/06/23																					0%	
831	Fire stopping / compartmentation works	10 days	Mon 03/07/23	Fri 14/07/23																						
832	Make good surfaces for redecs	10 days	Mon 17/07/23	Fri 28/07/23																						
833	Internal decorations (Class O Staircase Walls, Ceilings & Soffits)	15 days	Mon 31/07/23	Fri 18/08/23																						
834	Internal signage	5 days	Mon 21/08/23	Fri 25/08/23																						
835	Issue 'Flooring notification letter'	0 days	Mon 24/07/23	Mon 24/07/23																						
836	Repair covered flooring and prep' substrate for vinyl as necessary	5 days	Mon 14/08/23	Fri 18/08/23																						
837	Replace vinyl flooring / Nosings to stairs	5 days	Mon 21/08/23	Fri 25/08/23																						
838	External Works	61 days	Wed 05/07/23	Thu 28/09/23																						0%
839	External brickwork repairs, Cleaning to planters, parapet & garden walls, etc	10 days	Wed 05/07/23	Tue 18/07/23																						
840	Timber repairs, incl' tenants fencing & gates	10 days	Wed 19/07/23	Tue 01/08/23																						
841	External decoration	10 days	Wed 02/08/23	Tue 15/08/23																						
842	Drainage repairs (5), test & witness	10 days	Thu 24/08/23	Thu 07/09/23																						
843	Make good Hard landscaping (external tarmac/asphalt/walkways, paths, vehicle circulation areas not included, estate owned surfaces to be identified)	10 days	Fri 08/09/23	Thu 21/09/23																						
844	Make good Soft landscaping	5 days	Fri 22/09/23	Thu 28/09/23																						0%
845	Completion	5 days	Fri 29/09/23	Thu 05/10/23																						0%
846	Block Completion & sign off	5 days	Fri 29/09/23	Thu 05/10/23																						0%
849	Fire Doors - Actual	45 days	Thu 02/02/23	Wed 05/04/23																						0%
850	1/38542B United Living CWH - Wharnclyffe Gardens - ELMTON /HUCKNALL 25no. Sets (as per attached sheet) Delivery per LR email 30 January 2023 15:54	0 days	Thu 02/02/23	Thu 02/02/23																						02/02
851	Install @ 4/day - RTT yet to confirm	6 days	Mon 06/02/23	Mon 13/02/23																						0%
852	1/38542C United Living CWH - Wharnclyffe Gardens - HELSBY / BIRCH VALE COURT 22no. Sets (as per attached sheet) Delivery per LR email 30 January 2023 15:54	0 days	Thu 09/02/23	Thu 09/02/23																						09/02
853	Install @ 4/day - RTT yet to confirm	6 days	Tue 14/02/23	Tue 21/02/23																						0%

