












































ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
1			Wharncliffe - Exit programme	Mon 09/01/23	Tue 23/01/24			63%				
2			Birchvale	Mon 09/01/23	Mon 16/10/23			76%				
3			Scaffolding	Mon 09/01/23	Wed 01/02/23			100%				
4			Asbestos	Wed 08/02/23	Wed 01/03/23	3FS+5 days		100%				
5			Window replacements	Wed 19/04/23	Wed 30/08/23	4FS+35 days		90%				
6			Lateral mains	Wed 10/05/23	Wed 27/09/23	5SS+15 days		50%				
7			Communal lighting	Wed 24/05/23	Wed 02/08/23	6SS+10 days		100%				
8			Masonry repairs	Wed 03/05/23	Wed 28/06/23	5SS+10 days		100%				
9			Roof repairs	Fri 03/03/23	Fri 24/03/23	4FS+2 days		100%				
10			external decs	Fri 10/03/23	Fri 21/04/23	9SS+5 days		100%				
11			Internal decs	Fri 21/04/23	Fri 19/05/23	10		100%				
12			Communal flooring	Mon 28/08/23	Mon 11/09/23	11FS+71 days		0%				
13			FRA Works	Mon 18/09/23	Mon 16/10/23	12FS+5 days		0%				























Project: Wharncliffe exit progra
Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
14			Strike Scaffolding	Wed 06/09/2	Wed 20/09/23	5FS+5 days		0%				
15			Rothley Court	Mon 09/01/2	Fri 24/11/23			76%				
16			Scaffolding	Mon 09/01/2	Wed 01/02/23			100%				
17			Asbestos	Wed 15/02/2	Wed 08/03/23	16FS+10 days		100%				
18			Window replacements	Wed 26/04/2	Wed 06/09/23	17FS+35 days		90%				
19			Lateral mains	Wed 17/05/2	Wed 04/10/23	18SS+15 days		40%				
20			Communal lighting	Wed 31/05/2	Wed 09/08/23	19SS+10 days		100%				
21			Masonry repairs	Wed 31/05/2	Wed 26/07/23	19SS+10 days		100%				
22			Roof repairs	Fri 10/03/23	Fri 31/03/23	17FS+2 days		100%				
23			external decs	Fri 17/03/23	Fri 28/04/23	22SS+5 days		100%				
24			Internal decs	Fri 28/04/23	Fri 26/05/23	23		100%				
25			Communal flooring	Fri 06/10/23	Fri 20/10/23	24FS+19 wks		0%				
26			FRA Works	Fri 27/10/23	Fri 24/11/23	25FS+5 days		0%				
27			Strike Scaffolding	Wed 13/09/2	Wed 27/09/23	18FS+5 days		60%				



















Project: Wharncliffe exit progra
Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
28			Pennyford court	Wed 01/02/23	Fri 08/12/23			74%				
29			Scaffolding	Wed 01/02/23	Fri 24/02/23	16		100%				
30			Asbestos	Mon 06/03/23	Fri 24/03/23	29FS+5 days		100%				
31			Window replacements	Mon 17/04/23	Fri 25/08/23	30FS+15 days		90%				
32			Lateral mains	Mon 17/04/23	Fri 29/09/23	31SS		40%				
33			Communal lighting	Mon 24/04/23	Fri 30/06/23	30SS+35 days		100%				
34			Masonry repairs	Mon 08/05/23	Fri 30/06/23	33SS+10 days		100%				
35			Roof repairs	Fri 03/03/23	Fri 24/03/23	4FS+2 days		100%				
36			external decs	Fri 10/03/23	Fri 21/04/23	35SS+5 days		100%				
37			Internal decs	Fri 21/04/23	Fri 19/05/23	10		100%				
38			Communal flooring	Mon 23/10/23	Mon 06/11/23	25FS+1 day		0%				
39			FRA Works	Fri 10/11/23	Fri 08/12/23	26SS+10 days		0%				
40			Strike Scaffolding	Mon 02/10/23	Mon 02/10/23	32		60%				
41			Brackley Court	Mon 27/02/23	Fri 15/12/23			87%				



















Project: Wharncliffe exit progra
Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




















ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
42			Scaffolding	Mon 27/02/2	Wed 22/03/23	29		100%				
43			Asbestos	Wed 22/03/2	Wed 12/04/23	42		100%				
44			Window replacements	Wed 26/04/2	Wed 06/09/23	43FS+10 days		90%				
45			Lateral mains	Wed 12/04/2	Wed 16/08/23	43		100%				
46			Communal lighting	Wed 12/04/2	Wed 21/06/23	45SS		100%				
47			Masonry repairs	Wed 24/05/2	Wed 19/07/23	44SS+20 days		95%				
48			Roof repairs	Wed 12/04/2	Wed 03/05/23	43		90%				
49			external decs	Wed 12/04/2	Wed 24/05/23	43		100%				
50			Internal decs	Wed 12/04/2	Wed 10/05/23	43		100%				
51			Communal flooring	Mon 06/11/2	Mon 20/11/23	38		0%				
52			FRA Works	Fri 17/11/23	Fri 15/12/23	39SS+5 days		0%				
53			Strike Scaffolding	Tue 03/10/23	Mon 16/10/23	40		0%				
54			Cheadle Court	Wed 22/03/2	Thu 04/01/24			67%				
55			Scaffolding	Wed 22/03/2	Fri 14/04/23	42		100%				

Project: Wharncliffe exit progra
Date: Tue 15/08/23
















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
56			Asbestos	Mon 17/04/2	Fri 05/05/23	55		100%				
57			Window replacements	Mon 15/05/2	Fri 22/09/23	56FS+5 days		80%				
58			Lateral mains	Mon 08/05/2	Fri 08/09/23	56		100%				
59			Communal lighting	Mon 08/05/2	Fri 14/07/23	58SS		100%				
60			Masonry repairs	Mon 26/06/2	Fri 18/08/23	57SS+30 days		60%				
61			Roof repairs	Mon 28/08/2	Fri 15/09/23	60FS+5 days		0%				
62			external decs	Mon 18/09/2	Fri 20/10/23	61		0%				
63			Internal decs	Mon 09/10/2	Fri 03/11/23	62SS+15 days		0%				
64			Communal flooring	Mon 06/11/2	Fri 17/11/23	63		0%				
65			FRA Works	Fri 24/11/23	Thu 04/01/24	52SS+5 days		0%				
66			Strike Scaffolding	Wed 25/10/2	Tue 07/11/23	62FS+2 days		0%				
67			Castleford Court	Mon 07/08/2	Thu 04/01/24			2%				
68			Scaffolding	Mon 07/08/2	Wed 30/08/23	55FS+16 wks		25%				
69			External surveys	Wed 30/08/2	Wed 20/09/23	68		0%				




















Project: Wharncliffe exit progra
Date: Tue 15/08/23














Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Tue 15/08/23 Rev1




















ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
70			Asbestos	Wed 30/08/2	Wed 20/09/23	68		0%				
71			Window replacements	Wed 06/09/2	Wed 11/10/23	70SS+5 days		0%				
72			Lateral mains	Wed 06/09/2	Wed 11/10/23	70SS+5 days		0%				
73			Communal lighting	Wed 06/09/2	Wed 04/10/23	70SS+5 days		0%				
74			Masonry repairs	Wed 20/09/2	Wed 25/10/23	69		0%				
75			Roof repairs	Wed 30/08/2	Wed 20/09/23	70SS		0%				
76			external decs	Wed 04/10/2	Wed 08/11/23	74SS+10 days		0%				
77			Internal decs	Wed 30/08/2	Wed 27/09/23	70SS		0%				
78			Communal flooring	Mon 06/11/2	Fri 17/11/23	64SS		0%				
79			FRA Works	Fri 24/11/23	Thu 04/01/24	65SS		0%				
80			Strike Scaffolding	Wed 08/11/2	Wed 22/11/23	76		0%				
81			Ashby Court	Wed 30/08/2	Thu 11/01/24			0%				
82			Scaffolding	Wed 30/08/2	Wed 20/09/23	68		0%				
83			External surveys	Wed 20/09/2	Wed 11/10/23	82		0%				

Project: Wharncliffe exit progra
Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Start	Finish	Predecessors	Resource Names	% Complete	07	09	11	13
84			Asbestos	Wed 20/09/2	Wed 04/10/23	82		0%				
85			Window replacements	Wed 04/10/2	Wed 08/11/23	84		0%				
86			Lateral mains	Wed 27/09/2	Wed 01/11/23	84SS+5 days		0%				
87			Communal lighting	Wed 27/09/2	Wed 18/10/23	84SS+5 days		0%				
88			Masonry repairs	Wed 11/10/2	Wed 08/11/23	83		0%				
89			Roof repairs	Wed 27/09/2	Wed 11/10/23	84SS+5 days		0%				
90			external decs	Wed 25/10/2	Wed 22/11/23	88SS+10 days		0%				
91			Internal decs	Wed 25/10/2	Wed 08/11/23	88SS+10 days		0%				
92			Communal flooring	Mon 20/11/2	Fri 24/11/23	78		0%				
93			FRA Works	Fri 01/12/23	Thu 11/01/24	79SS+5 days		0%				
94			Strike Scaffolding	Mon 27/11/2	Mon 11/12/23	90FS+3 days		0%				
95			Winchelsea House	Wed 20/09/2	Tue 23/01/24	82		0%				







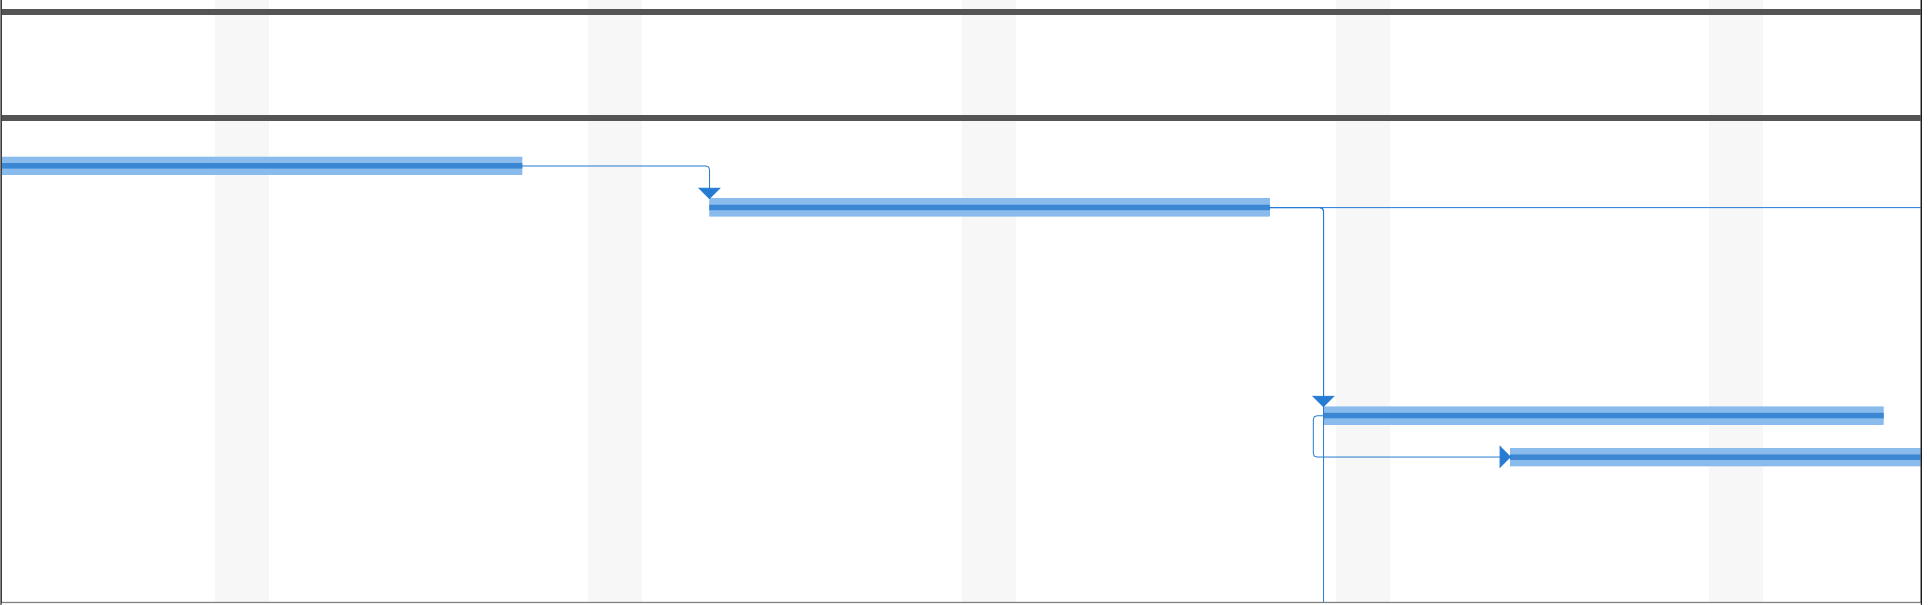












Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | 31 | February 2023 | 02 | 04 | 06 | 08 | 10 | 12 | 14 | 16 | 18 | 20 | 22 | 24 | 26 | 28 | March 2023 | 02 | 04 | 06 | 08 | 10 | 12 | 14 | 16 | 18 | 20 | 22 | 24







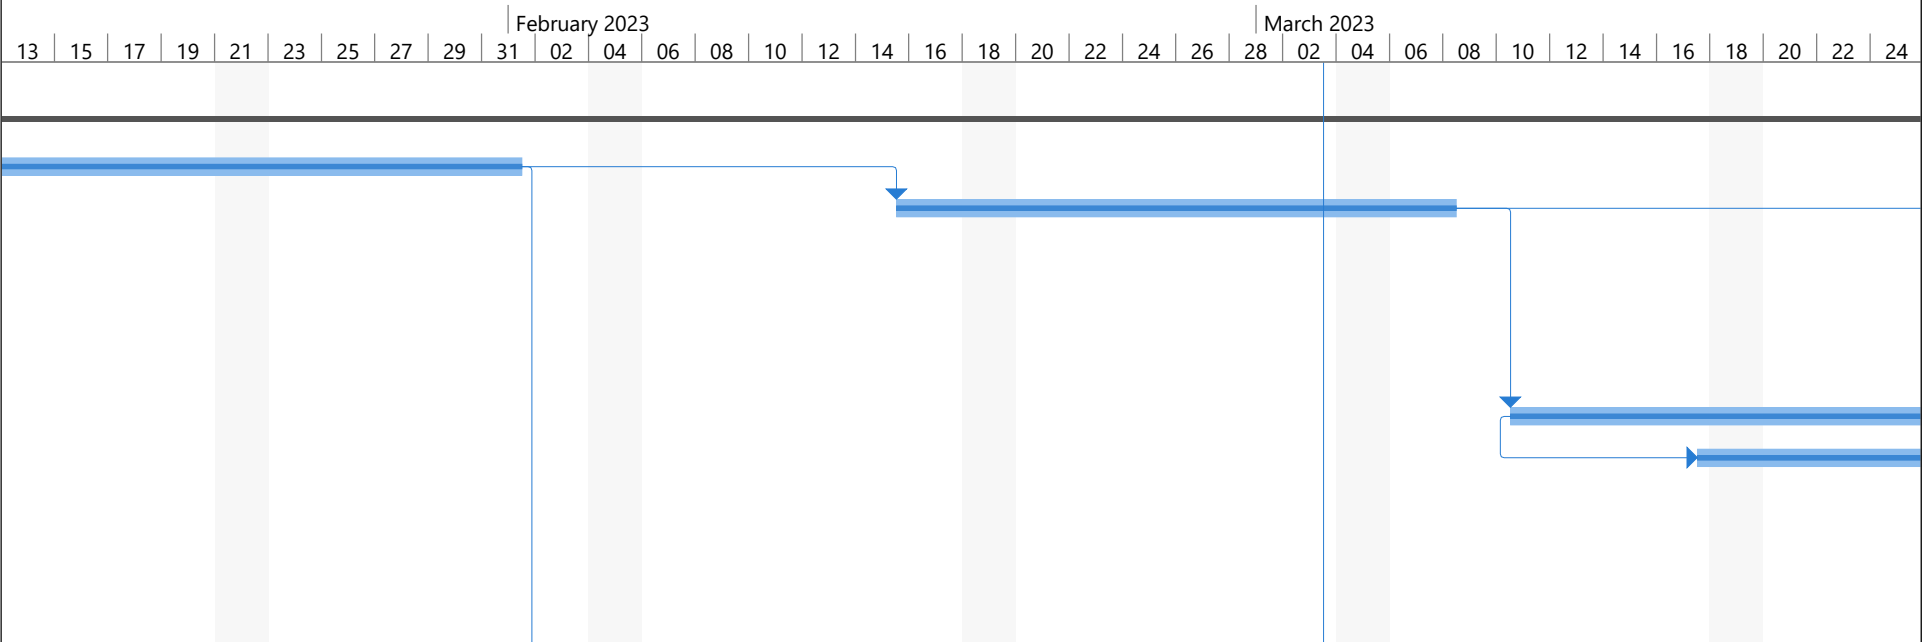














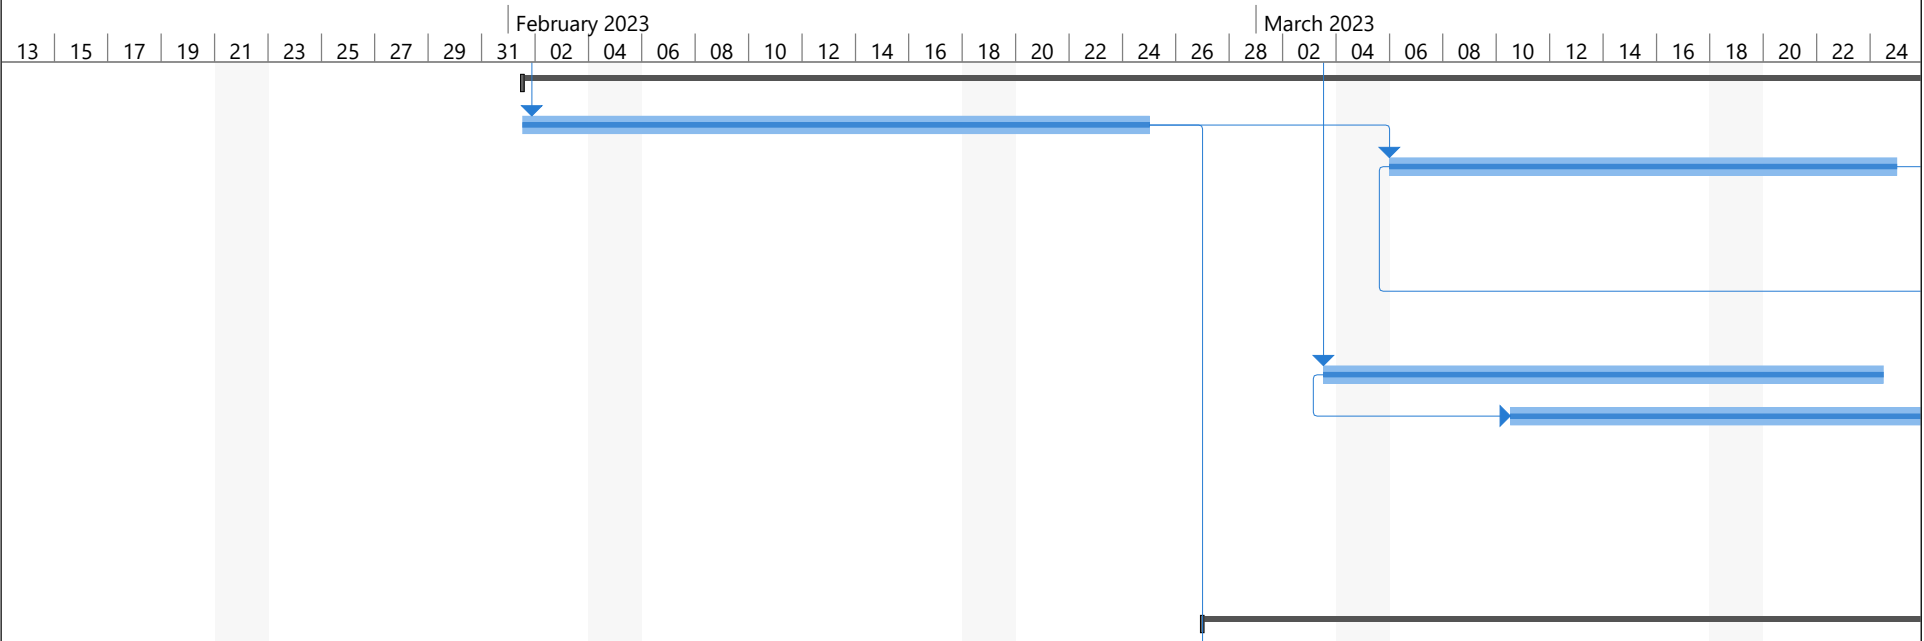
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			























Project: Wharncliffe exit progra
 Date: Tue 15/08/23




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Wharncliffe exit progra
 Date: Tue 15/08/23




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Wharncliffe exit progra Date: Tue 15/08/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			









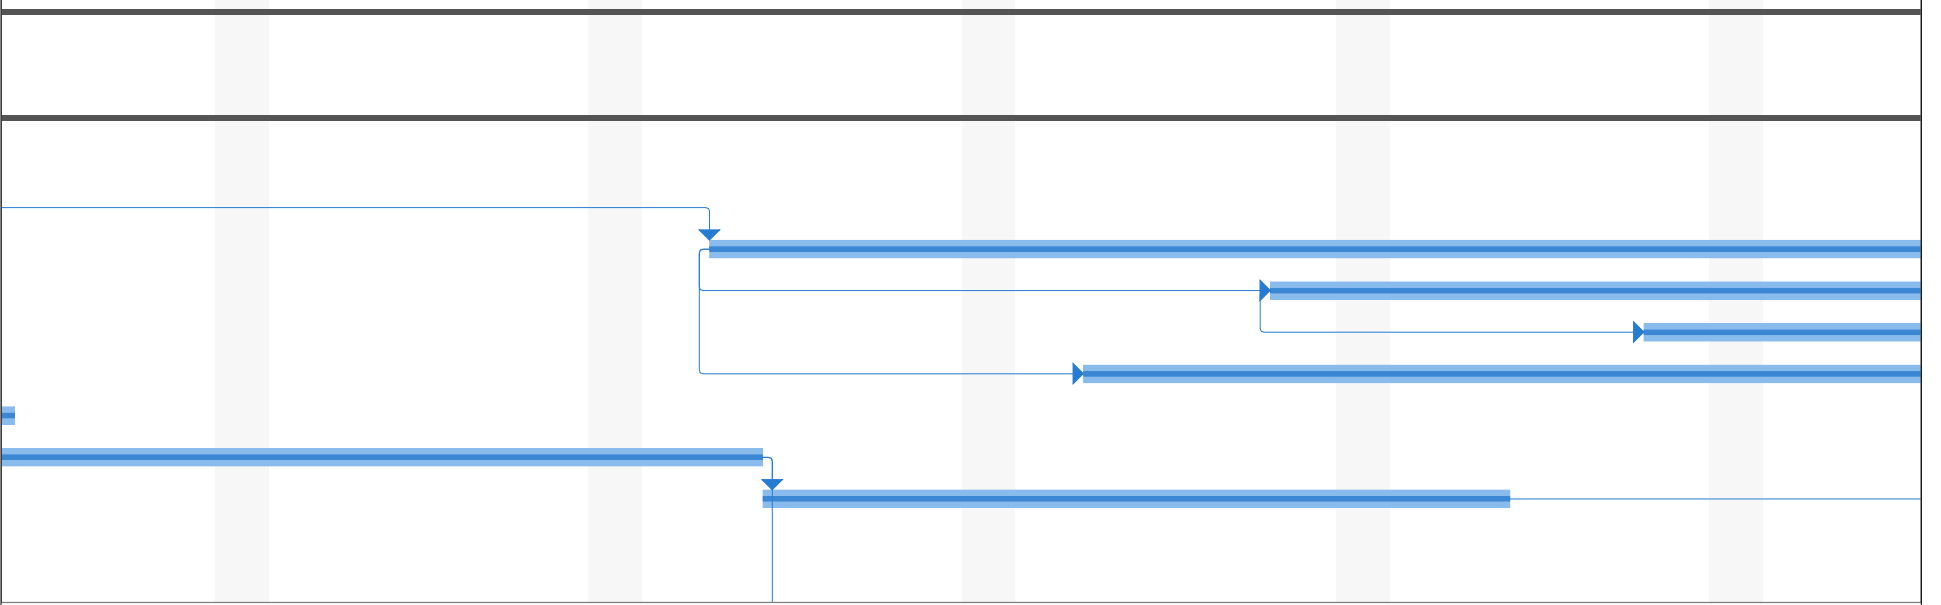












Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

24 | 26 | 28 | 30 | April 2023 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | May 2023 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | June 2023 | 01 | 02







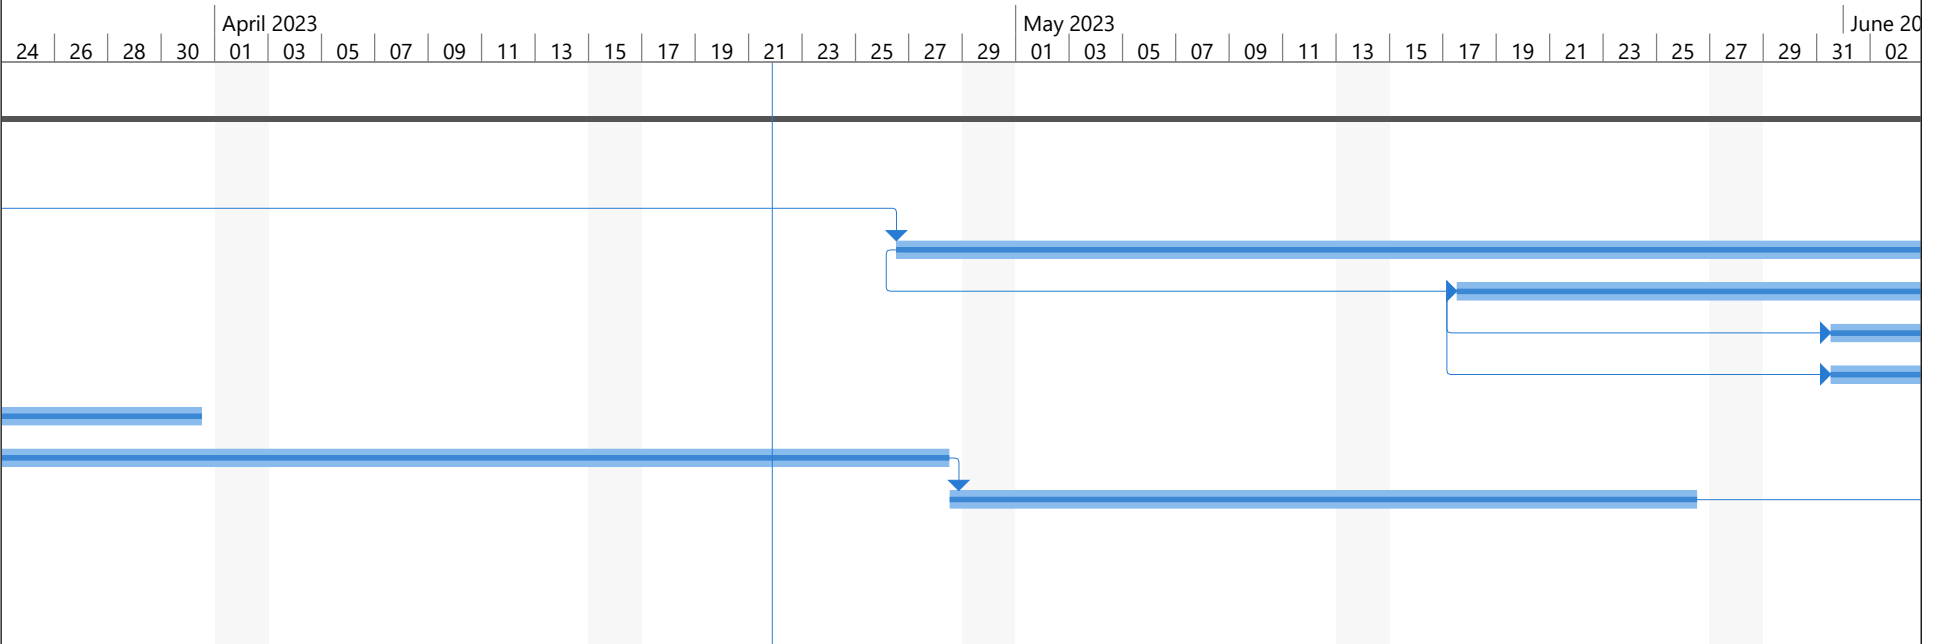














Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			










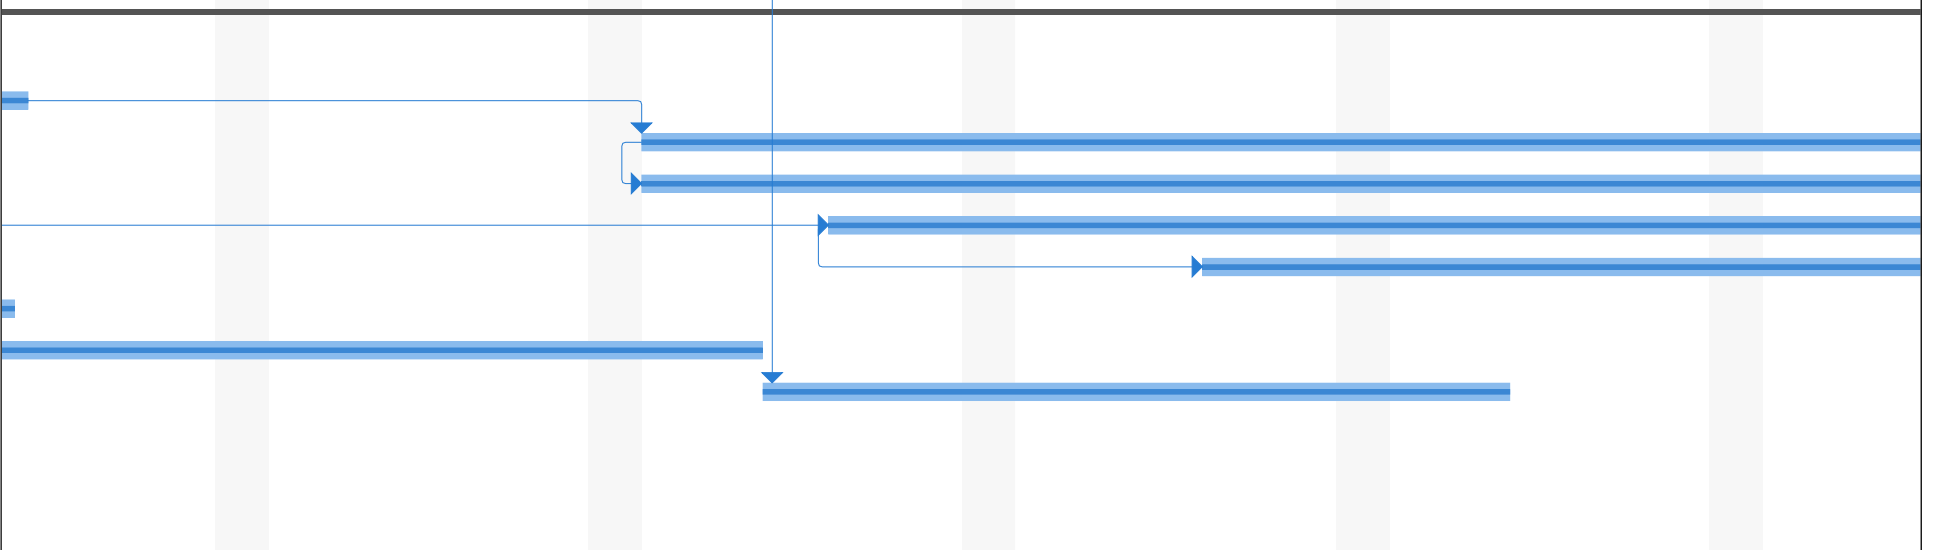











Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

24 | 26 | 28 | 30 | April 2023 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | May 2023 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | 31 | 02 | June 2023







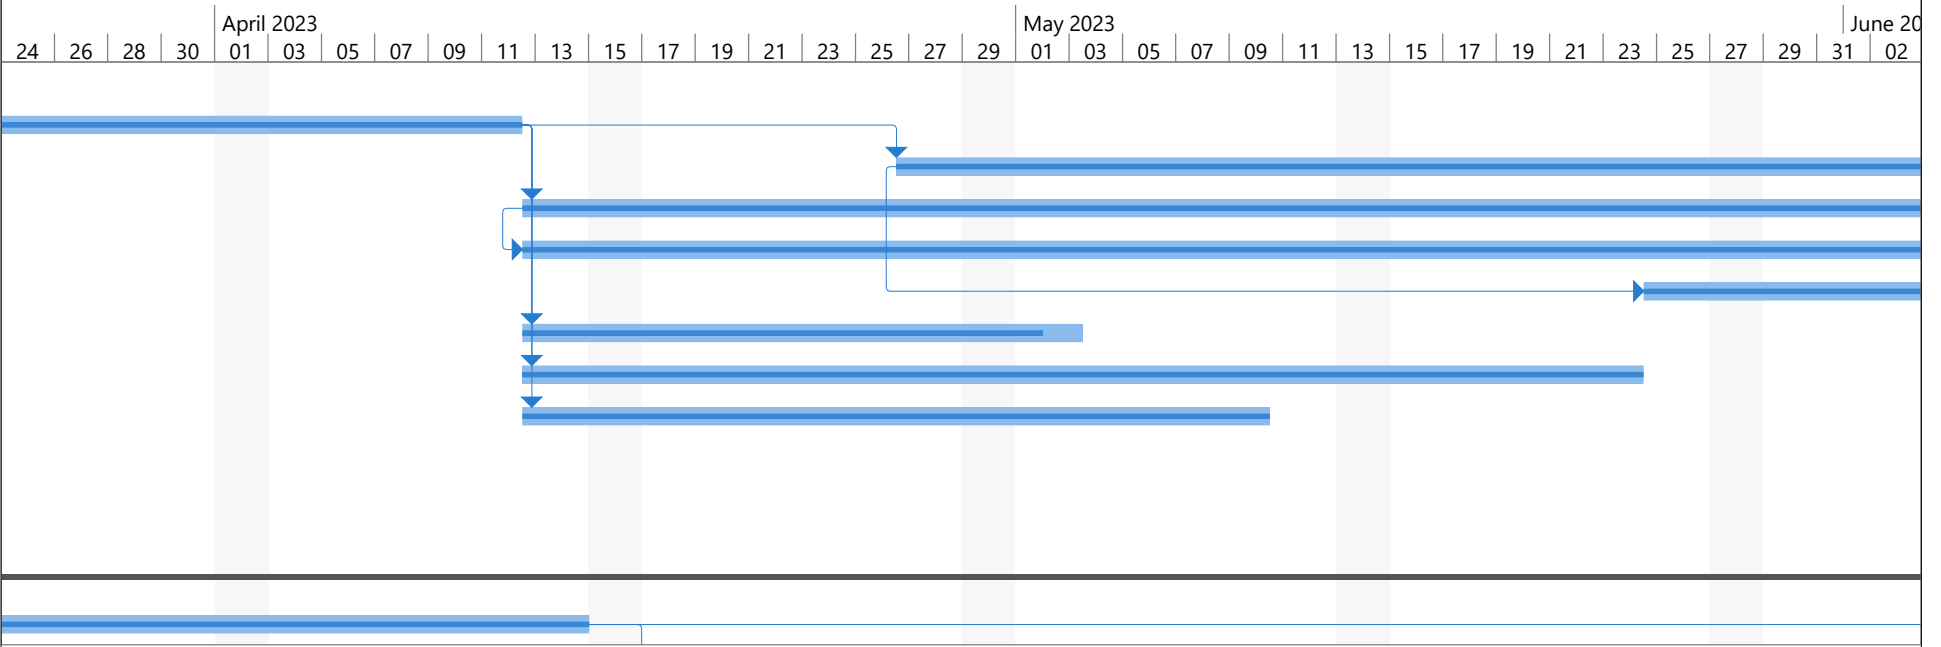














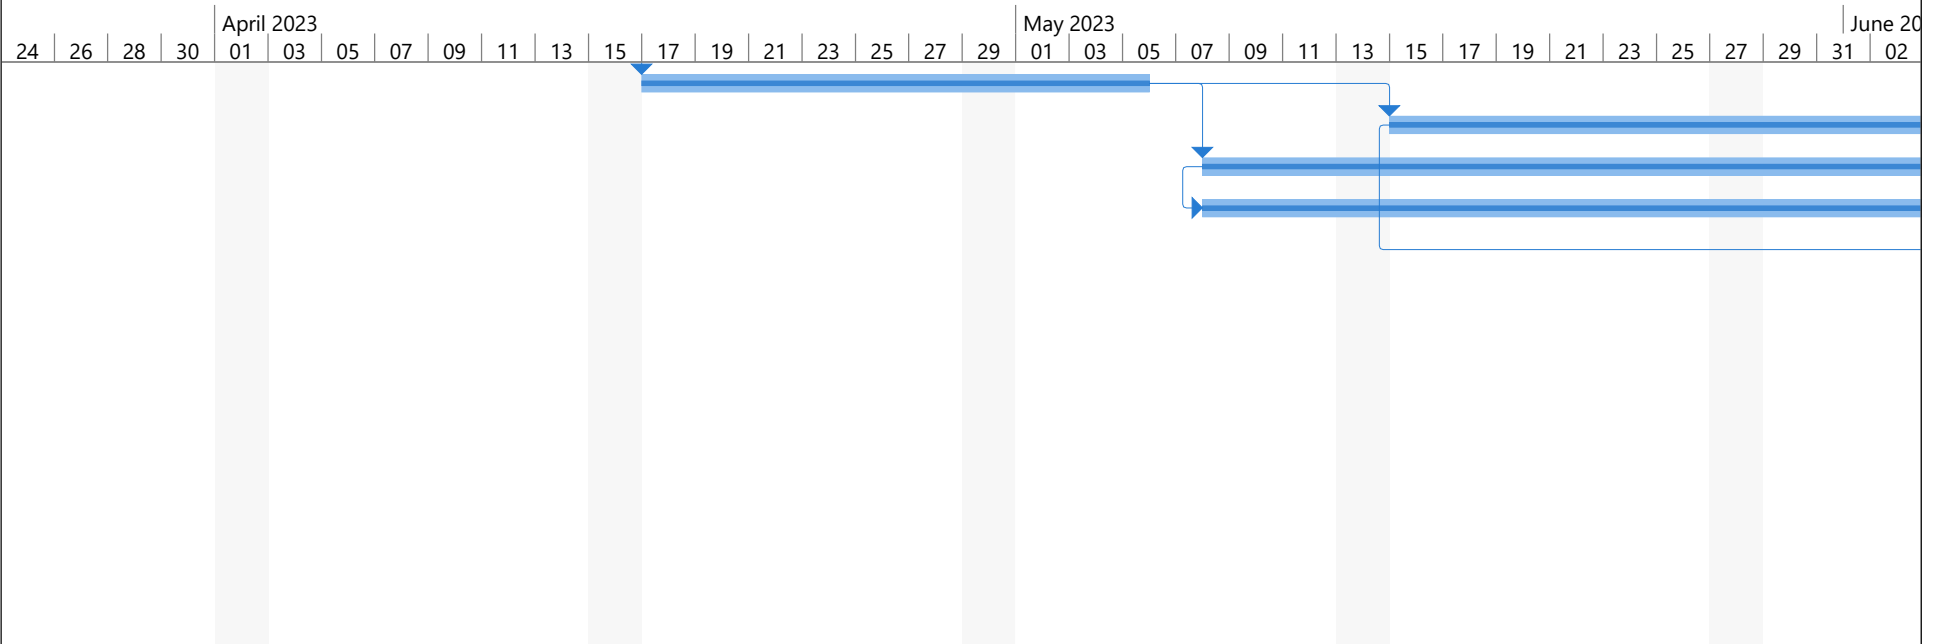
Project: Wharncliffe exit progra
 Date: Tue 15/08/23




















Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			























Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra Date: Tue 15/08/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			




Project: Wharncliffe exit progra Date: Tue 15/08/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			







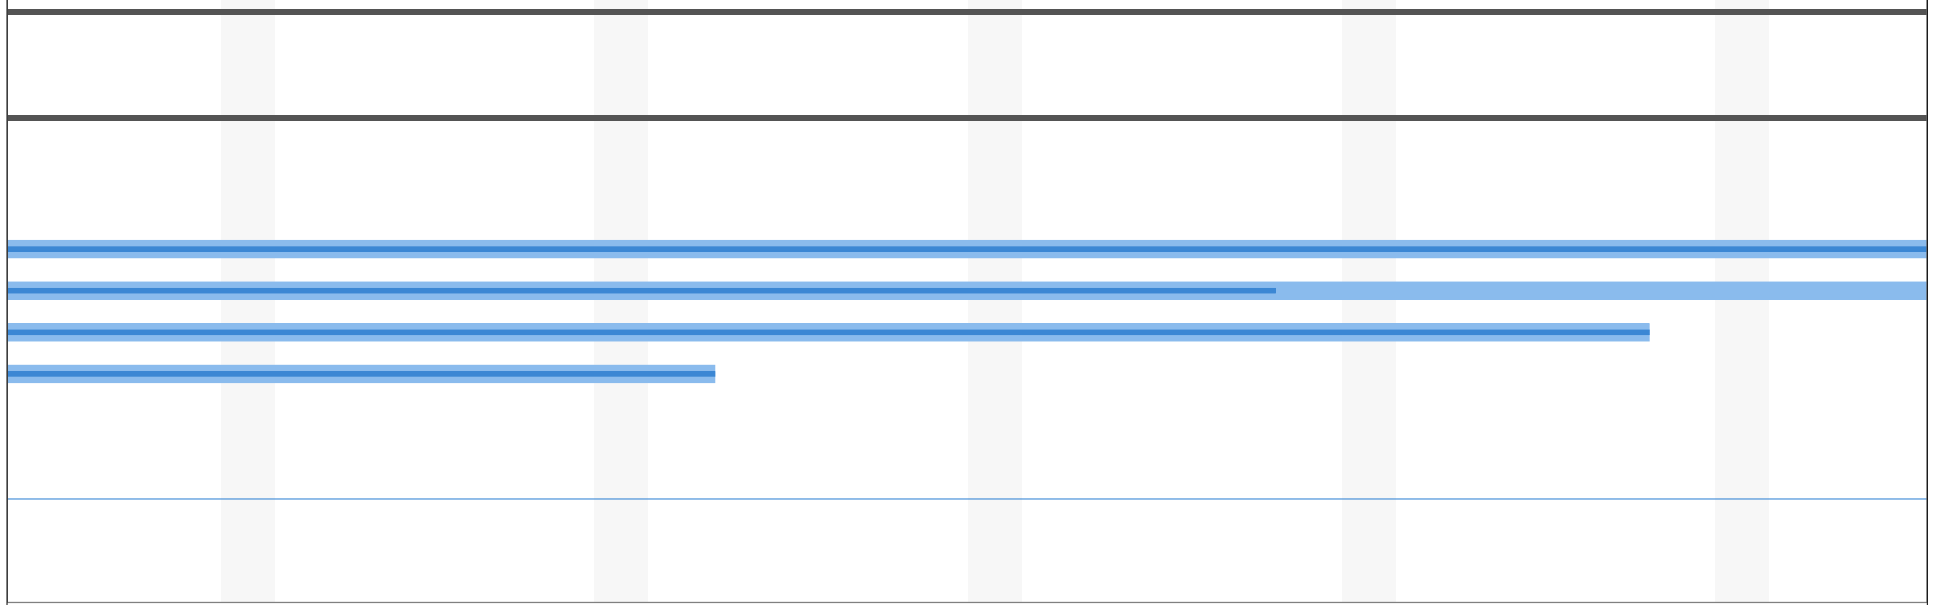














Project: Wharncliffe exit progra Date: Tue 15/08/23	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


June 2023 | July 2023 | August 2023
 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 01 03 05 07 09 11









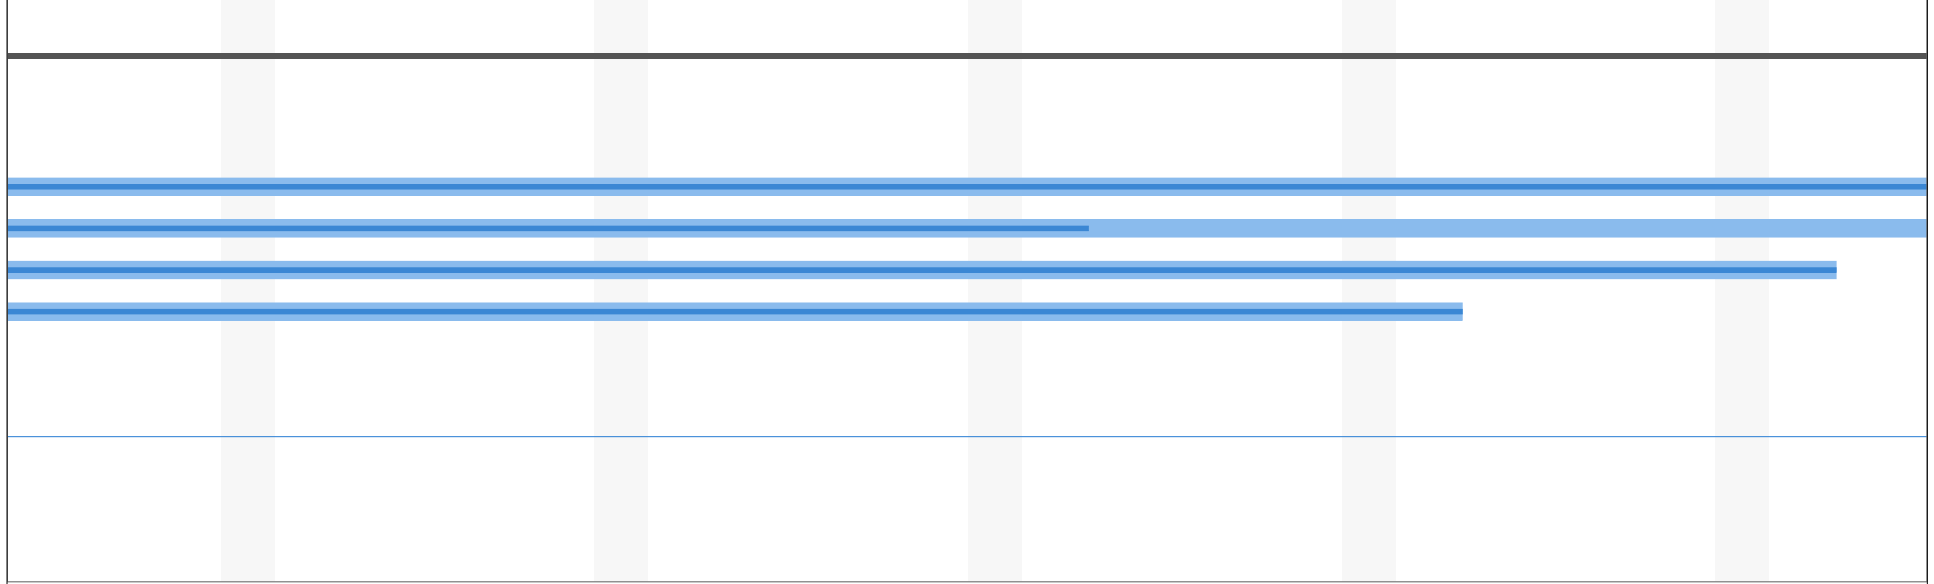












Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


June 2023 | July 2023 | August 2023
 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 01 03 05 07 09 11









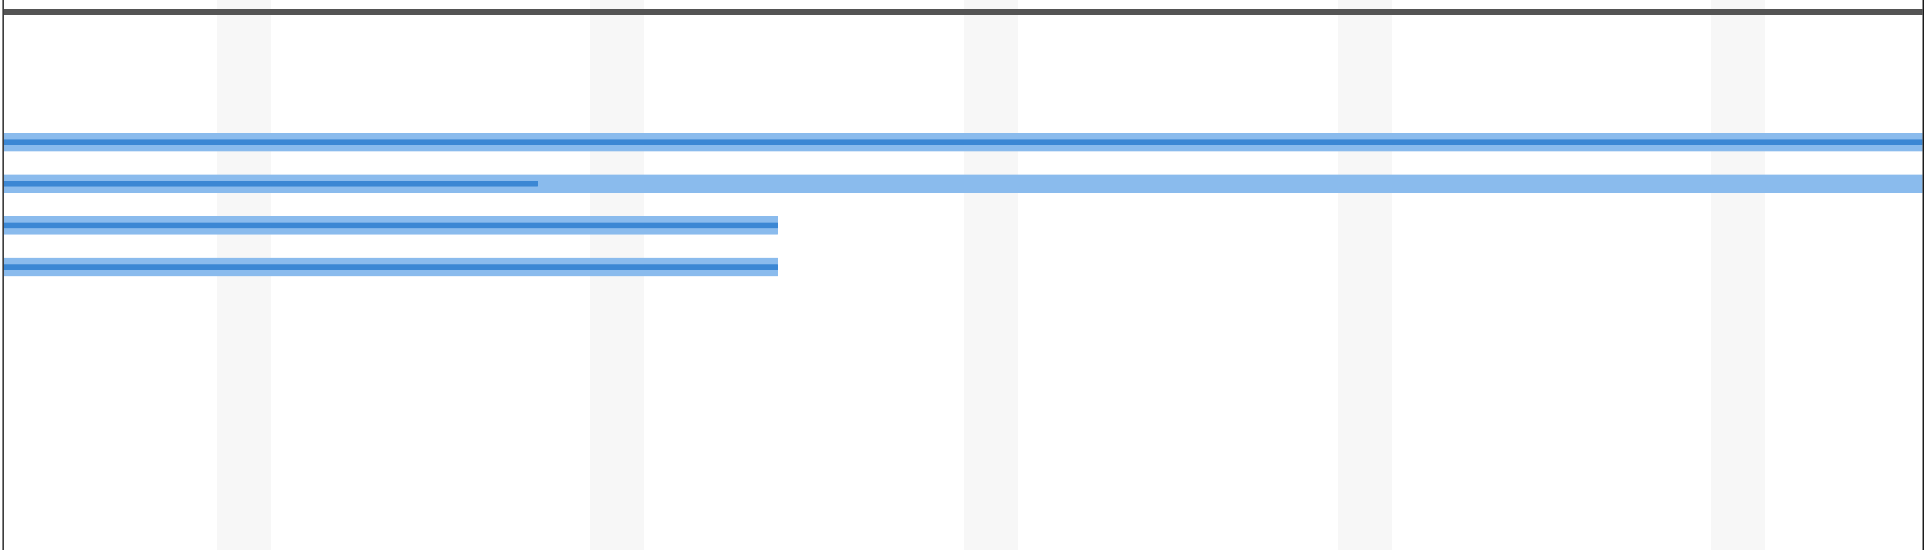












Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

June 2023 | July 2023 | August 2023
 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 01 03 05 07 09 11






















Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

June 2023 | July 2023 | August 2023
 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 02 04 06 08 10 12 14 16 18 20 22 24 26 28 30 01 03 05 07 09 11







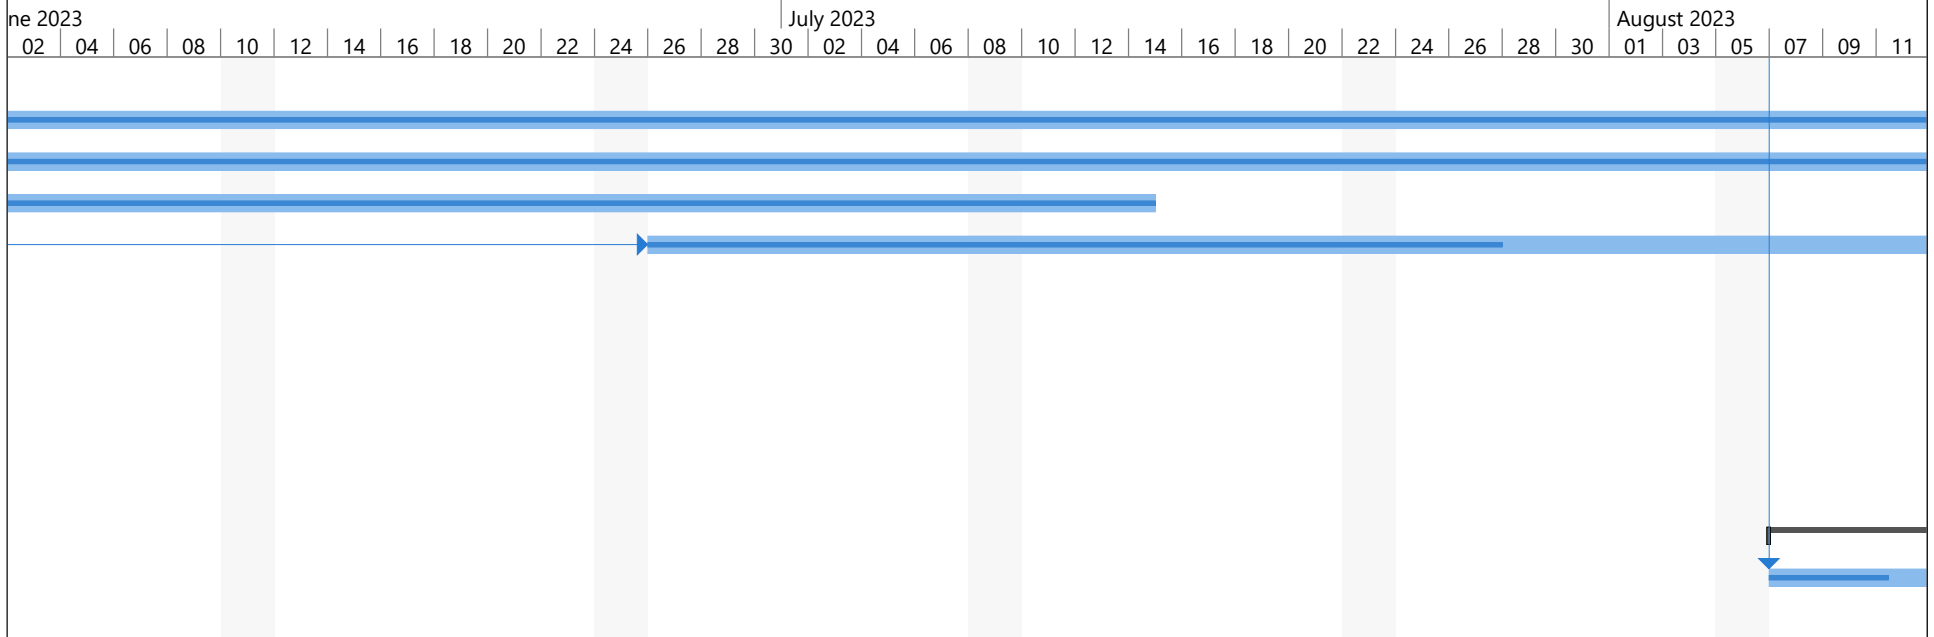














Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

June 2023 | July 2023 | August 2023
 02 | 04 | 06 | 08 | 10 | 12 | 14 | 16 | 18 | 20 | 22 | 24 | 26 | 28 | 30 | 02 | 04 | 06 | 08 | 10 | 12 | 14 | 16 | 18 | 20 | 22 | 24 | 26 | 28 | 30 | 01 | 03 | 05 | 07 | 09 | 11






















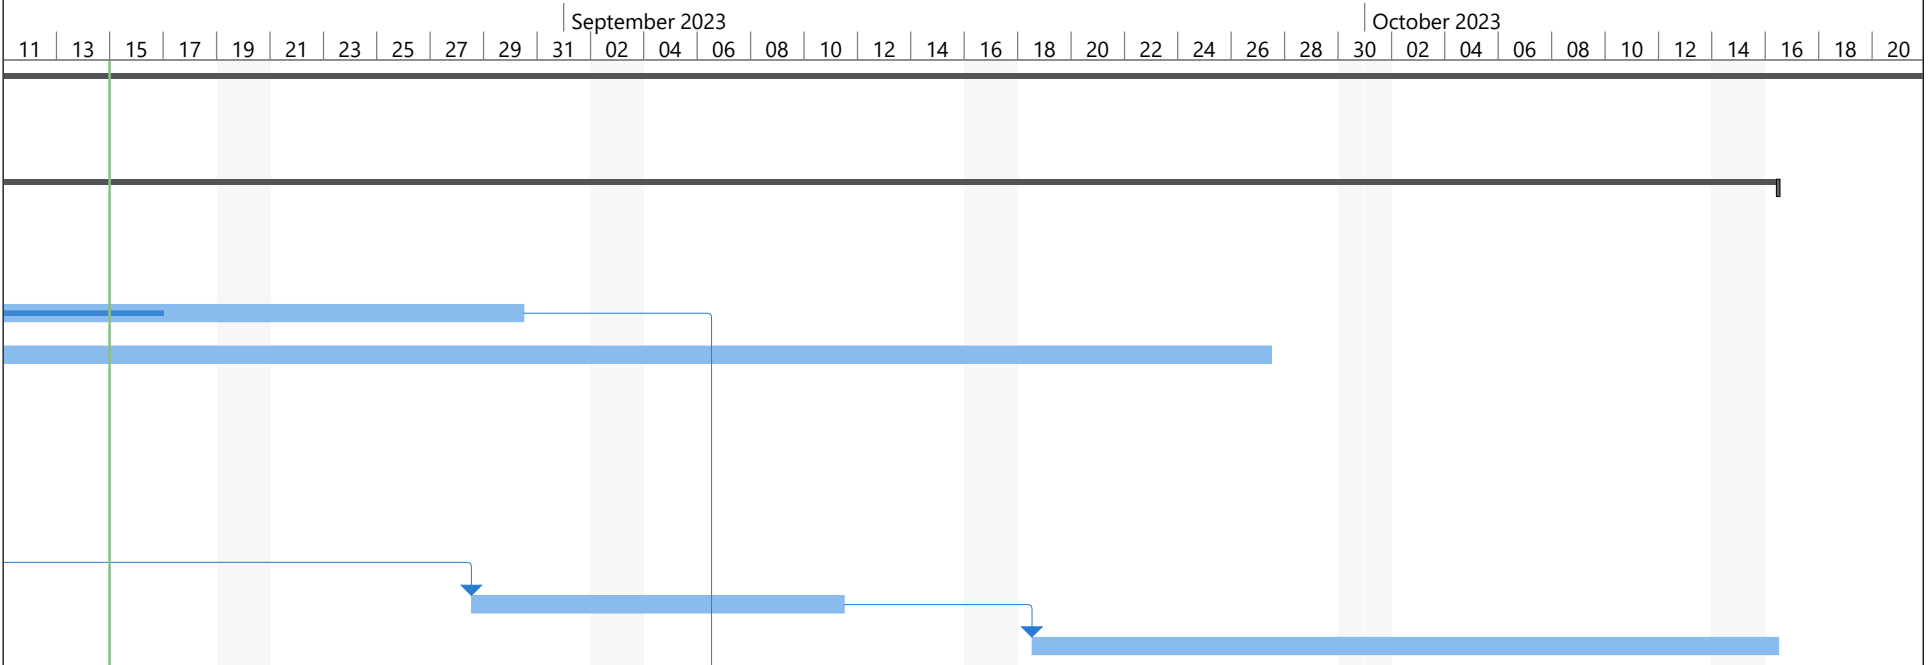
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















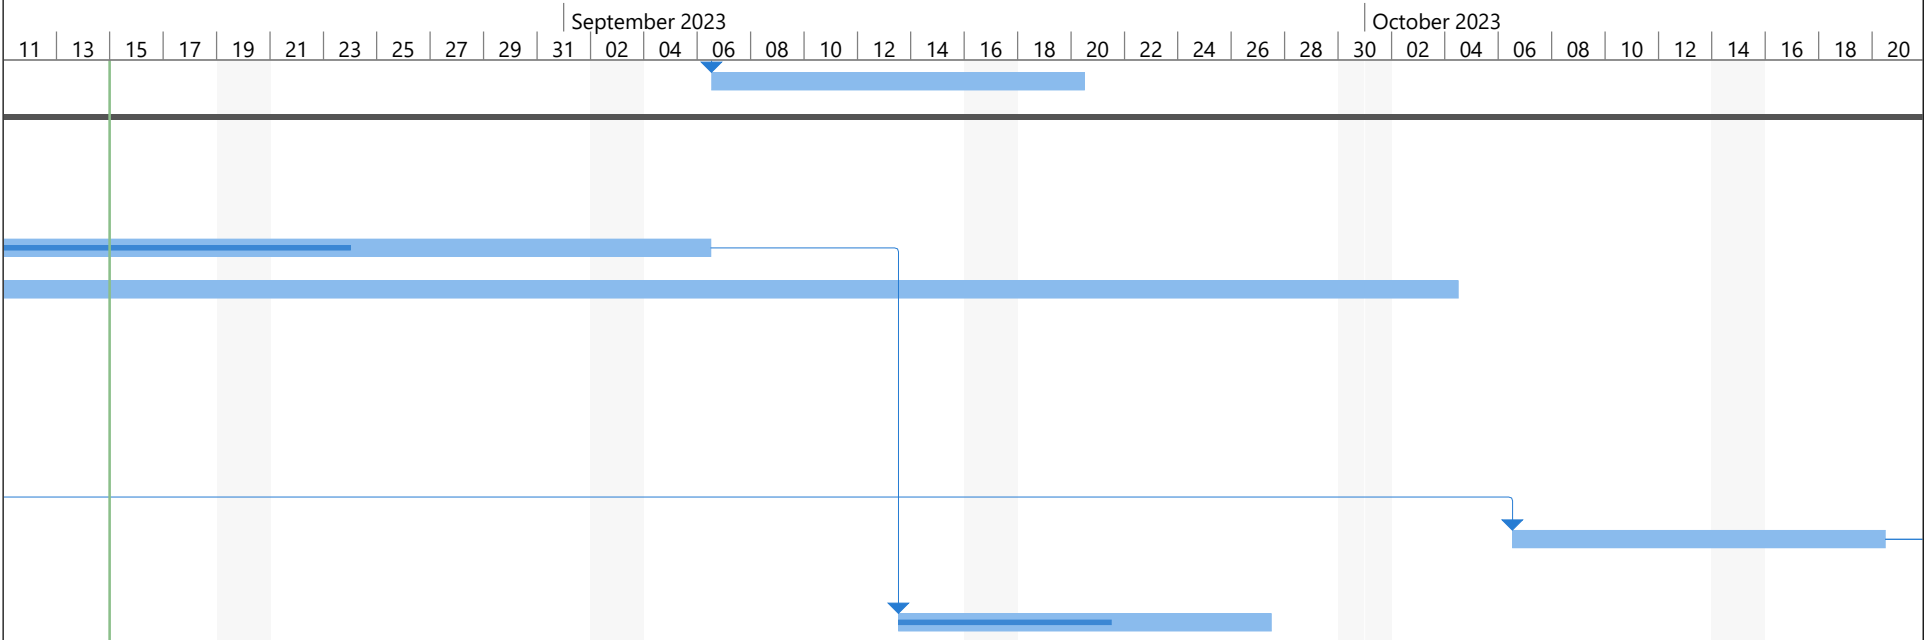
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















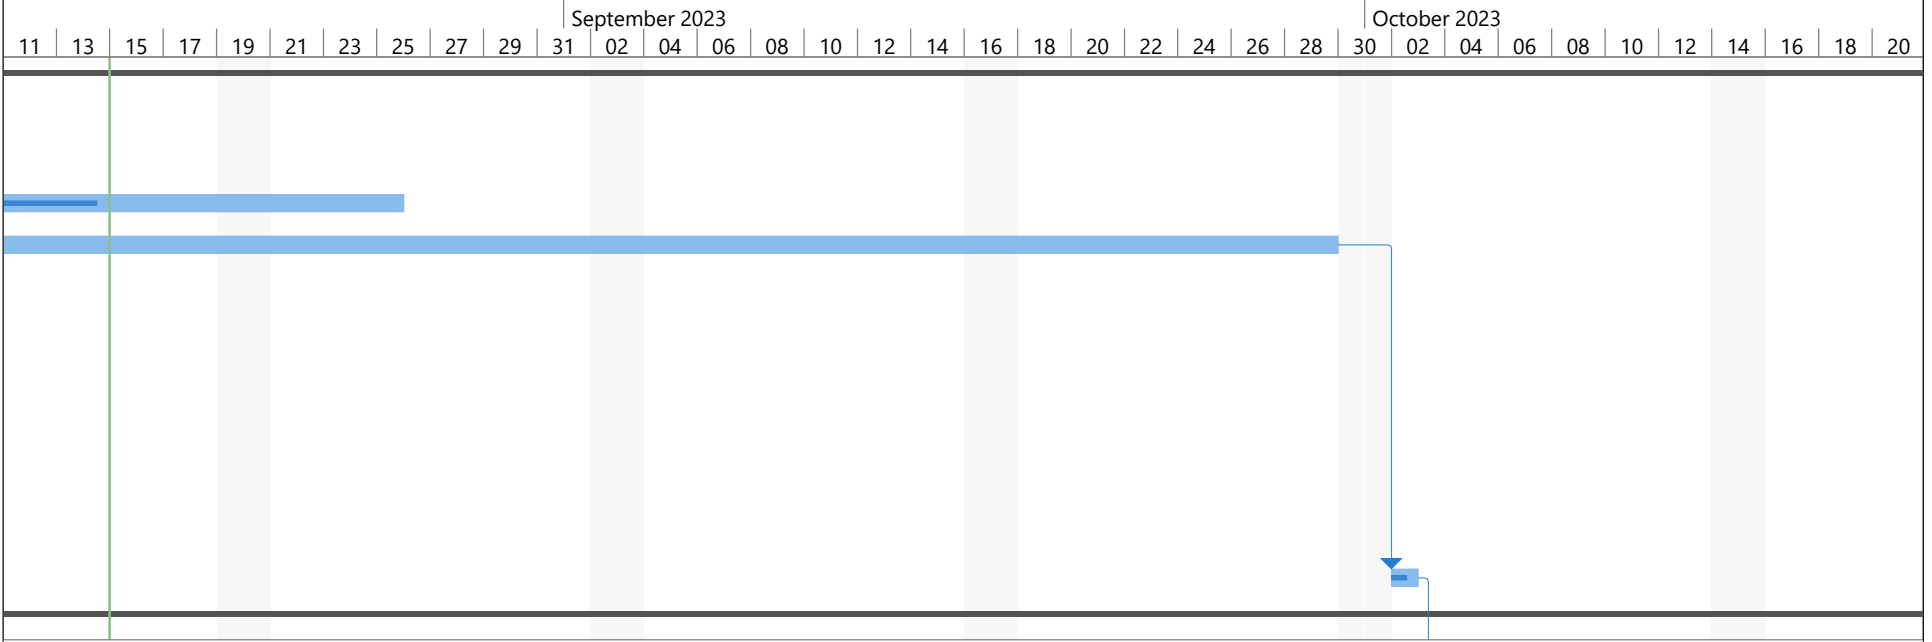
Project: Wharncliffe exit progra
Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















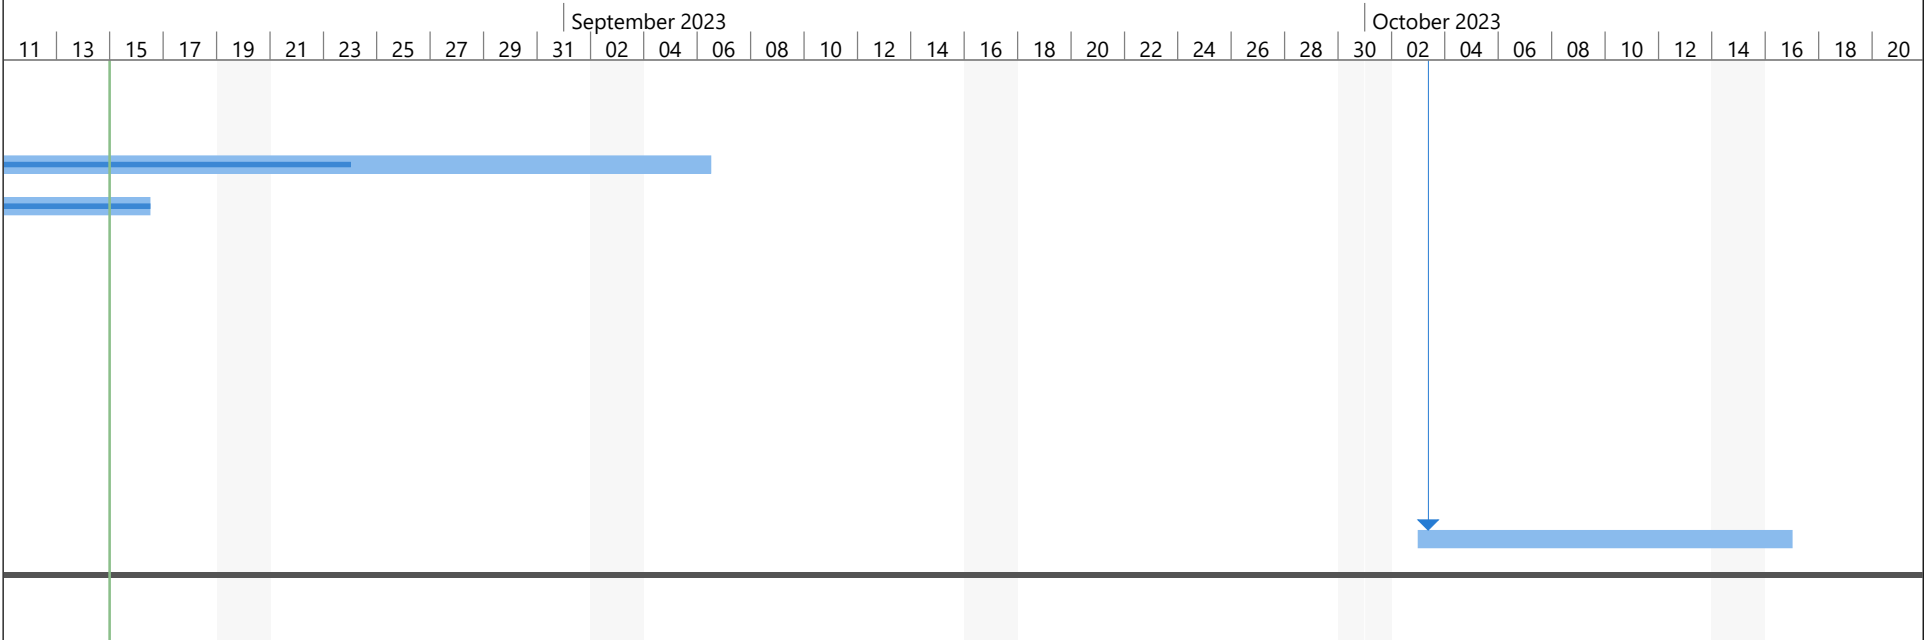
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















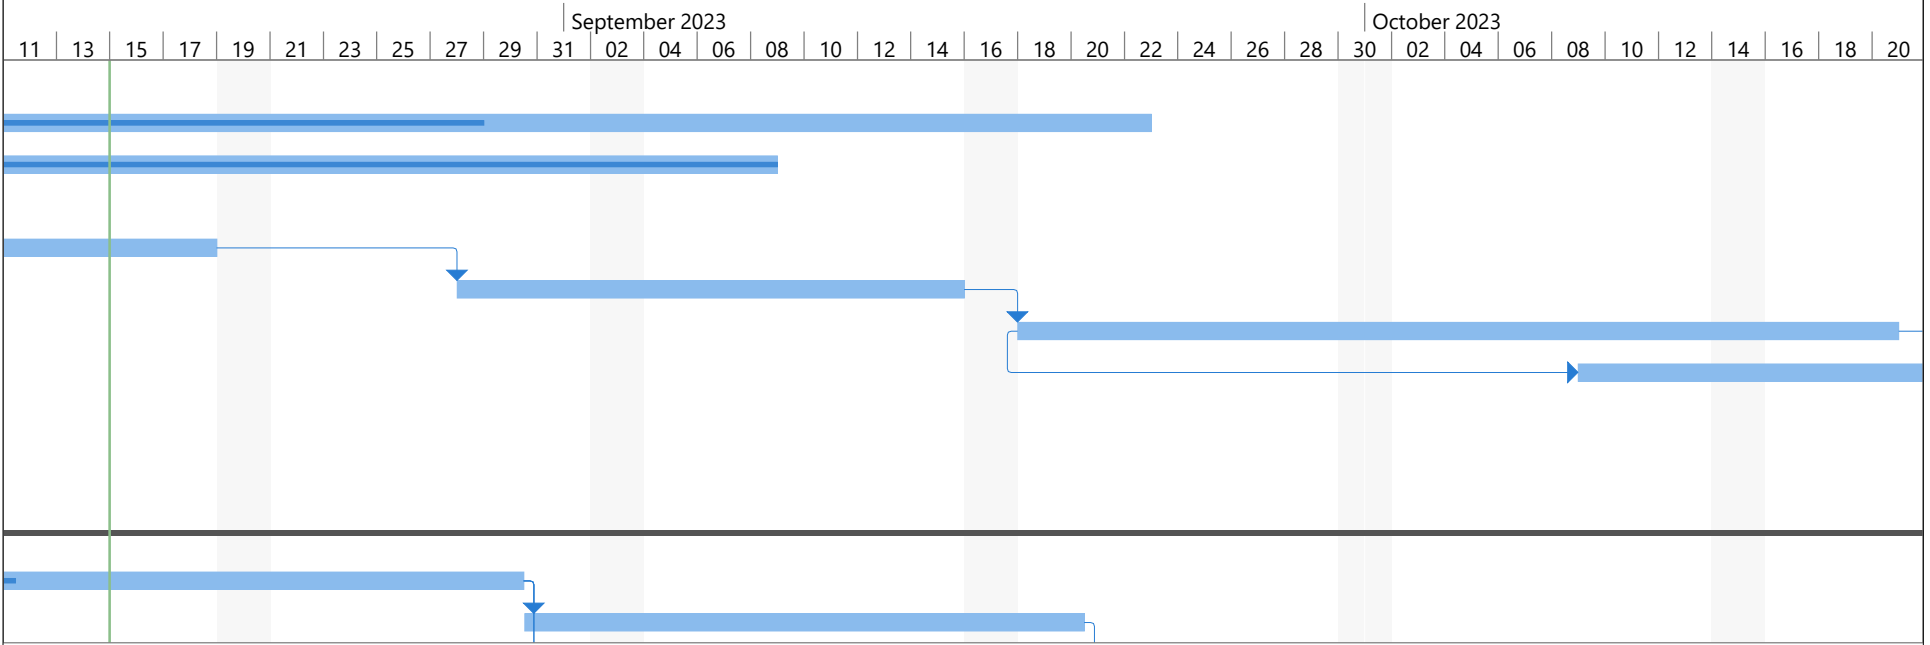
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















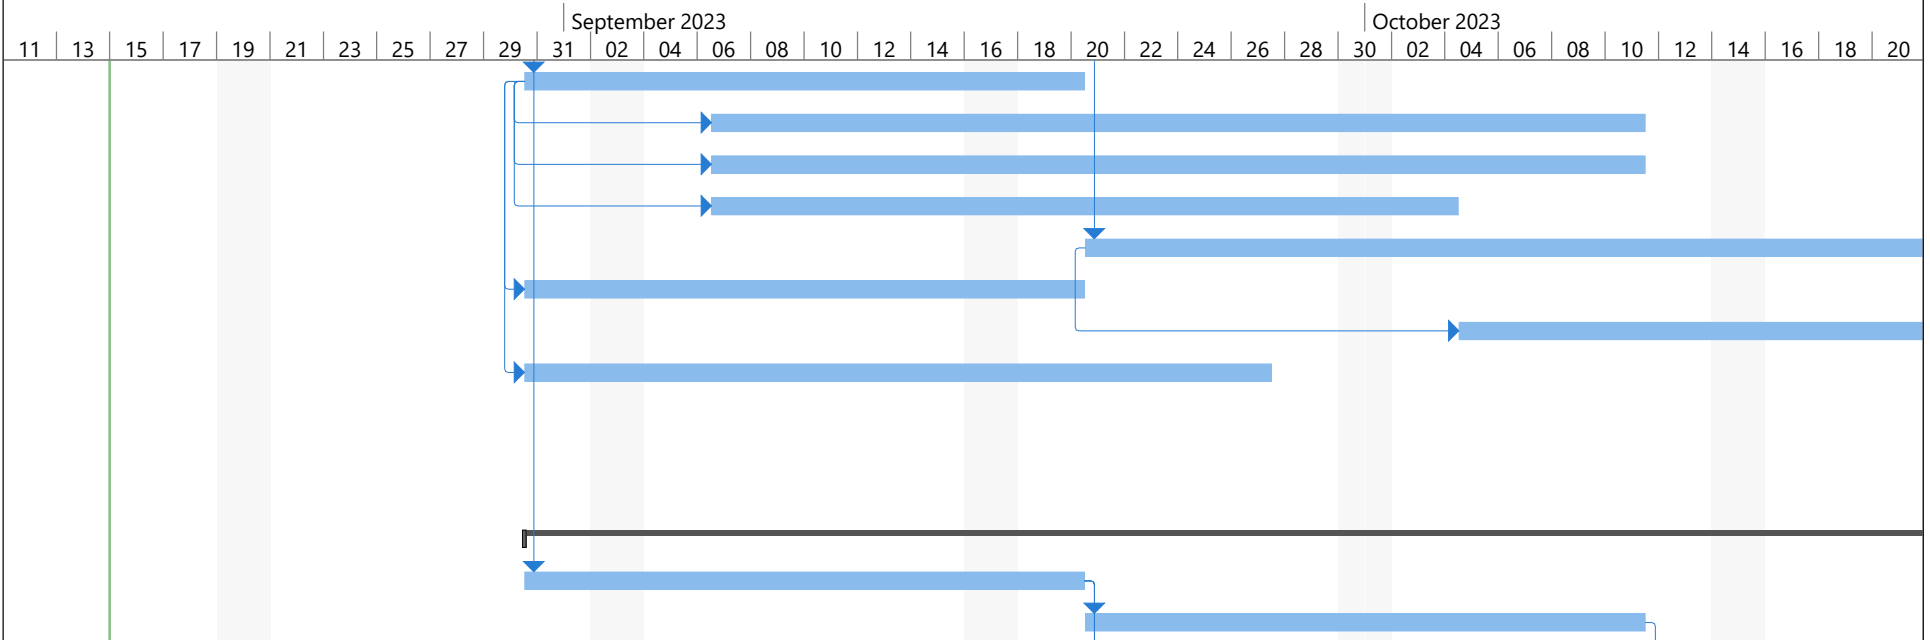
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















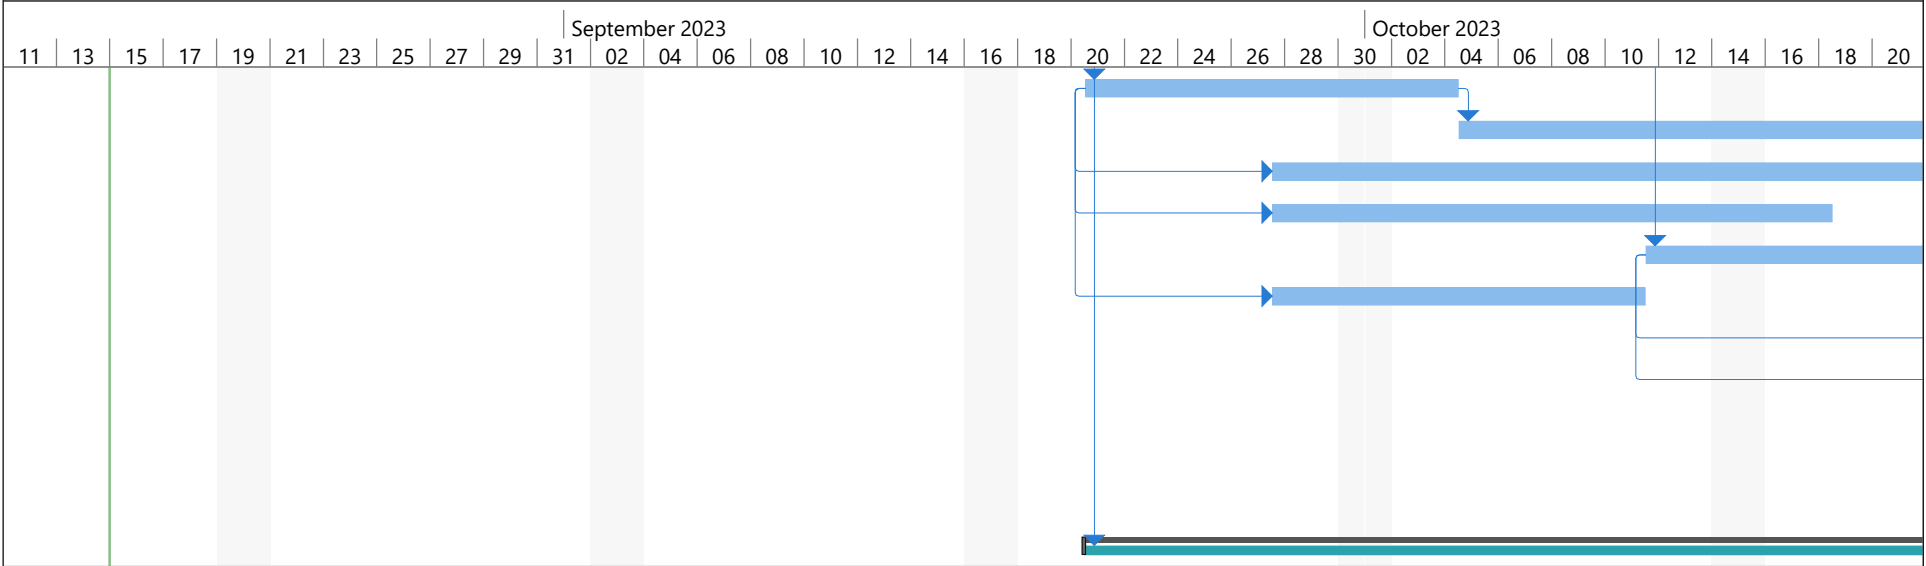
Project: Wharncliffe exit progra
Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

20 | 22 | 24 | 26 | 28 | 30 | November 2023 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | December 2023 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29







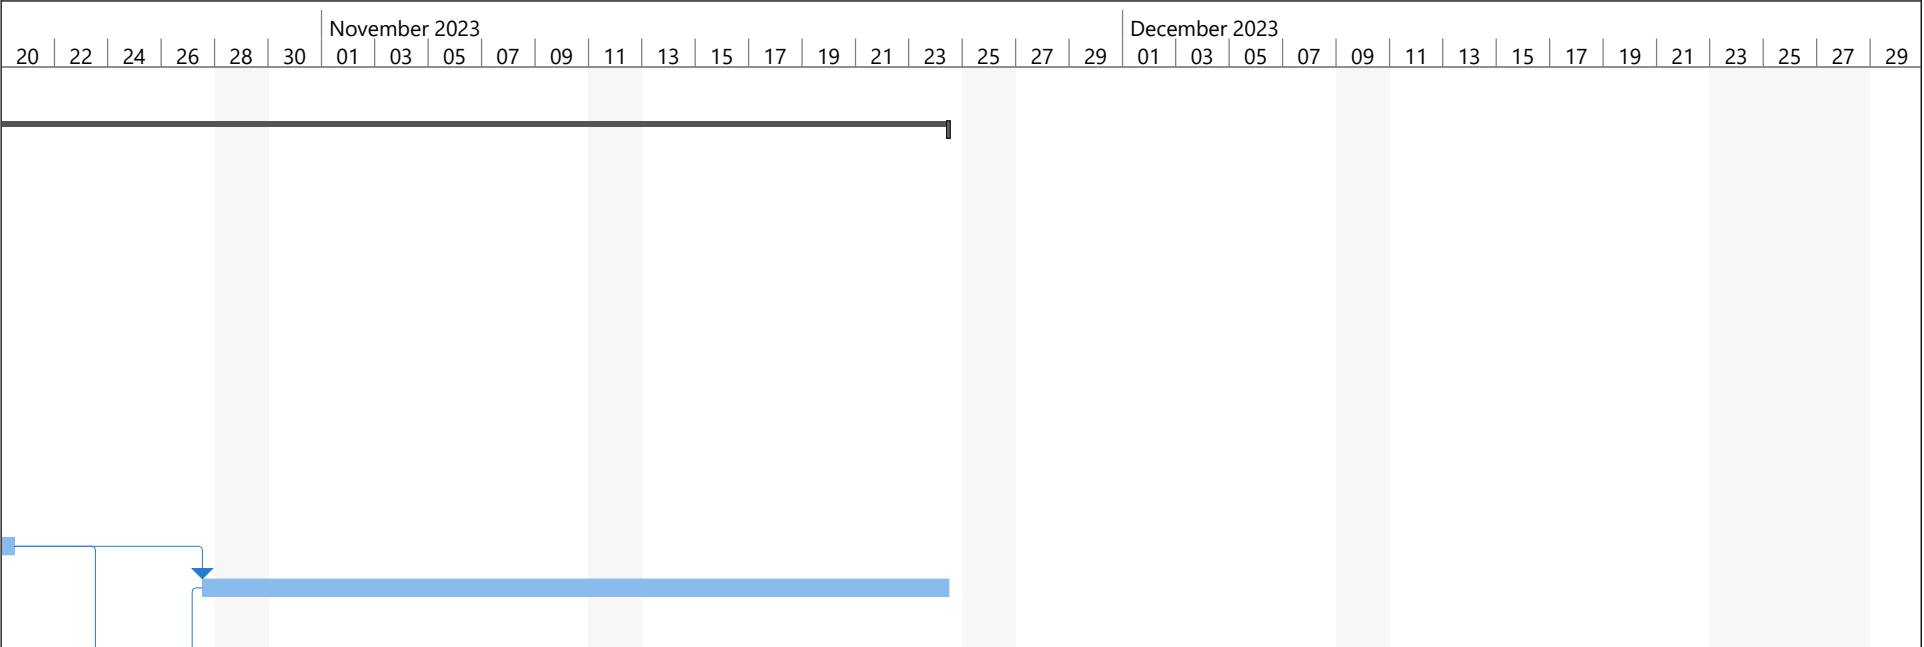














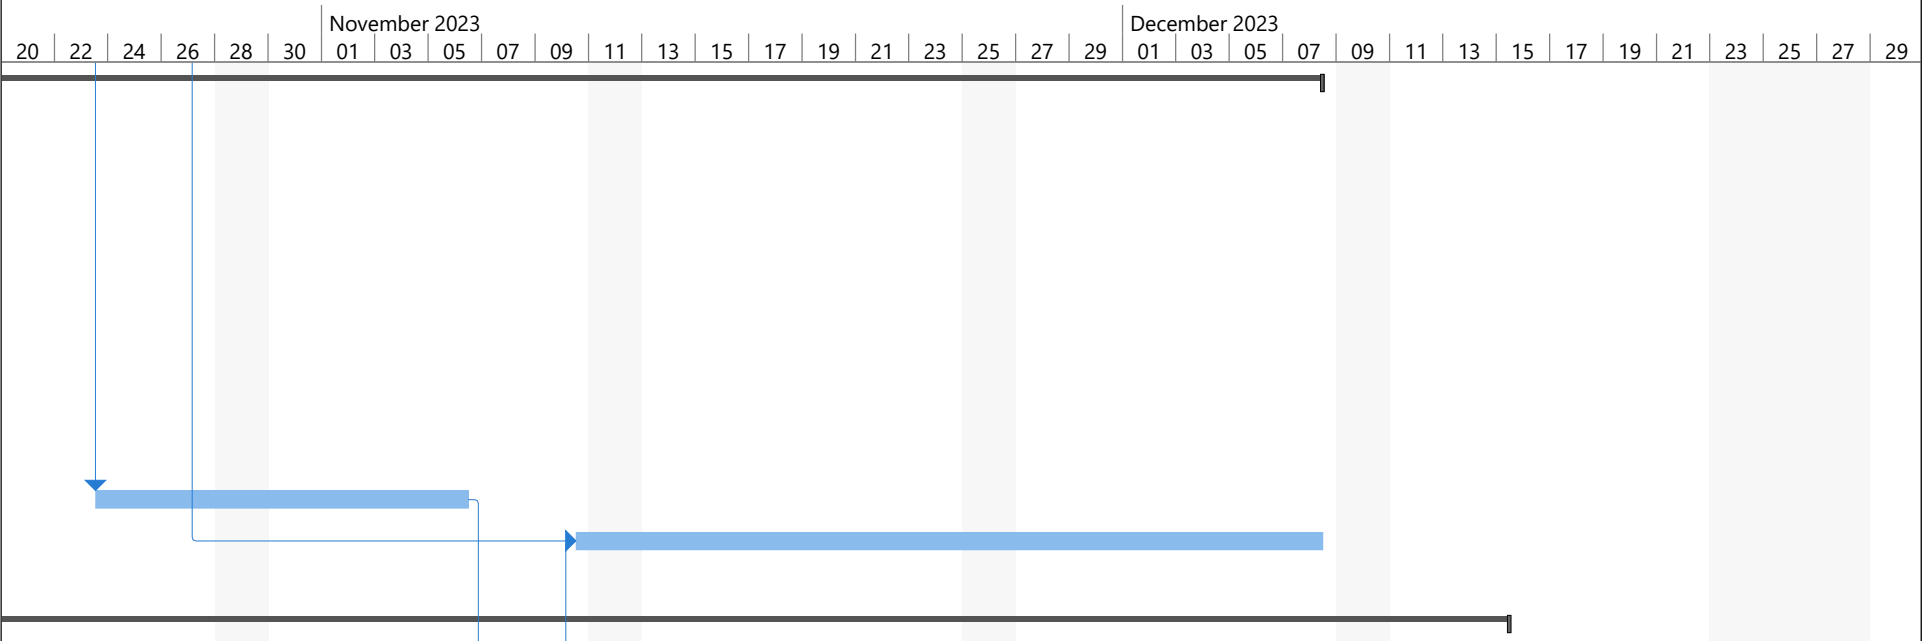
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















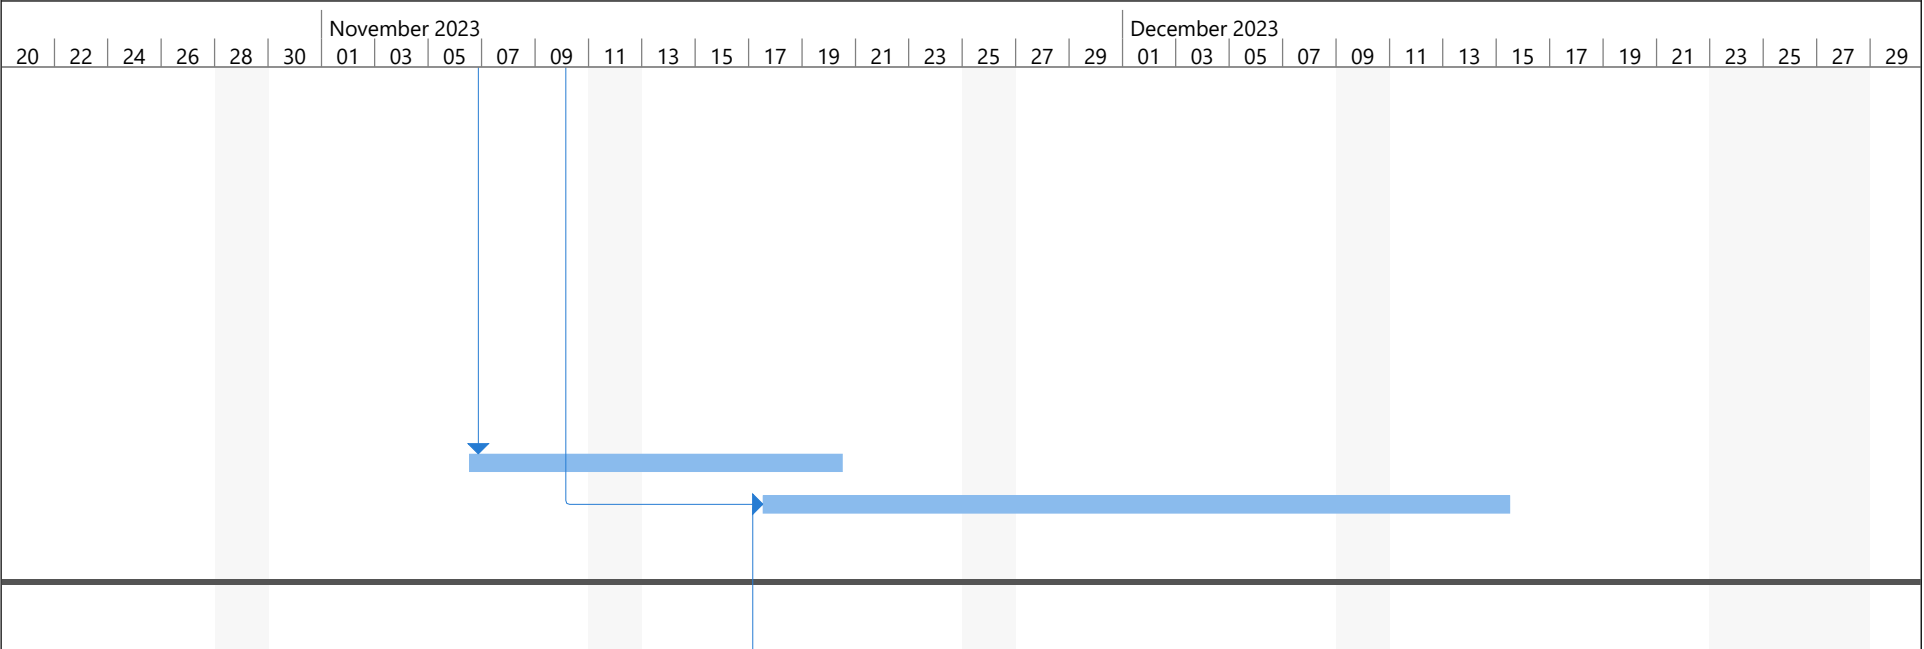
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















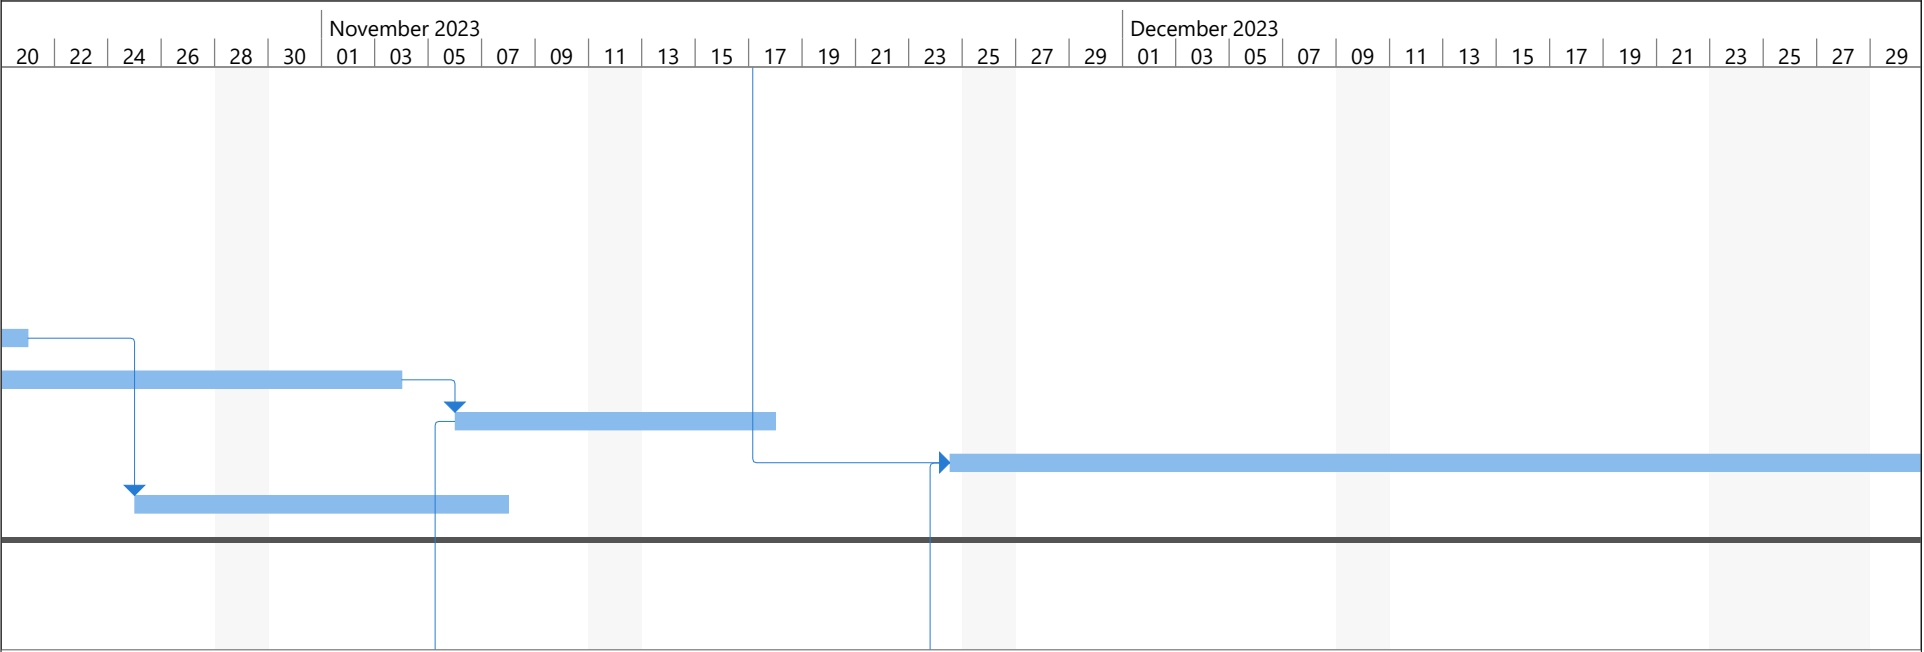
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















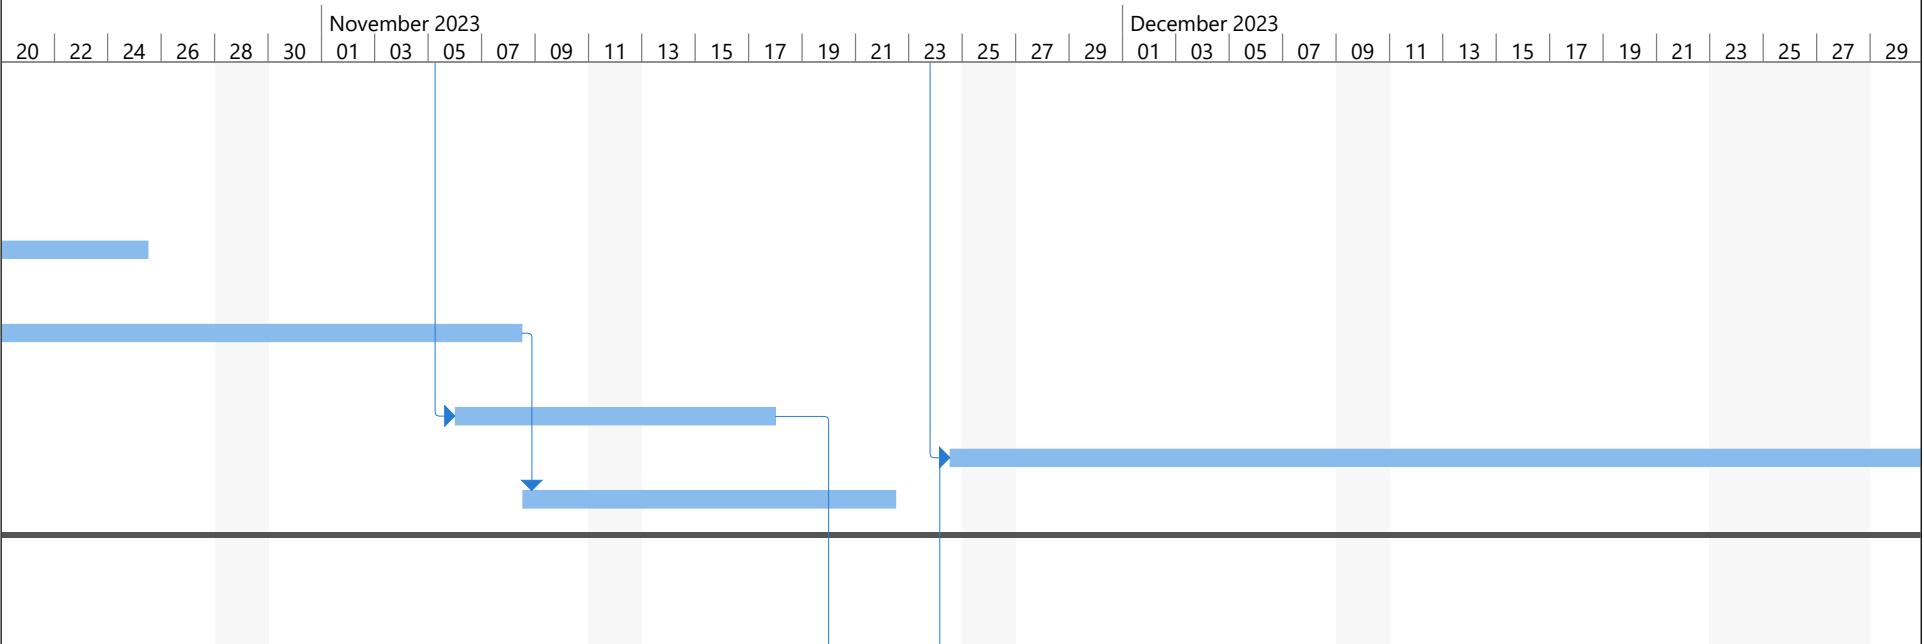
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















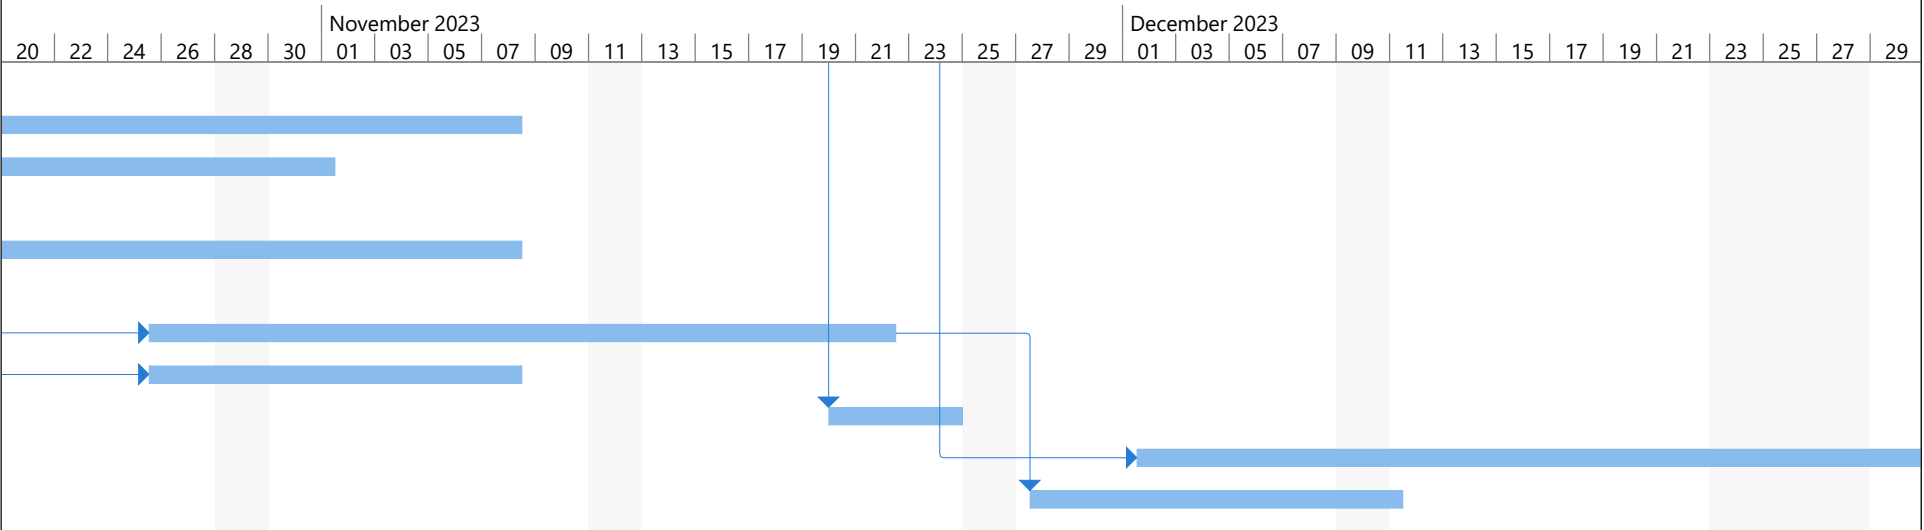
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			























Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















Project: Wharncliffe exit progra
 Date: Tue 15/08/23


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

January 2024 | February 2024 | March 2024
 29 | 31 | 02 | 04 | 06 | 08 | 10 | 12 | 14 | 16 | 18 | 20 | 22 | 24 | 26 | 28 | 30 | 01 | 03 | 05 | 07 | 09 | 11 | 13 | 15 | 17 | 19 | 21 | 23 | 25 | 27 | 29 | 02 | 04 | 06 | 08























Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















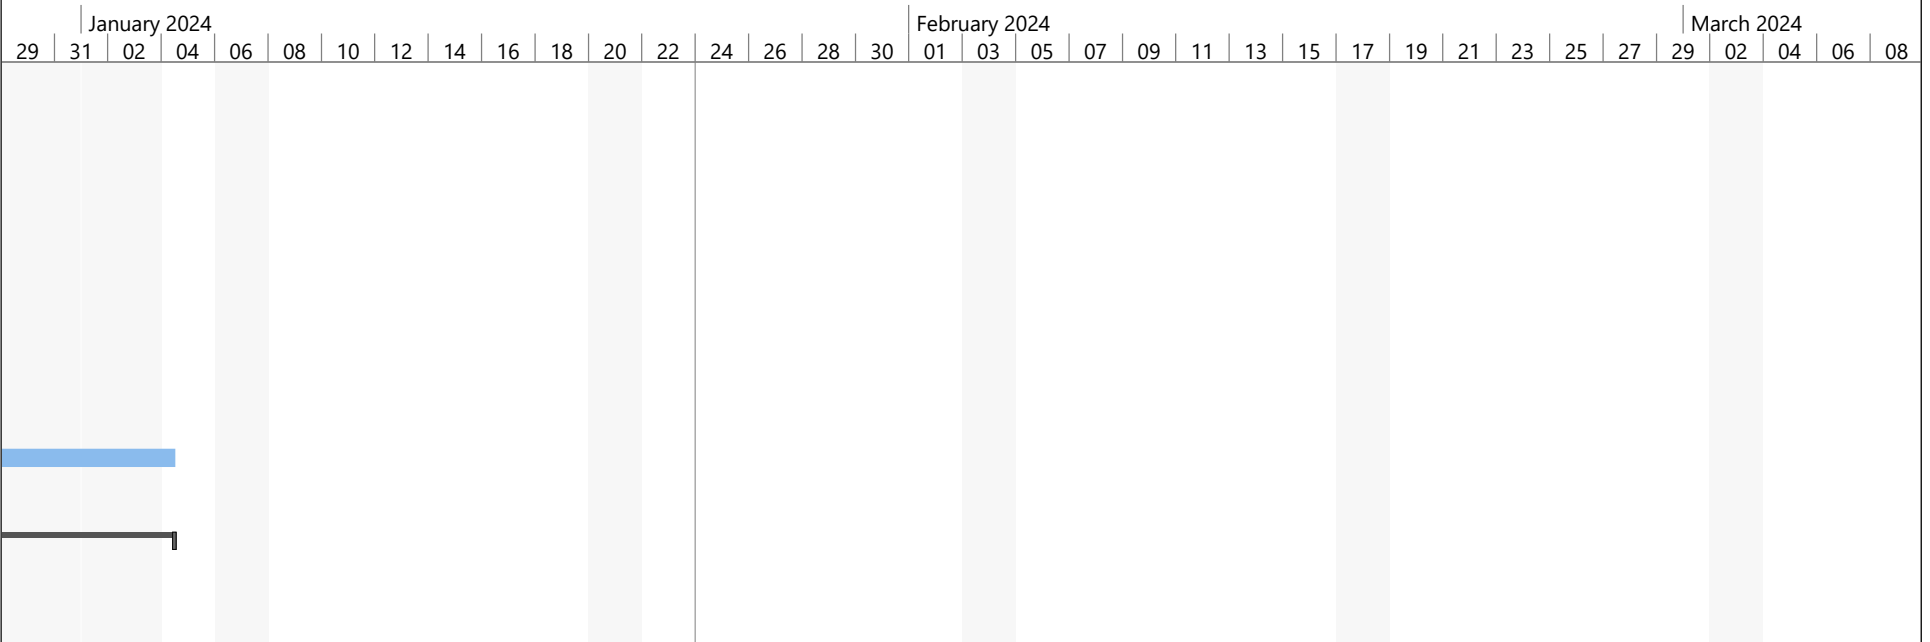
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















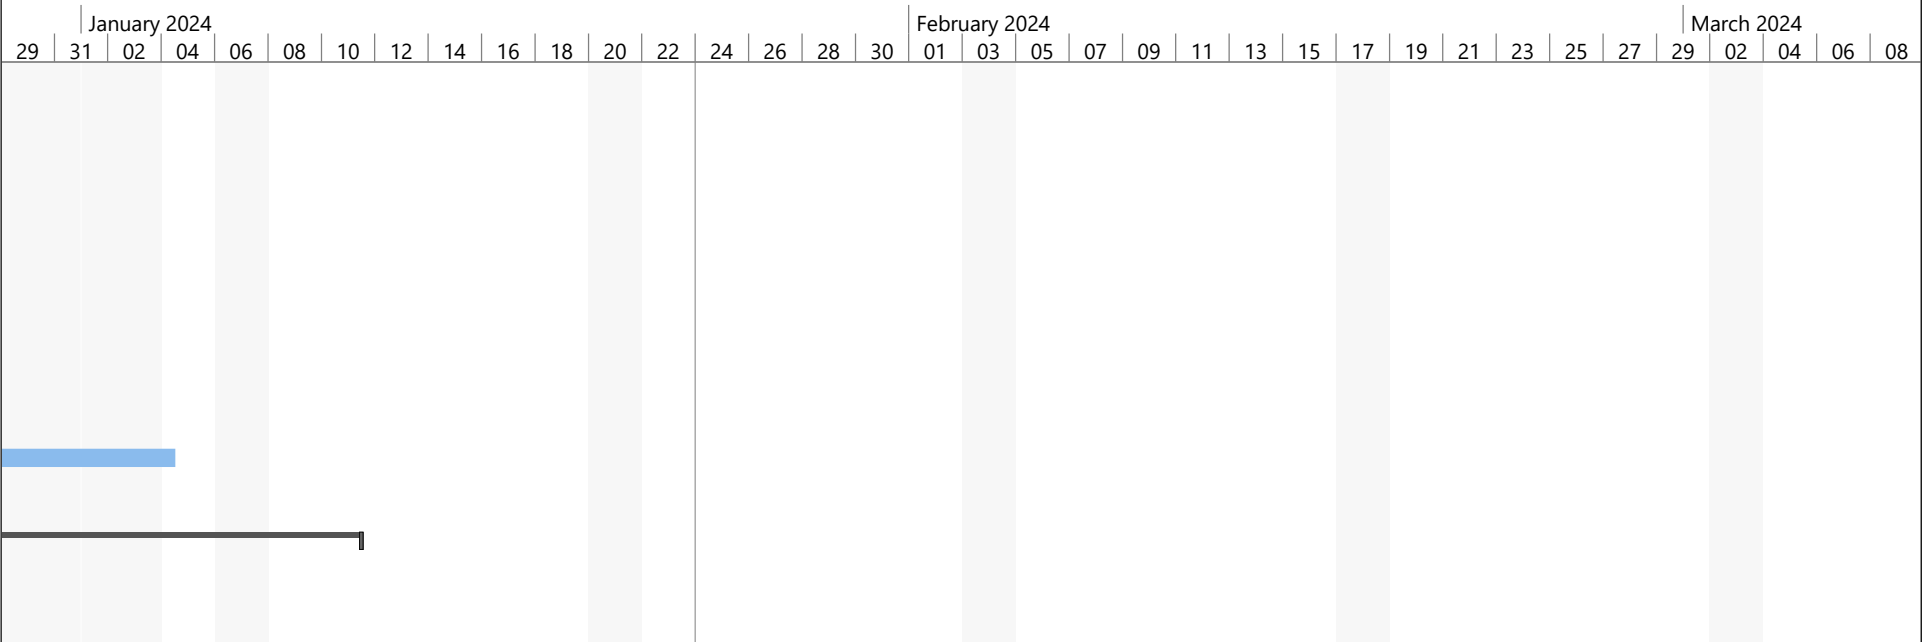
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			






















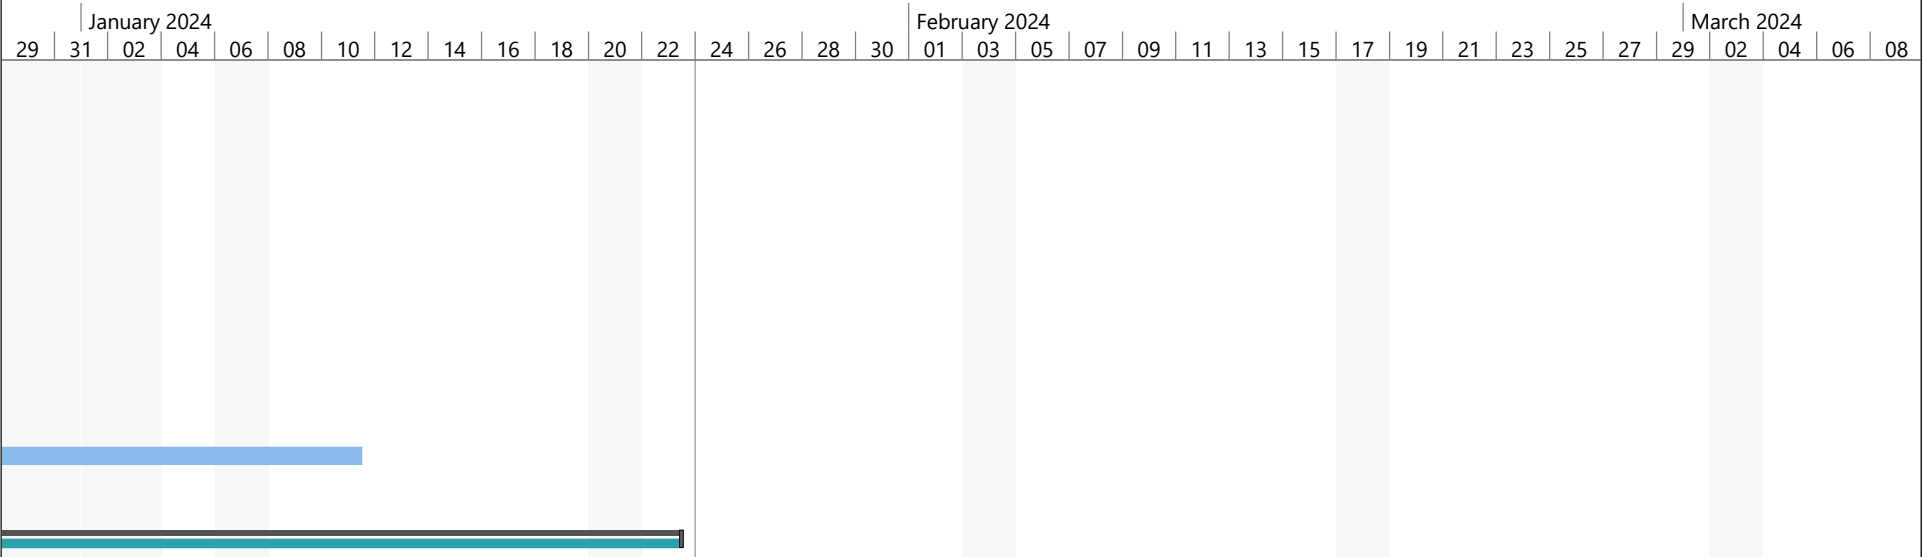
Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			





















Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Wharncliffe exit progra
 Date: Tue 15/08/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only	
